

APPENDICES

APPENDIX 1 – SITE COMPOUND PLAN




- CONTRACTORS COMPUND
 - Storage of materials
 - Plant and machinery
 - Welfare facilities
- SITE ACCESS AND PARKING
 - Site access for construction traffic
 - Site access for construction deliveries
 - Contractors parking
- EXISTING BUILDING OUTLINE
- PROPOSED BUILDING OUTLINE
- SITE RED LINE BOUNDARY

ABREVIATIONS	
A	Access
B	Building
C	Construction
D	Delivery
E	Existing
F	Footprint
G	Ground
H	Height
I	Infrastructure
J	Joint
K	Key
L	Level
M	Material
N	North
O	Outline
P	Parking
Q	Quantity
R	Ratio
S	Site
T	Time
U	Unit
V	Value
W	Width
X	Zone
Y	Year
Z	Zone

SCHEDULE 1	
1	OS grid & datum determined by GPS
2	Buildings & structures
3	Topography & ground levels
4	Contours & drainage
5	Other features to be included

APPENDIX 2 - CONSTRUCTION PROGRAMME

CARDONNEL COURT CARE FACILITY

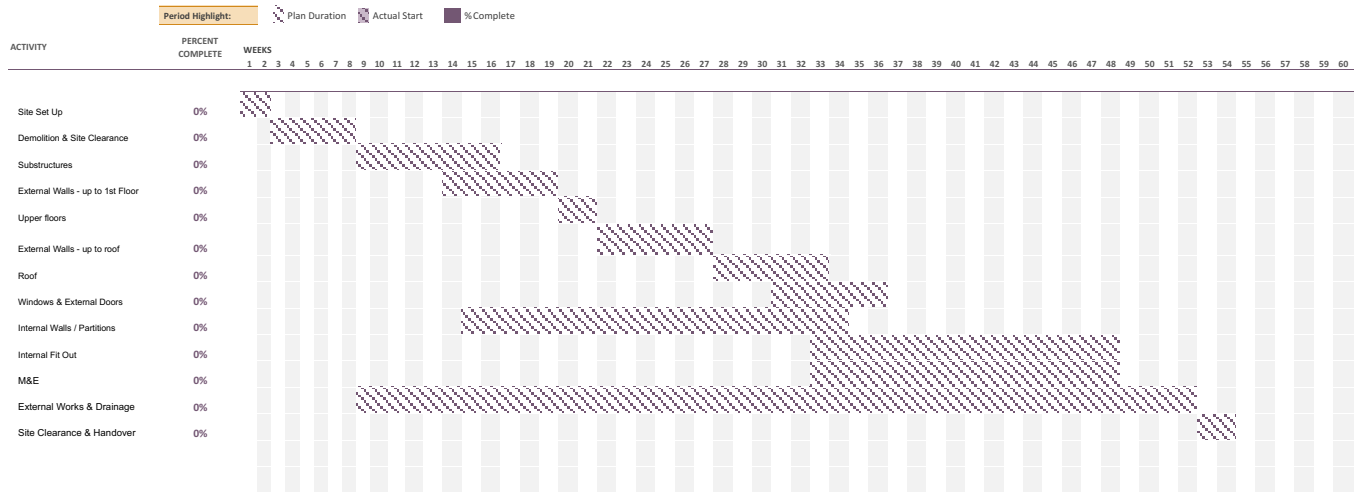

APPENDIX 3 – BAT SURVEY



**CARDONNEL COURT NURSING HOME, CARDONNEL ROAD,
NEATH**

BAT SURVEY

ISSUE 1, VERSION A

JUNE 2023

Bat Survey Report

Document control

Issue	Author	Checked	Approved	Date
1	BE	BE		19/04/23

Contents Amendment Record

This report has been issued and amended as follows:

Issue	Revision	Description	Approved by	Date
1	A	Update to include results of activity surveys	BE	22/06/23

DISCLAIMER

The report, content and all information contained herein may not be reproduced without the prior written permissions of BE ECOLOGICAL LTD. No part of this report or the information contained herein may be copied or reproduced without prior written consent from BE ECOLOGICAL LTD. This report has been prepared for the sole use of the commissioning party (s) contained herein and under no circumstance is any other party to make use of this report and information unless agreed in writing by BE ECOLOGICAL LTD. The report and information may not be used for any reason, including use for planning purposes, until such times as all outstanding fees relating to it have been paid to BE ECOLOGICAL LTD. No liability is accepted by BE ECOLOGICAL LTD for any use of the report or its contents, other than for those purposes stated.

Page left blank intentionally

CONTENTS

1	INTRODUCTION	7
1.1	Background	7
1.2	Site description	7
1.3	Proposed development	9
2	LEGISLATION & POLICIES.....	10
2.1	Conservation of Habitats & Species Regulations 2017 (as amended)	10
2.2	Wildlife & Countryside Act 1981.....	10
2.3	The Environment (Wales) Act 2016	10
3	METHODOLOGY.....	12
3.1	Survey Objectives.....	12
3.2	Survey Summary	12
3.3	Data Search.....	12
3.4	Surveyor Information	12
3.5	Internal & External Inspection	13
3.6	Activity Surveys (emergence/re-entry surveys).....	13
3.7	Survey limitations.....	14
4	RESULTS.....	15
4.1	Designated Sites.....	15
4.2	Inspection survey	15
1.1	Activity surveys	16
1.2	Survey Schedule and Weather Conditions	16
1.3	Activity Survey Results	17
4.3	Identified Roosts	18
4.4	Conclusion & Recommendations	18
4.5	Breeding Birds.....	18
5	INTERPRETATION & IMPACT ASSESSMENT	19
5.1	Active Season Usage	19
5.2	Hibernation Season Usage.....	19
5.3	Ecological Impacts of development	19
6	ENHANCEMENT	20
6.1	Bats.....	20
6.2	Birds.....	20
7	RECOMMENDATIONS	20

8	REFERENCES	21
9	METHOD STATEMENT.....	25

EXECUTIVE SUMMARY

It is proposed to demolish a former nursing home and replace it with a new 16 bed care facility.

An initial bat inspection survey of the site was undertaken on 17th March 2023. No bats or evidence of bats was seen on the exterior of the building, however, the building has a number of features suitable for roosting bats. As a result, the building was determined as being of at least moderate potential for roosting bats with a minimum of two activity surveys required.

Subsequent activity surveys revealed that the property is not a bat roost. Due to the difficult viewing angle of the building, it is considered necessary that the works are undertaken in line with a non-licensed method statement to safeguard the slight possibility of roosting bats. If at any point bats are observed, all works will cease, BE Ecological Ltd engaged and NRW consulted. Further surveys and/or a licence may be required prior to works re-commencing.

No evidence of breeding birds were found throughout the buildings at the time of survey. However, a single blue tit and a number of sparrows were seen throughout the survey.

1 INTRODUCTION

1.1 Background

BE ECOLOGICAL LTD was commissioned by the client to undertake an initial bat inspection survey and subsequent activity surveys of a former care home for the potential presence of birds and bats in order to support a planning application to demolish the property and replace it with a 16 bed care home.

The surveys were undertaken in line with the current guidance on standards for bat surveys (Bat Conservation Trust, 2016).

1.2 Site description

The building is a brick and block built, pebble dash rendered structure beneath a clay tile roof. The building is located immediately to the west of Cardonnel Road, Skewen, Neath (figure 1). The building is large and complex with multiple rooves, valleys and pitches. Generally the ridges run from south west to north east and north west to south east. The building is the subject of antisocial behaviour and vandalism.

The site is located on the edge of an urban area but is surrounded by trees and broad-leaved woodland and a railway line to the east. The site is adjacent to the (NPTSINC099 Pentrefynnon).



Figure 1- detailed view of site (arrowed red) (Google Maps, 2023)

1.3 Proposed development

It is proposed to demolish the existing building and replace it with a 16 bed care home.



2 LEGISLATION & POLICIES

BATS

2.1 Conservation of Habitats & Species Regulations 2017 (as amended)

The Conservation of Habitats and Species Regulations (2017) provides safeguards for European Protected Species (those listed under Annex IV Habitats Directive). With regards to bats, this makes it an offence to:

- Deliberately (or recklessly in Scotland) capture, injure or kill a bat
- Deliberately (or recklessly in Scotland) disturb a bat in a way that would (significantly in Scotland) affect its ability to survive, breed or rear young (or hibernate or migrate in England, Wales and Northern Ireland) or (significantly in England, Wales and Scotland) affect the local distribution or abundance of the species.
- Damage or destroy a roost (this is an 'absolute' offence)
- Possess, control, transport, sell, exchange or offer for sale/exchange any live or dead bat or any part of a bat

2.2 Wildlife & Countryside Act 1981

The Wildlife & Countryside Act 1981 (as amended) is the legislation for England and Wales for nature conservation, making it an offence to:

- Intentionally or recklessly disturb a bat at a roost
- Intentionally or recklessly obstruct access to a roost

2.3 The Environment (Wales) Act 2016

The Environment (Wales) Act 2016 requires that all public authorities, when carrying out their functions in Wales, seek to "maintain and enhance biodiversity" where it is within the proper exercise of their functions. In doing so, public authorities must also seek to "promote the resilience of ecosystems". This ensures that biodiversity is an integral part of the decisions that public authorities take in relation to Wales. It also links biodiversity with the long term health and functioning of our ecosystems, therefore helping to align the biodiversity duty with the framework for sustainable natural resource management provided in the Act. In Wales, this legislation replaces and enhances the Natural Environment and Rural Communities Act (2006) which sought to raise the profile of biodiversity and to make sure that it is considered in all local authority decisions by ensuring that "Every public authority must, in exercising its functions, have regard, so far as is consistent with the proper exercise of those functions, to the purpose of conserving biodiversity.". Other elements of NERC 2006 may still apply.

BIRDS

In Britain, all naturally occurring species (including hawfinches) are protected under Section 1 of the Wildlife and Countryside Act 1981 (as amended). The legislation protects all birds, their nests and eggs, and it is an offence to:

- intentionally kill, injure or take a wild bird;
- intentionally take, damage or destroy the nest of any wild bird whilst it is in use or being built; and
- intentionally take or destroy the egg of any wild bird.

In addition, birds listed on Schedule 1 of the above legislation, such as the red kite (*Milvus milvus*), are afforded further protection, and it is an offence to:

- Intentionally or recklessly disturb the bird whilst nest building or while at (or near) a nest with eggs or young; and
- Disturb the dependant young of such a bird.

Some birds however are exempt from this protection for certain purposes.

3 METHODOLOGY

3.1 Survey Objectives

- To carry out an initial bat inspection survey the building
- To present the above details and if necessary further surveys, recommendations for mitigation, future research and compensation within this report.
- To carry out a scoping survey for breeding birds

3.2 Survey Summary

The bat survey comprised of a five parts:

- Initial bat inspection survey of building (including birds)
- Data search
- Activity survey 1
- Activity survey 2
- Activity survey 3

3.3 Data Search

The South East Wales Biodiversity Records Centre (SEWBReC) were formerly requested to supply a Bat and Roof-nesting Birds (BARB) survey for the site. The survey to provide; bat records within a 2km buffer, roof nesting birds within 150m buffer plus a list of all Special Areas of Conservation (SAC) and sites of Special of Special Scientific Interest (SSSI) designated for bat species within a 10km site buffer in June 2022.

3.4 Surveyor Information

The inspection survey was undertaken by Beth Evans. Beth is the owner of BE ECOLOGICAL LTD and has a postgraduate degree in Environmental Biology: Conservation & Resource Management, specialising in British bats. Beth has 11 years' experience of ecological surveys, both in a small scale and large multi-disciplinary context. Beth also holds Natural Resources Wales and Natural England bat licences to disturb and handle bats. Beth was accompanied on the survey by Gavin Vella.

Beth Evans was assisted during the activity surveys by Michael Rogers, Stephen Shutt, Gavin Vella, Dion Rowles and Sylvia Sanyalou. Stephen is an experienced licensed bat ecologist. Michael Hogan held a bat licence in Wales for many years. Gavin vella is an experienced ornithological surveyor and bat surveyor, with Mike, Dion and Sylvia having undertaken numerous bat surveys with BE Ecological Ltd over the last two seasons.

3.5 Internal & External Inspection


An initial inspection survey was carried out on 17th March 2023 by Beth Evans to search the building, both internally and externally to identify potential bat roosting areas and signs of bat use including; live bats, dead bats, droppings, urine staining, grease marks and discarded prey items. The buildings and all areas/items of interest were recorded and photographed. Extension ladders/steps were used to safely access areas where no safe access was available the survey was conducted using, close focus binoculars and/or a high powered lamp.

3.6 Activity Surveys (emergence/re-entry surveys)

Building 'emergence' and 're-entry' surveys were carried out on the following dates, times and weather conditions. Climatic conditions including rain, wind, temperature and cloud cover were recorded for each survey using a hand held Kestrel 4500 weather station.

3.6.1 Survey 1- 3rd May 2023

A dusk survey was carried out on 3rd May 2023 using surveyors, positioned in such a way that as much of the building was visible to surveyors as possible. Surveyors and cameras were equipped with Batlogger M detectors.

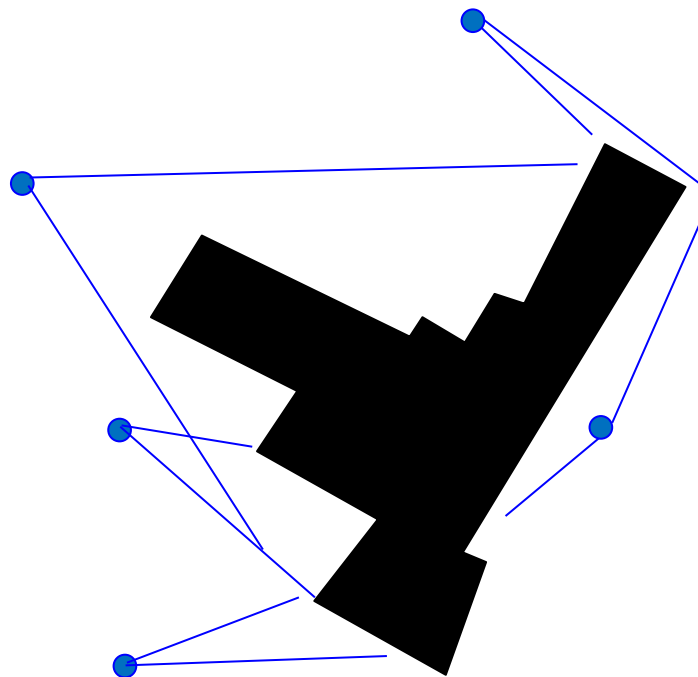

Approximate surveyor location

3.6.2 Survey 2- 18th May 2023

A dusk survey was carried out on 18th May 2023 as above.

3.5.1 Survey 3- 21st June 2023

A dusk survey was carried out on 21st June 2023 as above.

3.7 Survey limitations

Any survey for bat species can only be a series of snapshots in time. Bats are highly mobile, long lived creatures (capable of living up to 30 years, sometimes longer) with complex social structures and utilising multiple roost sites within a year. The implications of this are that surveys and surveyors have to make informed assumptions based on observations, recorded data, local information and a detailed knowledge of the species.

Access around some areas of the building is dangerous and not accessible to surveyors for health and safety reasons. In addition to this, there are numerous trees surrounding the building that obscure view. Surveys were undertaken as best as practically possible.

4 RESULTS

4.1 Designated Sites

The site is adjacent to the Pentrefynnon SINC (NPTSINC099 Pentrefynnon) (noted from pre-application comments). Please note the data search did not identify this site as a SINC.

The closest records of roosting bats refer to roosts of common pipistrelle and brown long-eared bats approximately 180m from the site.

Other records further afield refer to noctule, myotis sp., and soprano pipistrelle.

4.2 Inspection survey

4.2.1 External survey results

The survey carried out by BE Ecological Ltd revealed no droppings or evidence of bats on the exterior of the building. However, a number of potential access points for bats were noted. These include but are not limited to:

- Gaps beneath ridge tiles
- Gaps beneath slipped/missing tiles
- Gaps via smashed windows and doors
- Gaps beneath fascias/soffits
- Gaps beneath lead flashing

As a result of the above, the building is of at least moderate potential and therefore will require at least two activity surveys to be undertaken in the appropriate season (May to September) prior to any planning determination.

4.2.2 Internal survey results

The building is the subject of vandalism and anti-social behaviour. As a result it was deemed unsafe for surveyors to enter the building due to human presence at the time of survey. This is unlikely to be a constraint as further emergence surveys have been recommended and commissioned. Any bats in the building will be observed during these surveys.

1.1 Activity surveys

The surveys were undertaken as per the table below:

1.2 Survey Schedule and Weather Conditions

Table 1: Schedule and weather conditions

Visit	Date (sunrise) (sunset)	Start End	Time	Temp C	Wind	Cloud Cover	Notes
Survey 1 03/05/23	20:42	Start End	20:30 22:15	14 13	Low Low	30% 15%	Dry evening, insects flying
Survey 2 18/05/23	21:05	Start End	20:50 22:35	18 18	Low Low/moderate	100% 100%	Dry evening insects flying
Survey 3 21/06/23	21:37	Start End	21:25 23: 10	10 18	Low Moderate	60% 40%	Dry evening insects flying

1.3 Activity Survey Results

1.3.1 Survey 1- 3rd May 2023

Activity was moderate throughout the course of the survey.

The first bat heard was a common pipistrelle, the bat was seen foraging along the vegetation to the north of the site approximately 15 minutes post sunrise. Following this, common pipistrelle bats were also seen foraging along the street to the south of the development site.

Throughout the course of the survey, a small number of common and soprano pipistrelles were seen foraging along the vegetated boundaries of the site. Approximately 40 minutes post sunrise a lesser horseshoe bat was recorded by the surveyor to the west of the building, foraging along the railway line to the rear.

No bats emerged from or interacted with the building on this date.

4.2.1 Survey 2- 18th May 2023

The results of this survey were similar to that of the previous survey with common and soprano pipistrelle activity present at the site for the majority of the night with bats favouring the tree lines surrounding the building.

A small number of noctule calls were heard throughout the course of the survey but the bats were not seen.

A small number of myotis sp. calls (natterers) were heard along the railway line to the west later into the evening. A number of common pipistrelles were observed flying high over the building at sunset.

No other bats emerged from or interacted with the building on this date.

4.2.2 Survey 3- 21st June 2023

Bat activity was relatively low compared with that of the previous two surveys.

The first bat heard was a common pipistrelle approximately 30 minutes post sunrise. The bat was seen foraging along the vegetation to the north of the site.

Small numbers of soprano and common pipistrelle calls were heard throughout the course of the survey with a single noctule and myotis sp. pass towards the end of the survey at the north of the site.

No bats emerged from or interacted with the building on this date.

4.3 Identified Roosts

The building was not identified as a bat roost on this date.

4.4 Conclusion & Recommendations

Bat activity at the site is moderate across the full set of surveys. Species heard include common pipistrelle, soprano pipistrelle, noctule, myotis sp and lesser horseshoe bats.

No bat roosts were identified within the building on the site. Due to the complex access around the building, it is considered necessary that the works are undertaken in line with a method statement (appended to this report).

If at any point bats or evidence of bats are found, all works will cease, BE Ecological Ltd will be informed, NRW consulted. Further surveys and/or a licence may be required prior to works recommencing on the building.

4.5 Breeding Birds

No evidence of breeding birds was found throughout the buildings at the time of survey. Should a birds nest be identified within the building during works, it will be left until such a time the young have fledged the nest of their own accord.

5 INTERPRETATION & IMPACT ASSESSMENT

5.1 Active Season Usage

At the time of survey it appears that the building is not a bat roost.

5.2 Hibernation Season Usage

It is considered that due to the level of disturbance presence at the building. Hibernation is unlikely.

5.3 Ecological Impacts of development

It is considered that the property is not a bat roost and therefore impacts on roosting bats are unlikely.

6 ENHANCEMENT

6.1 Bats

Three bat tubes <https://www.nhbs.com/ib-vl-05-vivara-pro-build-in-woodstone-batbox> or similar will be installed in the south eastern elevation of the new build. The bat boxes will be positioned beneath the eaves and protected from any lighting.

6.2 Birds

Three Schwegler 1SP Sparrow Terraces or the following <https://www.nhbs.com/sparrow-terrace-nest-box> will be attached to the northern and eastern elevations of the new build.

Native species planting will be incorporated into the final design and any landscaping.

7 RECOMMENDATIONS

7.1.1 Timing

It is considered that the building is not a bat roost and therefore restrictions on timings are not necessary.

7.1.2 Timber/roofing materials

N/A- the building is not a bat roost

7.1.3 Lighting

Bat boxes and any bat mitigation/compensation will not be directly illuminated. All external lighting will face downwards and be set on timers to ensure that bats can use the area should they wish. – In addition to this, any onsite lighting will conform to the following guidelines:

<https://theilp.org.uk/publication/guidance-note-8-bats-and-artificial-lighting/>

The eastern boundary of the site (railway line) should be protected from any onsite lighting due to the presence of lesser horseshoe bats.

7.1.4 Bat Licensing

A bat licence will not be required in this instance.

7.1.5 Supervision

N/A.

7.1.6 Compliance

Following completion of the project, the ecologist will visit the site to verify the correct installation of

the enhancement measures. E-mail confirmation will be issued to the LPA.

8 REFERENCES

Bat Conservation Trust. (2016) *Bat Surveys - Good Practice Guidelines*. Bat Conservation Trust, London.

Mitchell-Jones, A.J. & McLeish, A.P. (2004) *The bat workers' manual (3rd Edition)*. Joint Nature Conservation Committee.

Mitchell-Jones, A.J. (2004). *Bat Mitigation Guidelines*. Natural England.

The Conservation of Habitats and Species Regulations 2017 (HMSO).

The Natural Environment and Rural Communities Act (2006) (as amended) (HMSO).

The Wildlife and Countryside Act 1981 (as amended) (HMSO).

APPENDIX A- PHOTOGRAPHS







9 METHOD STATEMENT

1. A suitably licenced and experienced ecologist will be on call for the duration of the works.
2. Before any work begins on site, a briefing for contractors and other site-staff 'toolbox talk' will be given by an ecologist. The briefing will cover the issues in respect of protected species they may encounter on site, where they might find them, methods of working, and what they need to know to avoid committing an offence. Every briefing attendee will be provided with a copy of a Method Statement and the contact details of an ecologist and Natural Resources Wales.
3. If at any point bats or evidence of bats is found, all works will cease, BE Ecological Ltd informed and NRW consulted.
4. If bats or their signs are found, a EPS licence may be required before works can legally resume.

APPENDIX 4 - ARBORICULTURAL REPORT



ArbTS - Arboricultural Technician Services Ltd

(Tree Consultancy Services)

Stephen Lucocq *BSc (Hons), Tech Cert (ArborA), M.Arbor.A*
Professional Member of the Arboricultural Association

Web site: www.ArbTS.co.uk

Email: info@ArbTS.co.uk

Mobile: 07789 551 591

Arboricultural Report

Including:

Tree Survey Data &

Tree Constraints Plan,

Arboricultural Impact Assessment,

Tree Protection Plan and Arboricultural Method Statement

To the British Standard 5837:2012
*(Trees in relation to design, demolition
and construction. Recommendations)*

Date – 25th January 2023

Site – Cardonnel Road, Skewen

Project Reference – ArbTS_1574.1_Cardonnel Road

Table of Contents

1.0	Introduction	3
2.0	The Tree Survey	3
3.0	The Trees	4
4.0	Tree Constraints Plan Information	4
5.0	Arboricultural Impact Assessment	5
6.0	Arboricultural Method Statement	6
7.0	Conclusion	7
8.0	Qualifications & Further Information	8
9.0	Bibliography & Web Information	9
10.0	Appendix	
1A	Tree Survey Data + 1B - Detailed Tree Survey Data Summary	
2	Tree Constraints Plan	
3	Tree Survey Key	
4	Tree Protection Plan	
5	Tree Photographs	

Copyright © 2023

ArbTS - Arboricultural Technician Services Ltd, 5 Weavers Road, Ystradgynlais, Powys, SA9 1PQ. All rights reserved.

No part of this report may be copied or reproduced without prior written permission from ArbTS.

If you have received this report in error, please destroy all copies in your possession or control.

This report has been prepared for the exclusive use of the commissioning party, and unless otherwise agreed in writing by ArbTS, no other party may use, make use of or rely on the contents of this report.

ArbTS accept no liability for any use of this report other than for the purposes for which it was initially prepared and provided.

Opinions and information provided in the report are based on ArbTS using due skill, care and diligence in preparing the same. No warranty is provided as to their accuracy.

Surveys are undertaken to ensure that nothing in the final report will be omitted, amended or misrepresented by the client or any other interested party.

This report and its contents remain the property of ArbTS until payment has been made in full.

It should be noted, and it is expressly stated, that no independent verification of any of the documents or information supplied to ArbTS has been made.

1.0 Introduction

- 1.1 The purpose of this report is to assess the quality of the trees at Cardonnel Road, Skewen, assess the arboricultural impact of the proposed development design and provide details regarding the protection of retained trees during construction work.
- 1.2 This report identifies the quality of the trees on this site as categorised by the *British Standard 5837:2012, Trees in relation to design, demolition and construction - Recommendations*. The survey and findings, as reported here, represent an unbiased third-party opinion offering professional advice on the value of the trees on or adjacent to this site. To illustrate the constraints identified trees pose to the design of future development, a Tree Constraints Plan (TCP) has been drawn, as found in Appendix 2.
- 1.3 Arboricultural constraints within the surveyed site relate primarily to the preservation of trees recommended for retention. Identified trees must be protected during the construction phase by employing a combination of tree protection methods as illustrated in Appendix 4, Tree Protection Plan and detailed within Section 6 - Arboricultural Method Statement.
- 1.4 The trees' root system and the associated soil structure is often overlooked during the construction process and can be damaged or altered by compaction, causing significant damage to the health of the tree. Generally, the tree's entire root system is within the top 600mm of soil, where it can be easily damaged. A calculated ground area around the tree should be protected during the onsite construction phase. In this report, it is referred to as the Root Protection Area (RPA).

2.0 The Tree Survey

- 2.1 The tree survey was conducted by *Stephen Lucocq BSc (Hons), Tech Cert (ArborA), M.Arbor.A* on 18th January 2023.
- 2.2 Trees over 75mm were tagged where appropriate with numbered metal identification tags at around 2.0 metres above ground level.
- 2.3 All observations were made from the ground with an acoustic-sounding hammer. No invasive decay detective instruments were used.
- 2.4 The survey was carried out per *British Standard 5837:2012, Trees in relation to design, demolition and construction - Recommendations*. This standard gives a systematic, consistent, transparent evaluation method for tree surveying.
- 2.5 The tree survey was conducted with the aid of a topographical survey.
- 2.6 **Preliminary management recommendations:** The survey has identified preliminary management recommendations for the trees on or adjacent to this site. Details regarding these specified operations are given in this report (See Appendix 1 - Tree Survey Data). Where work priority is stated to be H – High due to safety reasons, these operations should be carried out as soon as possible. Where work priority is

said to be M/H – medium/high or higher, these operations should be undertaken before the commencement of any works on site.

- 2.7 **Limitations of the tree survey:** Whilst every effort is made to ensure an accurate assessment of the tree's condition during the survey, no responsibility can be taken for resultant damage or injury that occurred by a failing tree. The survey only gives a snapshot of what is visible and is not obscured on the day of the survey. The survey identifies trees of varying quality and their above-ground/below-ground constraints. This survey does not constitute a full tree condition survey/tree risk assessment of the site, and this report is only valid for 24 months from the date of the tree survey.

3.0 The Trees

- 3.1 The complete tree survey data can be found in Appendix 1A Tree Survey Data
- 3.2 Tree Survey Summary Table (See Appendix 3 for BS5837 category definitions).
(A more detailed Tree Survey Data Summary can be found in Appendix 1B)

BS5837:2012 Quality Category	Total Number of Individual Trees Surveyed	Total Number of Tree Groups Surveyed	Total Number of Tree Areas Surveyed	Total Number of Woodland Areas Surveyed	Total Number of Hedgerows Surveyed	Total
A (High - Most desirable for retention)	1	0	0	0	0	1
B (Moderate - Desirable for retention)	1	0	0	0	0	1
C (Low - Optional for retention)	2	5	0	0	1	8
U (Poor - Unsuitable for retention)	0	0	0	0	0	0
Total A,B,C,U	4	5	0	0	1	10

4.0 Tree Constraints Plan (TCP) Information

- 4.1 A Tree Constraints Plan (TCP) can be found in Appendix 2 of this report. An introduction to TCP can also be found at the start of this Appendix Section. For further information and details regarding TCP, please see the *British Standard 5837:2012, Trees in relation to design, demolition and construction – Recommendations*.

5.0 Arboricultural Impact Assessment (AIA)

5.1 The following Arboricultural Impact Assessment has been made for the proposed development design.

5.2.1 Tree Loss – AIA – LOW - The following trees are required to be removed to facilitate the construction of the proposed development design.

5.2.2 Individual Tree Loss –

- Tree T4 - Sycamore – Low quality (C category)

5.2.3 Grouped Tree Loss –

- Tree Group – G9 – Leyland Cypress – Low quality (C category)

5.2.4 Overall Tree Loss –

One tree and one tree group are identified to be removed to facilitate the construction of the proposed development design. All these trees identified for removal are low-quality (C Category). These trees should not present a constraint on developing the site.

5.3 Root Protection Area (RPA) – AIA – LOW - RPA potential damage can be managed by installing tree protective fencing, as designed by an Arboriculturist, which will ensure no significant long-term adverse effects impact will occur to any of the retained trees.

5.4 Tree surgery work – AIA – LOW - Some minor branch reduction/branch lifting pruning work will be required to facilitate this proposed scheme, as detailed in the tree protection plan (Appendix 4). This work will be carried out to the *British Standard 3998:2010 tree work recommendations*. Adhering to this standard will ensure no adverse impact on these trees' long-term health or visual amenity.

5.5 Future Tree Pressures – AIA – LOW / MODERATE - The development design has considered the tree constraints of the larger higher value trees on this site to ensure they are suitably included in the design. Overall, the design has considered the size and value of the trees to minimise any future pressures to heavily prune or fell the higher-value trees

5.6.1 AIA – Conclusion – Overall AIA – LOW - The site has several Arboricultural constraints that must be considered in the development design phase. One tree and one tree group are identified to be removed to facilitate the construction of the proposed development design. All these trees identified for removal are low-quality (C Category). These trees should not present a constraint on developing the site.

5.6.2 This proposed development design has aimed to retain all of the higher-value trees (A + B Category) that form part of the site whilst sustainably using it for residential development.

- 5.6.3 The construction of the proposed development, whilst complying with the tree protection scheme as detailed in section 6, will ensure that no significant long-term adverse Arboricultural impact occurs on the health of any retained trees on or adjacent to this site or the long-term amenity of the area.

6.0 Arboricultural Method Statement

- 6.1 The Tree Protection Plan to facilitate the construction of the development design can be found in Appendix 4 of this report. The Tree Protection Plan must comply with all of the following:

- Be regarded as sacrosanct and follow the sequence of events as detailed in the table below
- Be installed before commencement of any demolishing or construction works on site
- Must not be removed or altered without prior approval of the local planning authority

- 6.2 The following table below provides a detailed sequence of events that must occur to protect the retained trees during all stages of the construction process. These methods must be communicated to the entire construction team before any work on site.

Stage	Arboricultural Method Statement (In the sequence of events)
1.) Preconstruction (Prior to any on-site construction work, including demolition work, site material storage etc.)	1.1 – Design areas for construction site storage by the site supervisor and the appointed Arboriculturist.
	1.2 – Design position, form and construction methods of all utility services with Arboricultural consideration. All underground service designs MUST conform to the NJUG Volume 4 Guidelines for the Planning, Installation and Maintenance of Utility Apparatus in Proximity to Trees. The full document is available at http://www.njug.org.uk/ . Local Planning Authority to be consulted on utility service design details and, if satisfied, to be approved in writing before installation during the construction phase.
	1.3– Tree surgery work to be carried out is detailed in the Tree Protection Plan (Appendix 4) of this report and to the <i>British Standard:3998:2010: Recommendation for tree works</i> .
	1.4 – Tree protective fencing installed in the position and form as detailed in the Tree Protection Plan (Appendix - 4). Installation is to be supervised by the appointed Arboriculturist. All weather tree construction exclusion zone posters are to be secured to fencing at regular intervals.
	1.5 – Site storage area containers installed as designed and supervised by the site supervisor and the appointed Arboriculturist.
	1.6 – Appointed Arboriculturist to document all tree protection methods in situ and photographs taken for reference purposes. Copy of document report sent to all parties.

2.) Construction	2.1 – The site supervisor is to be briefed by the appointed Arboriculturist regarding the Tree Protection Plan/Methods, and a laminated copy of the plan/methods is to be secured onto the wall in the site supervisor's office. Contact details of the appointed Arboriculturist, Council's Tree Officer, to be included. Emphasis is to be made to the site supervisor on the importance of the Tree Protection Plan/Methods and possible planning enforcement action (Stop Notice), problems with discharging tree protection conditions and/or legal action for noncompliance with these tree protection methods.
	2.2 – All contractors are to be briefed by the site supervisor and/or the appointed Arboriculturist regarding the tree protection plan and methods before starting work on site. Emphasis made to contractors on the importance of the Tree Protection Plan/Methods and possible planning enforcement action (Stop Notice), problems with discharging tree protection conditions and/or legal action for noncompliance with these tree protection methods.
	2.3 – The construction phase begins
	2.4- Tree Safe Construction (Throughout site) – areas outside of the construction exclusion zones, as shown on the tree protection plan, must adhere to the following: • Building materials and fuels such as oil, bitumen or cement should not be stacked or discharged within 20 metres of the tree's stem. • Fires will not be lit beneath any tree or in a place where flames could extend to within 10 metres of the tree. • Trees to be retained and protected should not be used as anchorage for services or equipment. • The use of cranes and large machinery on site should be planned and care taken not to damage the trees during the process.
	2.5 – Unforeseen issues which require the alteration of the Tree Protection Plan/Methods, required tree surgery work or immediate remedial work will be submitted to the Local Planning Authority for approval in writing.
3.) Post Construction (<i>Once all construction work has been completed, this includes all utility services</i>)	3.1 – Tree Protection fencing Removed.
	3.2 – Hard and soft landscaping commence - All landscape team members are to be briefed regarding tree protections by an Arboriculturist.
	3.3 – Any required remedial tree action is taken , such as Leaf Mulch Application, soil de-compaction methods, contamination clean up etc., to be carried out.

7.0 Conclusion

- 7.1 Adhering to the tree protection details in this report, the proposed development can be constructed without any significant long-term adverse impact on the retained trees or the area's amenity.

8.0 Further Information & Qualifications

Stephen Lucocq has been involved in Arboriculture within South Wales for over twenty years. He has worked as an Arborist for many of these years and has an excellent working knowledge of the practical side of the profession. He has always taken an active interest in all areas of Arboriculture and kept up to date with current research and developments.

Qualifications

- First Class BSc (Hons) Degree – Combined Studies - Biology and IT
- Arboricultural Association Technicians Certificate – Level 4 - (Merit)
- PTI - Professional Tree Inspection (Lantra Awards)
- 2D Computer-Aided Design (City and Guilds - Level 3)
- Quantified Tree Risk Assessment (QTRA) – Mike Ellison
- Visual Tree Assessment (VTA) – Mike Ellison
- Arboriculture and Bats (Lantra)
- Industrial Rope Access Trade Association (IRATA)
- Practical Arboriculture Qualifications (NPTC)

Membership

- Arboricultural Association Professional Member (M.Arbor.A)

9.0 Web Information & Bibliography

Web Information

- Arboricultural Association
<http://www.trees.org.uk/>
- Cellular Confinement System
GeoWeb - [GreenFix](#)
CellWeb - [Geosynthetics](#) [Cellweb](#)
- Underground Utilises Installation
<http://www.njug.org.uk/>

Bibliography

- British Standards 3998 (2010) Recommendations for Tree Work UK; British Standards Intuition
- British Standard 5837:2012, Trees in relation to design, demolition and construction - Recommendations UK; British Standards Intuition
- Coombes, A.J (1992) Trees London; Dorling Kindersley
- Lonsdale, D (1999) Principle of Tree Hazard Assessment and Management Edinburgh; Forestry Commission
- Mattheck, C (2007) Field Guide for Visual Tree Assessment Germany; Karlsruhe Research Centre
- Shigo, A.L (1991) Modern Arboriculture USA; Shigo and Trees, Association
- Sterry, P (2007) Collins Complete British Trees London; Collins
- Strouts, R.G (2000) Diagnosis of ill-health in trees Edinburgh; Forestry Commission
- Weber, K & Mattheck, C (2003) Manual of wood decay UK; Arboricultural Association

10.0 Appendix 1A -Tree Survey Data

Tree ID #	Tree Species	Age	Stems	Stem Diam (mm)	Cat	Height+ (Lower Branch Height)	Nrth	Est	Sth	Wst	Phys Cond	Struc Cond	Est. Remain Contrib	Comments	Preliminary Management Recommendations	Work Priority	RPR (m)	RPA (m2)
G1	Alnus glutinosa (Common Alder)	M	1	300	C2	12(5)	4	4	4	4	F/P	F	10+	low C category. Ivy on tree. Surrounding vegetation prevented close inspection of the tree therefore all observations and measurements are estimated.	fell poor condition alder	H/M	3.6	40.72
H2	Prunus laurocerasus (Cherry Laurel),privet	EM	1	75	C2	3(0)	1	1	1	1	F	F	10+	Received little noticeable recent maintenance.			0.9	2.55
T3	Quercus robur (Common Oak)	M	1	850	A2	12(6)	8	8	5	8	G/F	N/A	40+	low A category. Surrounding vegetation prevented close inspection of the tree therefore all observations and measurements are estimated.	oak of some age, twin stem, fair to good form, southern side of crown cut back from existing building, located on a lower level than site building		10.2	326.9
T4	Acer pseudoplatanus (Sycamore)	EM	1	300	C2	9(3)	4	4	2	3	F	F	10+	Surrounding terrain prevented close inspection of the tree therefore all observations and measurements are estimated.	small multistemmed sycamore, ivy on stems		3.6	40.72
T5	Alnus glutinosa (Common Alder)	M	1	350	C2	12(3)	4	2	4	4	F	N/A	10+	Surrounding terrain prevented close inspection of the tree therefore all observations and measurements are estimated.	multistemmed alder with ivy cover		4.2	55.42
T6	Quercus robur (Common Oak)	M	2	450	B2	10(1)	6	6	7	7	G/F	G/F	20+	Ivy on tree.	twin stem oak located on high level behind retaining wall		7.63	182.9
G9	X Cupressocyparís leylandii (Leyland Cyp)	M	1	200	C2	6(0)	2	2	2	2	G/F	F	10+	small section of leylandii conifers growing along side retaining wall			2.4	18.1
G10	X Cupressocyparís leylandii (Leyland Cyp)	M	1	350	C2	11(0)	4	4	4	4	G/F	F	10+	small section of leylandii conifers			4.2	55.42
G11	Acer pseudoplatanus (Sycamore)	M	1	350	C2	12(4)	4	4	4	4	F	N/A	10+	Surrounding vegetation prevented close inspection of the tree therefore all observations and measurements are estimated.	boundary group of sycamore upright in form, inspected from a distance		4.2	55.42
G12	Unknown (Unknown)	M	1	350	C2	12(4)	4	4	4	4	F	N/A	10+	Surrounding vegetation prevented close inspection of the tree therefore all observations and measurements are estimated.	boundary group of upright in form, inspected from a distance		4.2	55.42

10.0 Appendix 1B – Detailed Tree Survey Data Summary

(Please see Appendix 3 - Tree Survey Key)

Field Usage Results.		
Total Records: 12		
Type	Count	% of Total
T	4	33.3
G	5	41.7
H	1	8.3
Tree Species	Count	% of Total
Alnus glutinosa (Common Alder)	2	16.7
Quercus robur (Common Oak)	2	16.7
Acer pseudoplatanus (Sycamore)	2	16.7
X Cupressocyparis leylandii (Leyland Cyp)	2	16.7
Unknown (Unknown)	1	8.3
Average Stem Diameter	Count	% of Total
<50	2	16.7
<100	1	8.3
<250	1	8.3
<500	6	50
<750	1	8.3
<1000	1	8.3
Cat	Count	% of Total
A2	1	8.3
B2	1	8.3
C2	8	66.7
U	2	16.7
Age	Count	% of Total
EM	2	16.7
M	8	66.7
Height	Count	% of Total
<5	1	8.3
<10	2	16.7
<15	7	58.3


Phy Cond	Count	% of Total
G/F	4	33.3
F	5	41.7
F/P	1	8.3
Stuc Cond	Count	% of Total
G/F	1	8.3
F	5	41.7
N/A	4	33.3
Est. Remain Contrib	Count	% of Total
10+	8	66.7
20+	1	8.3
40+	1	8.3
RPR	Count	% of Total
<5	10	83.3
<10	1	8.3
<15	1	8.3

10.0 Appendix 2 - Tree Constraints Plan

An introduction to the Tree Constraints Plan (TCP)

Trees identified to be retained should be treated as constraints to the design of future development. A Tree Constraints Plan has been drawn and can be found over leaf.

- **Tree Quality** - The TCP highlights the above and below-ground constraints each tree poses to design future development schemes. Further, the BS5837 tree quality category (A - High, B - Moderate, C - Low and U- Unsuitable for retention) are coloured coded as solid circles at the centre of the tree's position.
- **Root Protection Area** – The magenta circle on the TCP sets out the root protection area (RPA). No construction work in this area, ground-level alteration or site traffic (machinery or persons) should occur. This prevents damage to tree roots and soil compaction. (Where possible, an Arboriculturist can design suitable tree protection methods to facilitate construction work/site traffic within these areas).
- **Tree Canopy** - The green circle/oval on the TCP sets out the above-ground constraints of tree canopy spread. Within this area, no construction work or site traffic (machinery or persons) should occur if the tree is to be retained. This prevents damage to the tree branches and trunk. (Where possible, an Arboriculturist can design suitable tree protection methods to facilitate construction work/site traffic within these areas).
- **Tree Shading** – Shade from the retained trees should be considered in the development design. Depending on the tree's height and width, the shade cast will be from a North West to East pattern through the central part of the day.
- **Tree Future growth** - Within future development design, consideration should also be given to the ultimate height and extent of the canopy spread of all trees within site identified to be retained.



Legend

- Category A (High)**
Tree with a high level of preservation value, often due to its size, age, or historical significance. These trees are subject to strict protection measures.
- Category B (Medium)**
Tree with a medium level of preservation value. These trees are subject to moderate protection measures.
- Category C (Low)**
Tree with a low level of preservation value. These trees are subject to minimal protection measures.
- Category D (None)**
Tree with no preservation value. These trees are not subject to any protection measures.

Tree Constraints Plan

This plan shows the location and status of trees on the site. Trees are categorized into four groups based on their preservation value. The plan also shows the proposed development and the constraints imposed by the trees.

Tree Constraints


The plan shows the constraints imposed by the trees on the proposed development. These constraints are shown as shaded areas on the plan.

Tree Constraints Legend

- Tree Constraints**
The shaded areas on the plan represent the constraints imposed by the trees on the proposed development.
- Tree Constraints Legend**
The shaded areas on the plan represent the constraints imposed by the trees on the proposed development.

Notes

1. The plan shows the location and status of trees on the site.
2. Trees are categorized into four groups based on their preservation value.
3. The plan also shows the proposed development and the constraints imposed by the trees.
4. The shaded areas on the plan represent the constraints imposed by the trees on the proposed development.
5. The plan shows the constraints imposed by the trees on the proposed development.
6. The shaded areas on the plan represent the constraints imposed by the trees on the proposed development.
7. The plan shows the constraints imposed by the trees on the proposed development.
8. The shaded areas on the plan represent the constraints imposed by the trees on the proposed development.
9. The plan shows the constraints imposed by the trees on the proposed development.
10. The shaded areas on the plan represent the constraints imposed by the trees on the proposed development.

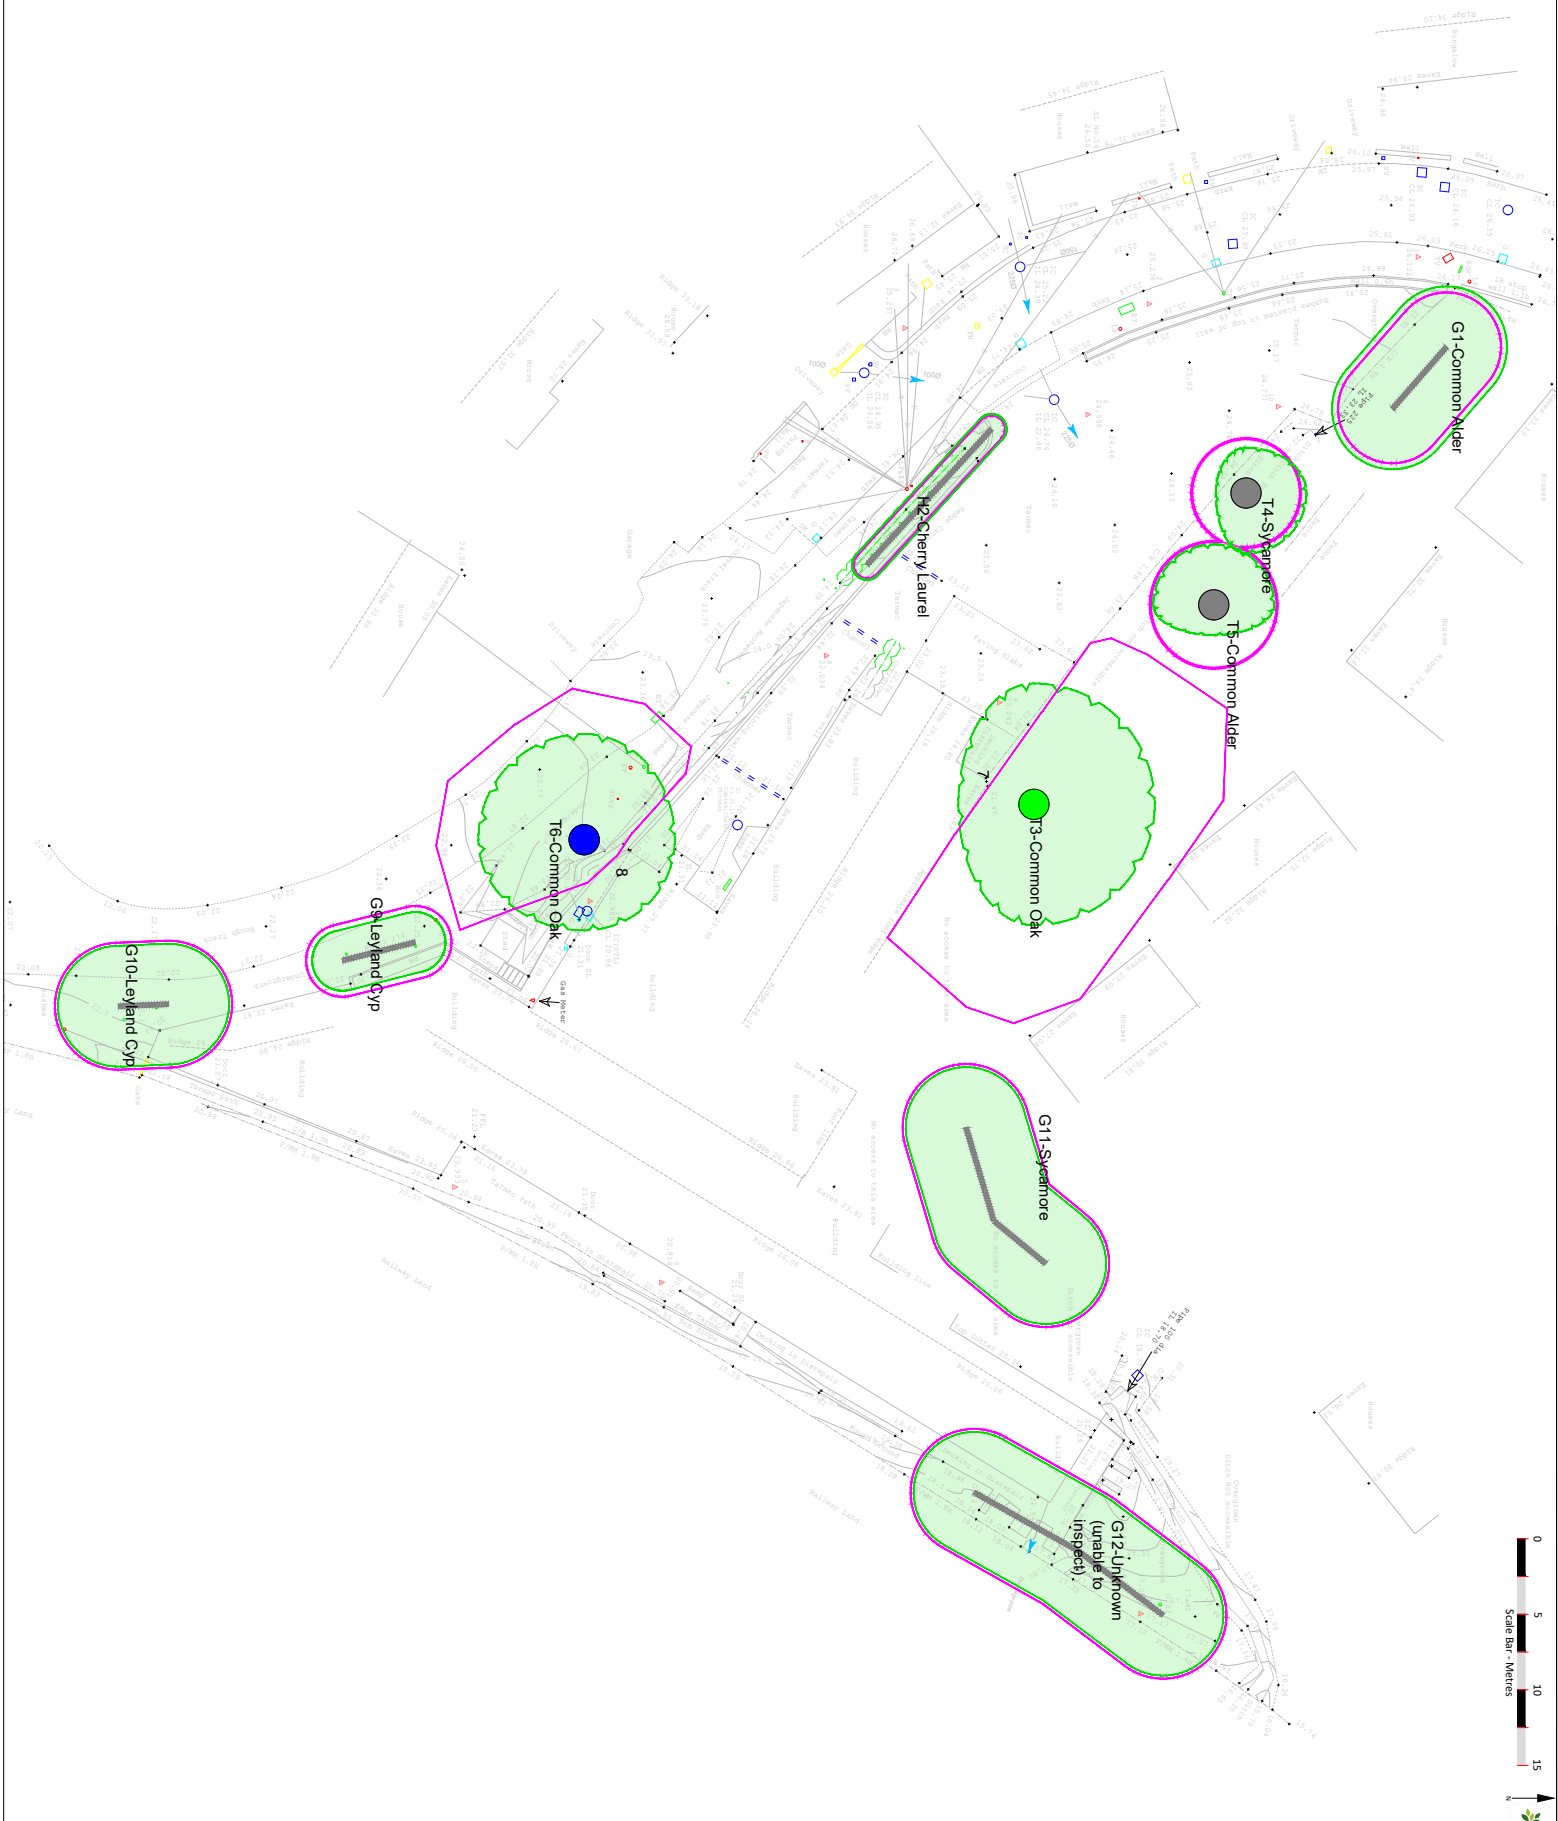

Legend

- Category 1 (High)
- Category 2 (Medium)
- Category 3 (Low)
- Category 4 (Dead)
- Category 5 (Dead)

Tree Constraints Plan

This plan shows the location and status of trees within the project area. Trees are categorized based on their size, health, and potential impact on the development. The plan also shows the proposed location of the development and the boundaries of the project area.

Tree Constraints

The following trees are identified as being subject to constraints:

- T1 - Common Alder
- T2 - Sycamore
- T3 - Common Oak
- T4 - Sycamore
- T5 - Common Alder
- T6 - Common Oak
- T7 - Sycamore
- T8 - Common Oak
- T9 - Sycamore
- T10 - Common Oak
- T11 - Sycamore
- T12 - Common Oak
- T13 - Sycamore
- T14 - Common Oak
- T15 - Sycamore
- T16 - Common Oak
- T17 - Sycamore
- T18 - Common Oak
- T19 - Sycamore
- T20 - Common Oak
- T21 - Sycamore
- T22 - Common Oak
- T23 - Sycamore
- T24 - Common Oak
- T25 - Sycamore
- T26 - Common Oak
- T27 - Sycamore
- T28 - Common Oak
- T29 - Sycamore
- T30 - Common Oak
- T31 - Sycamore
- T32 - Common Oak
- T33 - Sycamore
- T34 - Common Oak
- T35 - Sycamore
- T36 - Common Oak
- T37 - Sycamore
- T38 - Common Oak
- T39 - Sycamore
- T40 - Common Oak
- T41 - Sycamore
- T42 - Common Oak
- T43 - Sycamore
- T44 - Common Oak
- T45 - Sycamore
- T46 - Common Oak
- T47 - Sycamore
- T48 - Common Oak
- T49 - Sycamore
- T50 - Common Oak
- T51 - Sycamore
- T52 - Common Oak
- T53 - Sycamore
- T54 - Common Oak
- T55 - Sycamore
- T56 - Common Oak
- T57 - Sycamore
- T58 - Common Oak
- T59 - Sycamore
- T60 - Common Oak
- T61 - Sycamore
- T62 - Common Oak
- T63 - Sycamore
- T64 - Common Oak
- T65 - Sycamore
- T66 - Common Oak
- T67 - Sycamore
- T68 - Common Oak
- T69 - Sycamore
- T70 - Common Oak
- T71 - Sycamore
- T72 - Common Oak
- T73 - Sycamore
- T74 - Common Oak
- T75 - Sycamore
- T76 - Common Oak
- T77 - Sycamore
- T78 - Common Oak
- T79 - Sycamore
- T80 - Common Oak
- T81 - Sycamore
- T82 - Common Oak
- T83 - Sycamore
- T84 - Common Oak
- T85 - Sycamore
- T86 - Common Oak
- T87 - Sycamore
- T88 - Common Oak
- T89 - Sycamore
- T90 - Common Oak
- T91 - Sycamore
- T92 - Common Oak
- T93 - Sycamore
- T94 - Common Oak
- T95 - Sycamore
- T96 - Common Oak
- T97 - Sycamore
- T98 - Common Oak
- T99 - Sycamore
- T100 - Common Oak



10.0 Appendix 3 - Tree Survey Data Key

- **Tree ID #** - Identifies the location of individual trees (T-ID Number), Groups of trees (G-ID Number), Area of trees (A-ID Number), Hedgerow (H-ID Number), Woodland (W-ID Number), Row of trees (R-ID Number) and tree Stumps (S-ID Number) on the accompanying plan. *(Please note: A group of trees here refers to two or more standing trees that form a visual whole, whereas an area of trees refers to dispersed individual trees standing within the site)*
- **Tree Species** - Scientific names and common tree name in brackets are generally shown.
- **Age**
 - o (Y) Young – Less than 1/3 of life completed
 - o (SM) Middle Aged - 1/3 - 2/3 of life completed
 - o (EM) Early Mature – Just entering Maturity
 - o (M) Mature – more than 2/3 of life completed
 - o (OM) Over Mature - more than 3/3 of life completed and declining
 - o (V) Veteran - (v) Veteran – Veteran trees have no precise definition but are trees considered to be of biological aesthetic or ecological value because of their age
- **Stems** – Number of tree stems used to calculate the RPR/RPA
- **Stem Diam** (mm) - Diameter of tree stem measured in millimetres for single stem trees or average stem diameter calculated for multi-stemmed trees as detailed in section 4.6 & Annex C of the British Standard 5837:2012, Trees in relation to design, demolition and construction - Recommendations. The height above ground level where the stem measurement was taken will be shown if not measured at 1.5 metres above ground level. *(Please note: that the stem diameter of certain trees will have to be estimated due to difficulties in taking measurements or for trees with a large number of stems)*
- **Cat** – Tree Quality Category - British Standard 5837:2012 A, B, C, U + 1, 2, 3

Based on BS5837:2012, categories A, B, C, and U provide the basis for prioritising trees for retention:

- o A – Those of high quality with an estimated remaining life expectancy of at least 40 years. (*Most desirable for retention*)
- o B - Those of moderate quality with an estimated remaining life expectancy of at least 20 years. (*Desirable for retention*)
- o C – Those of low quality with an estimated remaining life expectancy of at least 10 years, or young trees with a stem diameter below 150mm. (*Optional for retention*)
- o U – Those in such a condition that they cannot realistically be retained as living trees in the context of the current land use for longer than 10 years. (*Unsuitable for retention unless provides high conservation value*)

Retention Criteria Subcategories: Used for identifying subcategories

E.g. A2 = A high-quality tree with high landscape qualities (further details can be found in British Standard 5837:2012, Trees in relation to design, demolition and construction - Recommendations UK; British Standards Intuition)

- o 1 – Mainly Arboricultural qualities
 - o 2 – Mainly landscape qualities
 - o 3 – Mainly cultural values, including conservation
- **Height + (Lower Branch Height)** - Tree height in metres and in brackets height in metres of the crown (tree branches) clearance at its lowest point above adjacent ground levels.
- **Nrth, Est, Sth, Wst** - Crown Spread (Metres) -Tree branch spread in metres measured in four directions (North, East, South, West) from the trunk.
- **Phys Cond** - Physiological Condition Indicating the health of the tree -
 - o (G) Good
 - o (F) Fair
 - o (P) Poor
 - o (D) Dead
- **Struc Cond** – Structural Condition indicating the structural integrity of the tree -
 - o (G) Good – No, or remediable physical defects or decay
 - o (F) Fair - Physical non-remediable defects or decay present, not presenting imminent danger but should be monitored
 - o (P) Poor - physical non-remediable defects or decay present, tree liable to imminent collapse or loss of major limbs.
 - o (D) Dead
- **Est. Remain Contrib - (<10, 10+, 20+, 40+)**

The trees estimated remaining contribution in years, recorded as:

 - o <10 – less than 10 years
 - o 10+ – at least 10 years
 - o 20+ – at least 20 years
 - o 40+ – at least 40 years
- **Comments** – Additional Comments, if required
- **Preliminary Management Recommendations** – Work Recommendations, including further investigation of suspected defects that require more detailed assessment and pose potential for wildlife habitat.

- **Work Priority** - Work Priority -This gives a work priority rating of preliminary management for each tree.
 - o H - High – Urgent work to be carried out as soon as practicable due to safety reasons (Within 14 days).
 - o H/M – High - Medium – Work to be carried out within 6 months/or before the construction phase begins
 - o M - Medium – Work to be carried out in 12 months
 - o L - Low – After consideration/Re-inspect in 18-24 months
 - o Blank – No work required.
- **RPR** – Root protection radius / **RPA** - Root Protection Area - Is a layout design tool indicating the minimum area around a tree deemed to contain sufficient roots and rooting volume to maintain the tree's viability and where the protection of the roots and soil structure is treated as a priority. RPR is a circular area measured as a radius in metres from the tree's centre, or RPA is an area in metres squared. This area may be changed in shape but not reduced in size, providing adequate protection for the tree's rooting system.

10.0 Appendix 4 – Tree Protection Plan

Tree Protection Plan
Site - Cardonell Road
Project Ref - 15741

- Scale 1:25 to A2
- KET3 and 2012 Final Quality Global Context
- Category A (High)
("Highly desirable to reference")
- Category B (Moderate)
("Useful for reference")
- Category C (Low)
("Useful for reference")

Category C (low)
("Optional for recreation")

Category U (poor)
("Unsuitable for recreation")


designed to protect the environment from or caused by fire or flooding, the Commission or Council or those of reserved to contain an effective

Diagram of a cell showing various organelles and their functions. The cell is bounded by a plasma membrane (pink) and a cell wall (green). Inside, there is a large central vacuole (blue), a nucleus (red), and various other organelles. Labels include: 'Plasma Membrane', 'Cell Wall', 'Nucleus', 'Mitochondrion', 'Chloroplast', 'Vacuole', 'Golgi Apparatus', 'Lysosome', 'Peroxisome', 'Centrioles', 'Cytoskeleton', 'Ribosomes', and 'Endoplasmic Reticulum'.



removed or altered without prior recommendation by an

- Local Planning Authority (LPA)

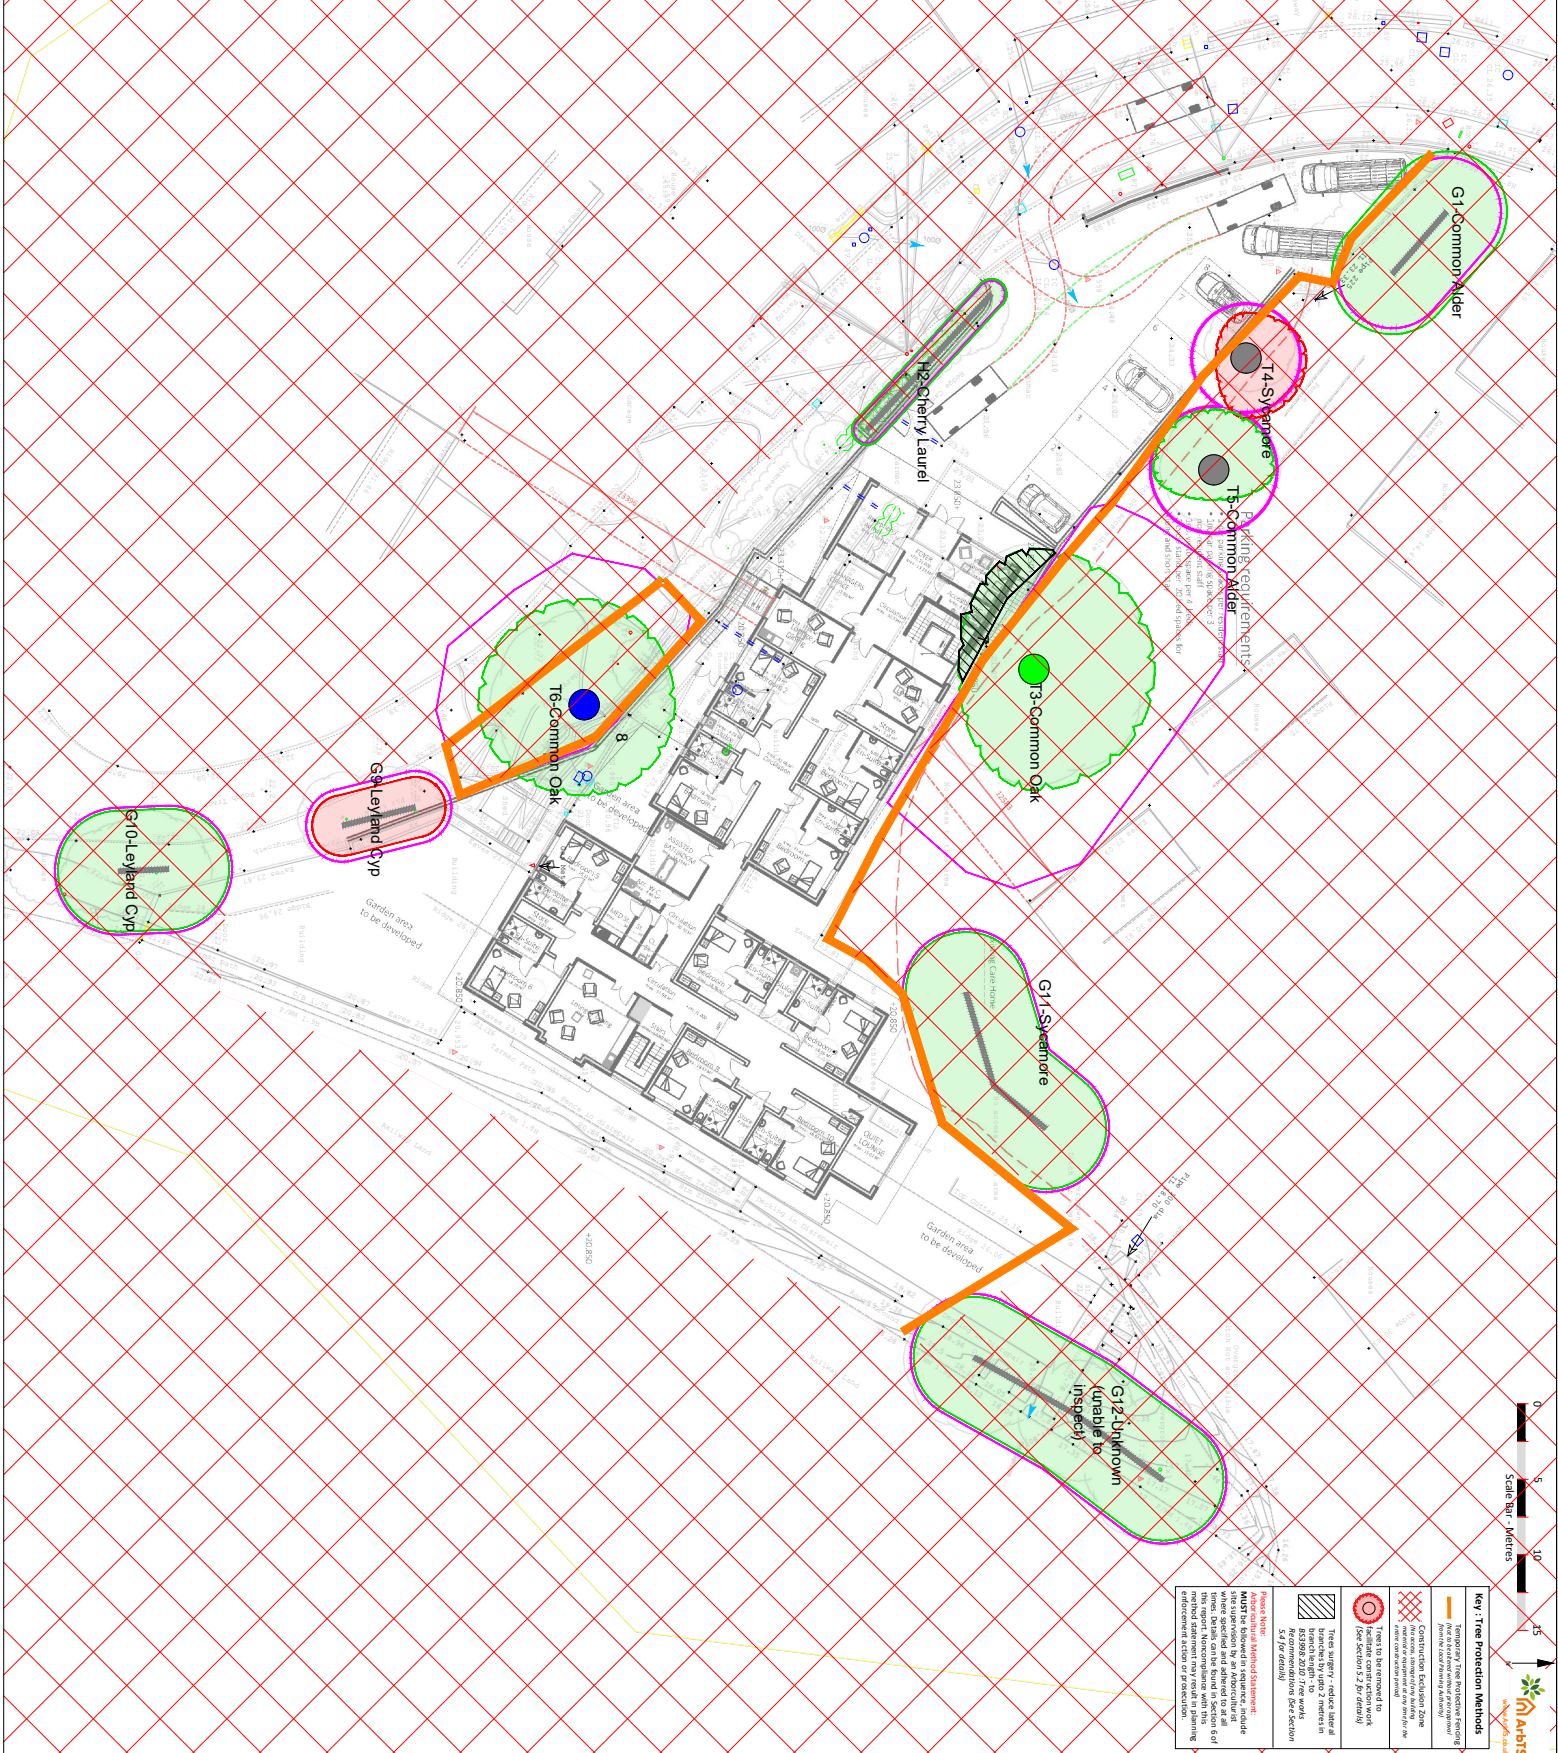

10.0 Appendix 5 – Tree Photographs

Tree ID#T3



Tree ID#G1, T4, T5



Tree ID#T3



Tree ID#T3 + H1



Tree ID#T6



Tree ID#G9



Tree ID#G10



Tree ID#G11





APPENDIX 5- JAPANESE KNOTWEED MANAGEMENT AND METHOD STATEMENT

Japanese knotweed Management Plan & Method Statement

SURVEYOR DETAILS

Company: Knotweed Control Swansea Limited
Name: Jo Mullett
Address: 4 Silver Close West Cross Swansea SA3 5PQ

CLIENT


Name: Mr Luke Hurley
Organisation: Hurley and Davies
E mail: luke@hurleyanddavies.co.uk

SITE DETAILS

Address: Cardonnel Court, Cardonnel Road, Neath SA10 6BS
Job ref: CC/ SA10 6BS/2023

DATES

Site visit: 19 January 2023
Report: 1 February 2023



CONTENT

- 1. BACKGROUND INFORMATION**
- 2. SITE DETAILS**
- 3. JAPANESE KNOTWEED ON SITE**
- 4. JAPANESE KNOTWEED DETAIL**
- 5. PROPOSED WORKS ON SITE IN RELATION TO THE JAPANESE KNOTWEED**
- 6. JAPANESE KNOTWEED METHOD STATEMENT**
- 7. JAPANESE KNOTWEED MANAGEMENT PLAN**
- 8. OTHER INVASIVE NON NATIVE PLANT SPECIES**

APENNDICIES

- i. KNOTWEED CONTROL SWANSEA LIMITED DETAILS**
- ii. THE SPREAD AND INVASIVE NATURE OF JAPANESE KNOTWEED**
- iii. SITE HYGIENE – BIOSECURITY MEASURES**
- iv. GENERAL JAPANESE KNOTWEED CONTROL METHODS**
- v. JAPANESE KNOTWEED CONTROL METHODS OFFERED BY KNOTWEED CONTROL**
- vi. LEGISLATION**
- vii. CODES & MORE INFORMATION**
- viii. KNOTWEED CONTROL SWANSEA LIMITED'S TERMS & CONDITIONS**
- ix. THE ENVIRONMENT AGNECY'S SUGGESTED WORDING FOR EXCLUSION FENCING**
- x. THE ENVIRONMENT AGNECY'S GUIDE TO JAPANESE KNOTWEED RHIZOME ID**

1. BACKGROUND INFORMATION

1.1. Background

- Formerly a 39 bed care home for the elderly, the site is now a state of disrepair and in the process of being sold.
- A pre-planning application enquiry (reference Q2022/0081) proposal has been registered with the Planning Department of Neath and Port Talbot Country Borough Council for the demolition of the existing build and construction of a new 2 storey building for 16 adults requiring supported living.
- The Planning Department require a Japanese knotweed Eradication Method Statement/Report in addition to information already received as both to limit the disturbance or spread the Japanese knotweed during any preparatory site investigation/survey as well as during the development phase of the proposed scheme.
- In January 2023 Mr Luke Hurly from Hurley and Davies, Chartered Surveyors contacted Knotweed Control Swansea Limited for assistance in regard to the Japanese knotweed on site on behalf of their clients who is in the process of purchasing the site.
- A site visit was undertaken by Knotweed Control Swansea Limited 19 January 2023 and this Japanese knotweed Management Plan report has been created laying out the options available for the Japanese knotweed following all current relevant legislation and best practice guidance.
- Although the Environment Agency's [Managing Japanese knotweed on Development Sites: Code of Practice](#) was withdrawn in 2016 and some of the information is out of date, it still is the best guidance for development or redevelopment sites with regards to Japanese knotweed.
- It is essential that all biosecurity measures (see ii. **SITE HYGIENE – BIOSECURITY MEASURES** are put in place BEFORE any other works or investigations are carried out.
- Several other invasive non-native species (INNS) were observed within the boundaries (see 8. **OTHER INVASIVE NON NATIVE SPECIES**).
- There is no equivalent development site guidance for the other invasive non-native species but there is a good legacy of suitable control, biosecurity and monitoring measures.

1.2. Scope of the Report

- Knotweed Control has not been given any details of the timing of the development and has only been supplied with a floor plan of the main building so the Japanese knotweed Management Plan and Method Statement covers the control, biosecurity and monitoring measures for;
 - Pre development works
 - Vegetation clearance/ control
 - Tree works
 - Demolition and removal works
 - Waste disposalAnd to a lesser degree;
 - Post development maintenance and management ground works
 - Use of the garden and outdoor space

1.3. Objectives

- The main objectives of this Japanese knotweed Management Plan/ Method Statement are to
 - ensure the owner & operators is aware of the potential issues, legalities and obligations with regards to Japanese knotweed
 - locate the general position of and condition, health and state the Japanese knotweed affecting the site
 - help to contain and minimise any spread of any viable Japanese knotweed propagules during all phases of the project both around and off site
 - provide control and management options of the Japanese knotweed
 - provide monitoring and longer term management options of the Japanese knotweed

2. SITE DETAILS

2.1. Site details

- The site is currently a derelict nursing home complex in a triangle of land between Cardonnel Road running diagonally from the north west to the south east, Bendle Close to the north and a railway line to the east.
- The foot print of the old buildings cover most of the east of the site with tarmacked parking and access towards the west.
- The boundary along Cardonnel Road from the north west to the south east consists of a raised concrete bed with woody shrubs, the old vehicle and pedestal entrance and a soil bank.
- The boundary along Bendle Close or northern boundary has running parallel an old wooden fence, a ditch and stream and a line of trees all backing onto the rear gardens of 2 to 17 Bendle Close.
- The boundary to the east has a fence separating the railway line embankment which falls steeply away down to the track, along the longest axis of the old building.

2.2. General Site Plan



General Site Plan

Key	
	Site boundary
	Existing building
	Stream/ ditch
	Railway line



2.3. Site ownership, boundaries, permissions & access

- The ownership of the site and potential purchaser are currently unknown to Knotweed Control, the houses to on Cardonnel Road and Bendle Close are assumed to be privately owned and railway line assumed to be owned and managed by Network Rail.
- The pre-planning application enquiry plans have been provide to Knotweed Control by Mr Luke Hurley from Hurley and Davies.
- Access is restricted to parts of the plot due to fencing, rotten decking, dense vegetation and the railway line and there are some steep slippery slopes, uneven ground, running water and fly tipped waste. The building has been broken into and some looting taken place.
- Japanese knotweed does not respect ownership or legal boundaries so permission to access and control any Japanese knotweed not within the site boundaries will be required so as not to cause reinfection.

Please note:

 *Where land owners cannot be located but all reasonable effort has been made to find and contact them, the owner of the subject property will be required to take responsibility and give written permission for treatment in the land owners absence before treatment can commence*

2.4. Water courses

- The stream in the ditch and along the northern boundary comes from a culvert popping out beneath Cardonnel Road and runs from west to east across the site.

Please note:

 *Under the Control of Pesticides Regulations 1986 a [Simple or Higher Risk Agreement for the use of Herbicide near water or a designated site](#) may be required from Natural Resources Wales.*


 *Aquatic approved herbicides only must be used near water courses by qualified operators.*

3. JAPANESE KNOTWEED ON SITE

3.1. General description

- The Japanese knotweed was observed in several locations around the site but all on the boundary perimeter.
- Japanese knotweed areas are as followings;
 - JK01, within the site boundary. subdivided into 4 different locations (JK01a, b, c & d)
 - JK02; along the boundary with Cardonnel Road
 - JK03; along the boundary with Cardonnel Road showing evidence of herbicide treatment
 - JK04; along the railway track showing evidence of herbicide treatment
 - JK05; to the north east of the site other side of the stream

3.2. Japanese knotweed Distribution Map

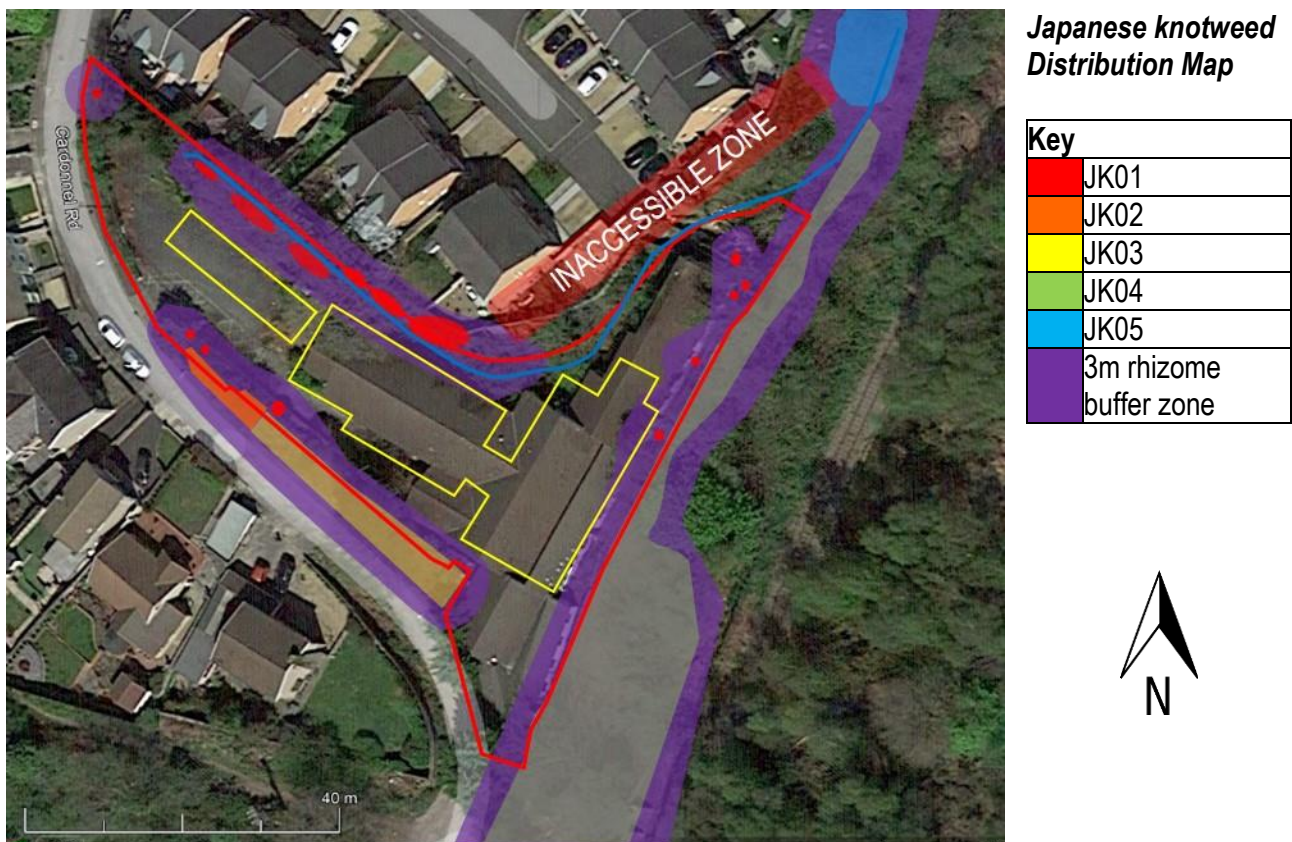

3.3. Original source of infection

- It can be impossible to say with certainty where the original source of the Japanese knotweed is on site.
- However in this case the railway is the most likely historical source the Japanese knotweed and the area is generally a well-known for Japanese knotweed.

Please note;

- ⚠ *South Wales is a hotspot for Japanese knotweed especially in where there is a history of heavy industry, soil disturbance helping spread the plant.*
- ⚠ *It is readily spread along railway lines, tramways, rivers, canals, roads & action such as fly tipping, contaminated waste & poor biosecurity practices, all of which have played their part in its spread.*
- ⚠ *Other invasive species are also not uncommon in this area and south Wales as a whole.*

3.4. Local sources of re-infection

- All mature established areas of Japanese knotweed that will affect the works directly and functions of the have been identified in this report and but it is possible there are smaller out breaks in the dense vegetation (see **3.6. History or evidence of herbicide treatment, control, disturbance & monitoring**)
- It must also be noted that there is a risk from other sources of Japanese knotweed including that;
 - not visible or obvious during the site visit due to evidence being removed, covered, treated etc.
 - dormant rhizome material under the ground
 - new contaminated material brought onto site
 - areas not treated as part of the Japanese knotweed Management Plan
 - secondary spread or cross contamination on site

3.5. Length of time Japanese knotweed on site

- Again it is often impossible to say with certainty how long the Japanese knotweed have been on site
- However the extensive areas of mature knotweed growing as a monoculture with tall thick stems and the deep leaf litter and in some places such as along the railway line where there are tell-tale large crowns, all indicate knotweed has been on site for many years.
- The oldest Google Earth aerial images available show Japanese knotweed has been on site since at least 1999 and the oldest Google Street View available for this area shows Japanese knotweed along Cardonnel Road since at least 2008.

3.6. History or evidence of herbicide treatment, control, disturbance & monitoring

- It appears there has been some control of the Japanese knotweed in areas JK01a, JK03 and JK04
- During the site visit on 19 January 2022 there were tall thick stems of Japanese knotweed in area JK01a are assumed to be from 2021 growing season not only because they are brittle faded but also there appears to be no growth in the 2022 season looking at Google Street View photos from June 2022. It is assumed the herbicide treatment took place in 2021.
- During the site visit area JK03 had the winter remains of short thin sporadic growth assumed to be from the 2022 season as it was moist and still brown orangey. There was also a lot of bare earth with limited revegetation from annual self-seeded plants that have blown in. Both indicated herbicide treatment. Some of the stems have stunted deformed regrowth called sub lethal bonsai growth not an uncommon response to glyphosate based herbicide treatment. Google Street View photos in area JK03 from June 2022 indicate that the area must have had herbicide treatment in 2021 and then again in 2022.
- The Japanese knotweed area JK04 along the railway embankment looking at Google Earth images shows it was a large mature and established area of knotweed from appeared from at least 1999 (large knotweed crowns still in evidence on site) but the aerial images appear to show treatment from 2016. During the site visit on 19 January 2022 the evidence supports this in area JK04 with remaining short thin sporadic regrowth and sub lethal bonsai growth typical of glyphosate based herbicide treatment.



Google Street View photos showing no live Japanese knotweed growth in June 2022 in area JK01a



During the site visit on 19 Jan 2022, faded brittle standing canes assumed to be from 2021 season



Google Street View photos from June 2022; JK03 yellow showing evidence of herbicide treatment



Site visit 19 January 2022; JK03 yellow showing bare ground, short thin sporadic regrowth




JK04 on railway embankment showing old large knotweed crowns (dark brown lumps in photo on the right), bare ground and short thin sporadic regrowth and some sub lethal bonsai growth

Please Note:

- △ Correct control from the outset is essential as inconsistency or incorrect control or disturbance can make the Japanese knotweed spread quicker than it might have otherwise reducing the effectiveness of future treatment, extending the timeframes and increasing costs. It is also very easy to spread Japanese knotweed as it only takes 0.7gm of rhizome the size of a pea to create new area of infestation.

4. JAPANESE KNOTWEED DETAIL

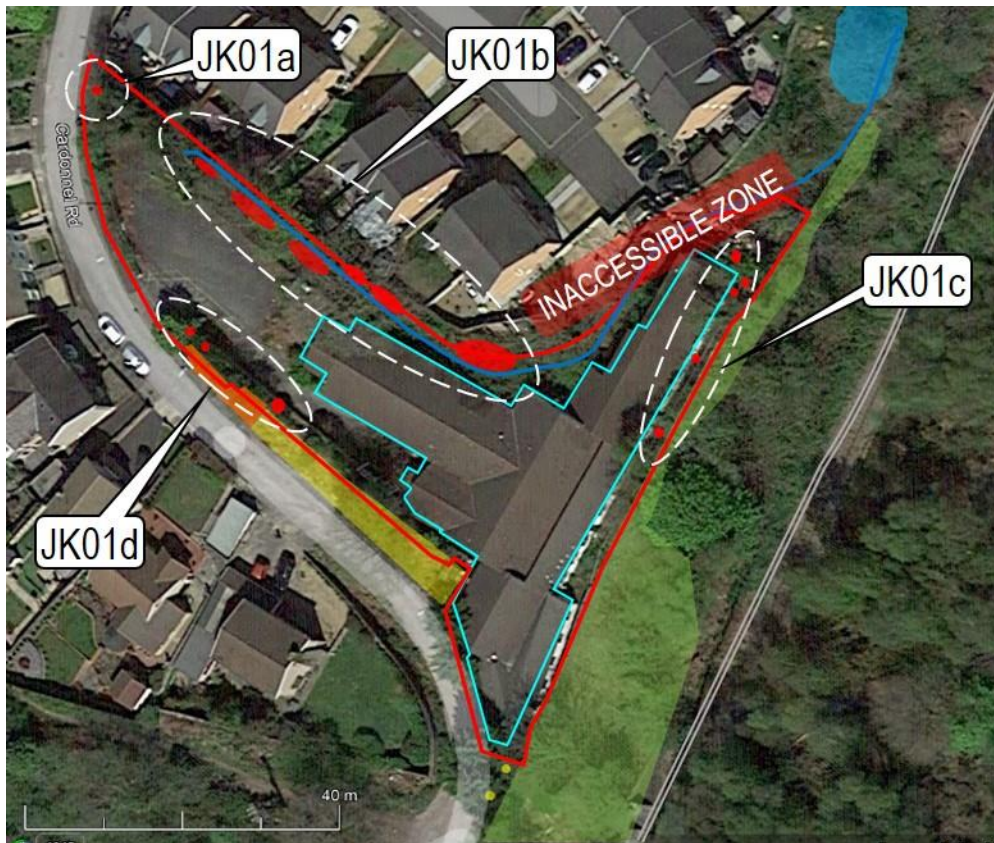

*Japanese knotweed
Distribution Map*

Key	
■	JK01
■	JK02
■	JK03
■	JK04
■	JK05

4.1.a. JK01a

Location	Within the site boundary in the raised concrete planting border along Cardonnel Road					
General	Small area of mature established knotweed					
2023 Growth	• Too early in the season any growth					
2022 Growth	• No evidence from growth from 2022 growing season					
2021 Growth	• A small area of mature and dense knotweed growth with tall thick fading fragile tall thick stems still standing from the 2021 growing season					
	Height	1-2.5m	Stem diameter	> & <8 mm	Density	Med
Other vegetation	Bramble					
Note	Evidence of herbicide (see 3.4. History or evidence of herbicide treatment, control, disturbance & monitoring)					



During the site visit on 19 Jan 2022, faded brittle standing canes assumed to be from 2021 growing season

4.1.b. JK01b

Location	Within the site boundary along the northern boundary with Bendle Close behind the wooden fence					
General	Mature established knotweed in several clumps mainly on the stream bank closest to the site although some on the opposite bank near some trees that have been felled					
2023 Growth	• Too early in the season any regrowth					
2022 Growth	• Tall thick dark black brown robust canes still standing with brown orangey seed stalks still in place					
	Height	0.2-2.5m	Stem diameter	> & <8 mm	Density	Med
2021 Growth	• Tall thick faded and fragile canes only standing due to support from younger canes					
Other vegetation	Bramble, ivy and other native woodland species					
Note	Fly tipped household and garden rubbish Access hindered towards east of site from fallen branches, bramble					



General area of JK01a behind the fencing with tall stems from 2022 growing season still standing with brown orangey seed stalks still in place



JK01b: Tall thick dark black brown robust canes from the 2022 growing season and tall thick faded and fragile canes from the 2021 growing season all along the southern stream bank

4.1.c. JK01c

Location	Within the site boundary along the eastern boundary parallel to the railway line					
General	Several individuals stems with one larger area with multiple canes					
2023 Growth	Too early in the season any growth					
2022 Growth	- Several individual short thin brown orangey stems still standing - A larger area with many tall thick dark black brown robust canes still standing with brown orangey seed stalks still in place					
	Height	0.2-2m	Stem diameter	> & <8 mm	Density	Low to med
2021 Growth	Larger area with tall thick faded and fragile canes only standing due to support from younger canes					
Other vegetation	Bramble and ivy and woodland species					
Note	Hard to access					



Several individuals stems with one larger area with multiple canes



Individuals stems along site the old building

4.1.d. JK01d.

Location	Within the site boundary on Cardonnel Road					
General	3 small area of mature established knotweed in the bank next to the entrance to the old building					
2023 Growth	• Too early in the season any growth					
2022 Growth	• Tall thick dark black brown robust canes still standing with brown orangey seed stalks still in place					
	Height	1-2.5m	Stem diameter	> & <8 mm	Density	Med
2021 Growth	• Tall thick faded and fragile canes only standing due to support from younger canes					
Other vegetation	Bramble and over grown woody shrubs					
Note	On the other side of the bank along Cardonnel Road is untreated knotweed area JK02					



3 small area of mature established knotweed in the bank next to the entrance to the old building

4.2. JK02


Location	Outside the site boundary along Cardonnel Road opposite 57 Cardonnel Road					
General	A large area of mature established untreated Japanese knotweed					
2023 Growth	• Too early in the season any growth					
2022 Growth	• Tall thick dark black brown robust canes with brown orangey standing and seed stalks still in place					
	Height	1.5-2m	Stem diameter	> & <8 mm	Density	High
2021 Growth	• Tall thick faded and fragile canes only standing due to support from younger canes					
Other vegetation	Monoculture of Japanese knotweed but with bramble and other hedgerow species at the edges					
Note	On the other side of the bank by the old building is knotweed area JK01d					



Google Street View photos from June 2022; JK03 yellow showing JK02 orange untreated area



Site visit 19 January 2022; JK03 yellow showing JK02 orange untreated area

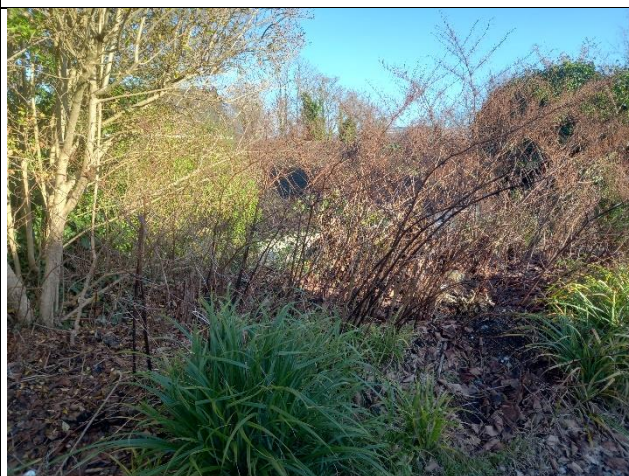

JK02 Tall thick dark black brown robust canes standing with brown orangey seed stalks still in place

4.3. JK03


Location	Outside the site boundary along Cardonnel Road opposite 57A Cardonnel Road					
General	A large area of mature established Japanese knotweed					
2023 Growth	Too early in the season any growth					
2022 Growth	- Winter remains of short thin sporadic growth moist and still brown orangey - Some stems with stunted deformed regrowth called sub lethal bonsai growth					
	Height	0.2-1.5m	Stem diameter	> & <8 mm	Density	High
2021 Growth	No older growth evident on site					
Other vegetation	Mainly bare earth with limited revegetation from annual self-seeded plants					
Note	Evidence of herbicide (see 3.4. History or evidence of herbicide treatment, control, disturbance & monitoring)					



Google Street View photos June 2022; JK03 yellow showing bare ground & short thin sporadic regrowth



Site visit 19 January 2022; JK03 yellow showing bare ground & short thin sporadic regrowth

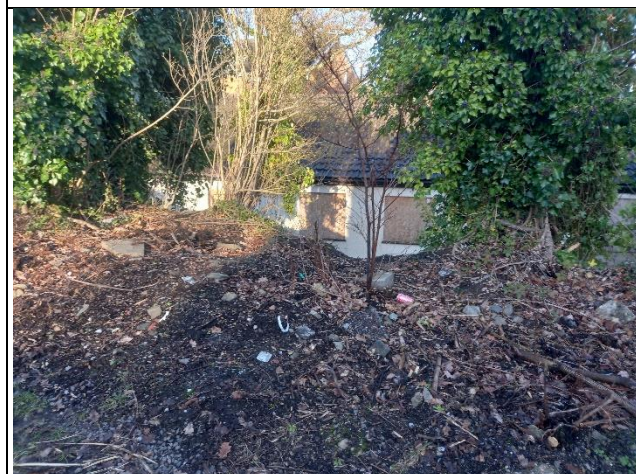

Bare ground and short thin sporadic regrowth all evidence of herbicide treatment

4.4. JK04

Location	Outside the site boundary along the railway embankment					
General	A large area of mature established Japanese knotweed					
2023 Growth	• Too early in the season any growth					
2022 Growth	• Winter remains of short thin sporadic growth moist and still brown orangey • Some stems with stunted deformed regrowth called sub lethal bonsai growth					
	Height	0.2-1.5m	Stem diameter	> & <8 mm	Density	High
Older Growth	• Large old crowns					
Other vegetation	Mainly bare earth with limited annual self-seeded revegetation					
Note	Evidence of herbicide (see 3.4. History or evidence of herbicide treatment, control, disturbance & monitoring)					



Winter remains of short thin sporadic growth & some stems with stunted deformed regrowth called sub lethal bonsai growth but mainly bare earth with limited revegetation



Large old crown old established mature knotweed (brown lumps)

4.5. JK05

Location	Unsure if within the boundary but in the north east of the general location perhaps along the stream/ ditch					
General	In inaccessible zone so observations from afar appear to show a large area of mature established Japanese knotweed					
2023 Growth	• Too early in the season any growth					
2022 Growth	• Appears to be tall thick dark black brown robust canes with brown orangey standing and seed stalks still in place					
	Height	1.5-2.5m	Stem diameter	> & <8 mm	Density	High
2021 Growth	• Too far to see					
Other vegetation	Appears to be a monoculture of Japanese knotweed surrounded by dense vegetation including thick bramble					
Note						



In an inaccessible zone but appears to be tall thick dark black brown robust canes with brown orangey standing and seed stalks still in place

4.6. Japanese knotweed Underground Rhizome Buffer Zone

- Japanese knotweed has been likened to an iceberg with only about 20% of the whole biomass of a mature plant being visible above ground including stems, leaves & crown material being above ground the rest being subterranean rhizome and root system.
- The actual extent of Japanese knotweed on site will depend on many factors including the volume, maturity and length of time growing on site and substrate/growing medium which will also affect the success of the herbicide treatment.
- In the **3.2. Japanese knotweed Distribution Map** the purple area is the theoretical 3m buffer zone potential underground rhizome growth around all visible areas of Japanese knotweed.
- 3m is required to be recorded and mapped in accordance with the Property Care Association [Code of Practice Management of Japanese Knotweed -2022](#) whilst the Environment Agency's Environment Agency [Managing Japanese knotweed on Development Sites: Code of Practice](#), (withdrawn in 2016) uses a 7m buffer/ safety zone which is now through to be very cautions but is still a good guide and to complicate things, research has shown rhizome rarely extends more than 4m from above ground growth. (Fennell, Wade, Bacon; [Japanese knotweed: An analysis of capacity to cause structural damage 2018](#)



5. PROPOSED WORKS ON SITE IN RELATION TO THE JAPANESE KNOTWEED

- Each site and situation is unique with regard to the control and management of Japanese knotweed and INNS with variations in the extent and age of infestation, location of planned works, infrastructure, access points, time and money available therefore different control methods and combinations can be adopted to suit the client and specific site issues (see v. **GENERAL JAPANESE KNOTWEED CONTROL METHODS**)
 - Although the Environment Agency's [Managing Japanese knotweed on Development Sites: Code of Practice](#) was withdrawn in 2016 and some of the information is out of date, it still is the best guidance for development or redevelopment sites with regards to Japanese knotweed.
 - Although most of the visible evidence of Japanese knotweed on site is limited to the outer boundaries it may affect the wider development as the rhizomes can extend much further than the above ground growth (see **4.6. Japanese knotweed Underground Rhizome Buffer Zone.**)
 - Knotweed Control has mapped a 3m rhizome buffer zone but refers to a 7m rhizome buffer zone in the Management Plan/ Method Statement to be extra cautious especially with some areas of knotweed being so well established.
 - Knotweed Control has not been given any details of the timing of the development as they are still unclear but has only been supplied with a floor plan of the main building so the Japanese knotweed Management Plan and Method Statement covers the control, biosecurity and monitoring measures for;
 - Pre development works
 - Vegetation clearance/ control
 - Tree works
 - Demolition and removal works
 - Waste disposal
- And to a lesser degree;
- Post development maintenance and management ground works
 - Use of the garden and outdoor space
- The timings and order of the Japanese knotweed Method Statement may change from this place due to the work schedules and this plan is assuming the knotweed works are to start straight away.
 - It must be noted however Japanese knotweed herbicide treatment is time critical and can only be undertaken at certain times with the optimum treatment taking place in late summer through to the autumn.

6. JAPANESE KNOTWEED METHOD STATEMENT

PRE DEVELOPMENT WORKS

1. Japanese knotweed does not respect ownership or legal boundaries so permission to access and control any Japanese knotweed not within the site boundaries will be required so as not to cause reinfection.

Please note:

⚠ *Where land owners cannot be located but all reasonable effort has been made to find and contact them, the owner of the subject property will be required to take responsibility and give written permission for treatment in the land owners absence before treatment can commence*

2. The site should ideally be **secured so that no material contaminated with Japanese knotweed** is brought onto site via fly tipping.
3. Again ideally, **an exclusion fence** around all known or visible areas of Japanese knotweed **with signage in a zone 7m** should be erected to prevent access and by site traffic and operatives to limit disturbance.

Please note

- ⚠ *Japanese knotweed is like an iceberg; only about 20% or so of the total biomass of the plant is visible above ground*
- ⚠ *The actual extent of Japanese knotweed on site will depend on many factors including the volume, maturity and length of time growing on site and substrate/growing medium which will also affect the success of the herbicide treatment.*
- ⚠ *7m is distance used by many organisations including surveyors and lenders as the “safe” distance from structures which is often over cautious.*
- ⚠ *Japanese knotweed and is required to be recorded and mapped 3m from visible growth in accordance with the Property Care Association’s [Code of Practice: Management of Japanese knotweed 2018](#)*

4. Where fencing may not be possible there should at least be signage and any works and vehicle movement or storage within 7m required approval/ supervision of a **Japanese knotweed Clerk of Works (JKCoW)** see point 5.
5. **A Japanese knotweed Clerk of Works (JKCoW)** should be appointed to approval, oversee and supervise any works and vehicle movement or storage within 7m on any visible above ground Japanese knotweed. This could be a member of the existing team who should be aware of the potential extent of the knotweed and who can identify Japanese knotweed in all states including winter and underground rhizomes (see pages x. **THE ENVIRONMENT AGENCY’S GUIDE TO JAPANESE KNOTWEED RHIZOME ID**) but also has the **authority to halt or improve works practice if concerned** about cross contamination or where there may be unapproved works near the knotweed.
6. There should be a **toolbox talk for all regular works** on site regarding **location of knotweed, legislation, the importance of biosecurity & good practice** with regard to Japanese knotweed who can intervene when they see back practise around the areas of Japanese knotweed or contact the **Japanese knotweed Clerk of Works (JKCoW)** to either halt or improve works practice as point 5.

VEGETATION CLEARANCE / CONTROL

7. It is this stage that fencing and signage is really important to prevent access and disturbance by site traffic and operatives especially as new contractors are brought onto site with no awareness.
8. Where vegetation is to be cleared/ controlled once again those areas that are **Japanese knotweed FREE should be removed first**, working towards the known areas with Japanese knotweed to reduce the likelihood of cross contamination or spreading viable propagules.
9. Where vegetation clearance/ control is to take place near the knotweed it should be done with **hand tools** and should take extra care should be taken – if knotweed canes are to be cut they **should be left in situ** to rot down as they are a controlled waste (see vi. **LEGISLATION**)
10. All tools, equipment and foot wear should be **thoroughly cleaned and inspected** by the **Japanese knotweed Clerk of Works before moving onto another area for clearance/ control** (to stop the spread around site) and **when moving off site** (to stop the spread off site as it an offence under the Environmental Protection Act 1990, see vi. **LEGISLATION**).
11. It must be noted that there **may be other areas of knotweed NOT MAPPED** either beneath the soil surface or just not visible for some other reason e.g. in dense vegetation therefore if during the clearance works if any other potential areas of Japanese knotweed are found, works should be halted and the **Japanese knotweed Clerk of Works** brought in to investigate.
12. If other areas of Japanese knotweed are found, they will have to have the similar procedures as above with the addition of the material being put back where it was and vehicles and machinery required to be pressure washed the in situ and inspected before being moved.
13. At this stage if my client chooses in some places that the **6.1.1. “Dig and dump” / excavation and landfill as per 6.1. JAPANESE KNOTWEED MANAGEMENT PLAN**, is required in some areas it could be done at this stage to remove contaminated soils and limited further potential spread.

TREE WORKS

14. Where trees require to be taken down, arborists should be made aware of the Japanese knotweed with their works overseen by the **Japanese knotweed Clerk of Works**.
15. They should work on trees in areas that are **knotweed FREE areas first** moving towards the trees in the known Japanese knotweed areas to reduce likelihood of spreading viable propagules.
16. When felling the trees or limbs are to be dropping in the knotweed area avoid disturbing the knotweed as much as possible in the 7m rhizome buffer zone around all visible above the ground knotweed.
17. When removing tree limbs once felled, careful extraction is required as not to pick up viable Japanese knotweed propagules and moving them around or off site especially on treads on vehicles and footwear
18. Careful **cleaning e.g. pressure washing and inspection** of any tools, treads on vehicles and footwear needs to be undertaken by the **Japanese knotweed Clerk of Works** to ensure no potential knotweed propagules are taken before leaving the location.

DEMOLITION AND REMOVAL WORKS

19. There is a high risk of cross contamination of potentially viable knotweed material during the demolition and removal due to the proximity of the knotweed to the structures – the building, foundations and car park and path areas including concrete and tarmac.
20. Work on again should start in areas that are **knotweed FREE areas first** moving towards the areas with Japanese knotweed so there is reduced likelihood of cross contamination or spreading viable propagules.
21. When demolishing structures or removing them from site, the knotweed should be disturbed as little as possible including the rhizome buffer zone 7m from the visible above the ground knotweed canes.
22. When removing materials and structures from site near the knotweed, careful extraction is required as not to pick up viable Japanese knotweed propagules and moving them around or off site especially on treads on vehicles and footwear or the structures or materials themselves.
23. Careful **cleaning e.g. pressure washing and inspection** of any treads on vehicles and footwear or the structures or materials needs to be undertaken by the **Japanese knotweed Clerk of Works** to ensure no potential knotweed propagules are taken before leaving the location.
24. Any vegetation, concrete, spoil, tarmac, soil etc. potentially contaminated with Japanese knotweed material is classed as a controlled waste (see (see **vi. LEGALSATION**) **so should be kept to a minimal and stored transported and disposed of appropriately** (see **WASTE DISPOSAL** point 25 below)

WASTE DISPOSAL

25. All Japanese knotweed and material potentially contaminated with knotweed propagules as small as 0.7gm, the size of a pea will be classed as a controlled waste (see. **vi. LEGALSATION**). It is therefore generally preferable to keep this waste on site **rather than take to a landfill** (see **7.1. “Dig & Dump”/ excavation & landfill**) with the associated extra costs and increased complexity in logistics.

POST DEVELOPMENT GROUNDS MAINTENANCE AND MANAGEMENT

26. Japanese knotweed is a long lived perennial, easily spread, unpredictable and notoriously hard to kill. Knotweed Control does not guarantee ERADICATION and the lack of above ground of regrowth does not mean the knotweed has all been killed. Japanese knotweed rhizome can remain dormant deep in the soil for over 20 years & can be broken by disturbance or a change in conditions.
27. If there are to be any ground works within 7m of any area of known Japanese knotweed it is essential that a Method Statement is created by the operator to show the steps being undertaken to limited the interfere with the management of the Japanese knotweed and all biosecurity steps and procedure put in place to stop or managed the spread across and off site.
28. Great care must be taken when undertaking general works on site that may disturb the knotweed rhizomes (e.g. vegetation or trees, paths ,track, or underground or ground work) and to ensure no viable material is spread around the site (e.g. on infected equipment, machinery, tools, footwear and material such as soil, plants etc.) It is therefore important there is fencing and/ or signage of the potential location of rhizome even when all visible sign of the knotweed has gone.


-
29. Careful **cleaning e.g. pressure washing and inspection** of any treads on vehicles and footwear or the structures or materials needs to be undertaken by the **Japanese knotweed Clerk of Works** to ensure no potential knotweed propagules are taken before leaving the location.
 30. Longer term monitoring is always required and even after the suggested timeframes it is likely a “mop-up” herbicide treatment may be required in the future.

USE OF THE GARDEN AND OUTDOOR SPACE

31. Again any activities that will potential interfere with or disturb the growth of the Japanese knotweed could stimulate the growth of and spread viable propagules
32. Also of the knotweed growth to be treated post development is damaged or compacted it could hindering the long term efficacy of any ongoing herbicide treatment as there needs to be as much surface area and growth on which to apply the herbicide and may take longer that it would otherwise.

7. JAPANESE KNOTWEED MANAGEMENT PLAN

- Japanese knotweed control comes with a few options available (see **iii. JAPANESE KNOTWEED CONTROL METHODS - INTERGREATED WEED MANAGEMENT (IWM)**)



- Each method has with its own pros and cons & **iv. PROS AND CONS OF JAPANESE KNOTWEED CONTROL METHODS**) but these are the options available to my client currently with details as follows.
- It may be that different locations of knotweed require different methods and may depend on the timing of the works.
- In this case it appears the only options available are as follows but it is up to my client to decide which is/ are the best;
 - 7.1. "Dig & dump" (excavation & landfill)**
 - 7.2. Herbicide treatment**
- There is no room for the following methods of control.
 - 7.3. The "Bund method" (excavation & herbicide treatment)**
 - 7.4. On site burial**

7.1. "Dig and dump" (excavation and landfill)

- The Environment Agency's [Managing Japanese knotweed on Development Sites: Code of Practice](#) states landfill should only be used if there is no viable alternative .
- 1. Ideally the Japanese knotweed would have at least 1 season of herbicide treatment to reduce the vigour of the plant and rhizome (see **7.2. Herbicide Treatment**)
- 2. The works to take place in this area
 - a. must be overseen by the **Japanese knotweed Clerk of Work**
 - b. A **dedicated track** lined with **an appropriate membrane** for the movement vehicles to minimise likelihood with to stop cross contamination
 - a. Any potentially soil contaminated with Japanese knotweed will need to be carefully excavated until there is no more visible rhizomes left in the soil.
 - b. Any removed spoil is classed controlled waste
 - c. This can be sieved / screened to remove knotweed material to reduce the volume going to landfill but the sieved material must still be treated as controlled waste.
 - d. An **extra bucket** of "clean" soil removed in case of extended rhizomes
 - c. All paper work including **transfer notes** must be in place to **show duty of care** at each stage
 - a. Transported by a licenced waste carrier in suitably covered
 - d. Needs to go to a **landfill site licenced to accept** Japanese knotweed and **tonnage agreed in advance**.
 - e. Vehicles, tools, footwear must be **thoroughly pressure washed and inspected** when leaving the development and landfill site before it can move off site

Please note:

- ⚠ *Under the Environmental Protection Act 1990 ALL Japanese knotweed material is classed as "controlled waste" however if the Japanese knotweed has been treated with certain pesticides the rhizomes and contaminated soil will be classed as a "hazardous waste" an different legislation comes into force under the 'Hazardous Waste Regulations 2005'.*
- ⚠ *Landfilling both "controlled" and "hazardous" waste are expensive and environmentally problematic and should only be undertaken if all other avenues have been explored.*
- ⚠ *When cleaning and inspecting vehicles and equipment all voids should all be checked with particular care is needed in the load space, tyre treads, wheel arches, digging buckets and caterpillar tracks where there are small moving parts are where any knotweed material could be trapped (it only takes 0.7gm the size of a pea of rhizome or crown material to create a new plant)*

3. Even after very careful and skilful excavation, very small pieces of viable rhizome may remain in the soil so a monitoring programme should be followed for several years with a herbicide treatment "mop up" annually of any regrowth (see **7.2. Herbicide Treatment**)
4. **Longer term monitoring is always required** as Japanese knotweed is a very long lived perennial and can be a highly unpredictable and notoriously hard to kill as well as remain dormant yet still viable in the soil for many years.

Please note:

- ⚠ *Japanese knotweed is a long lived perennial, is highly unpredictable and notoriously hard to kill*
- ⚠ *Knotweed Control does not guarantee ERADICATION and the lack of above ground of regrowth does not mean the knotweed has all been killed.*
- ⚠ *Japanese knotweed rhizome can remain dormant deep in the soil for over 20 years & can be broken by disturbance or a change in conditions*

7.2. Herbicide Treatment

1. **Permission for treatment, clearance & monitoring** must be gained by the subject property's owner from all land owners where control is to take place before any remediation works are undertaken and for duration of the agreed control plan. This permission is assumed at the start of treatment.
2. During the winter 2023, in knotweed's dormant period, any dense vegetation including bramble and old Japanese knotweed canes should be **cut down the and left in situ to rot**, carefully ensuring no viable material is spread or taken off site.

Please note:

- ⚠ *Clearance of old Japanese knotweed canes & other vegetation ensures any knotweed regrowth is not inhibited in the following spring making it bigger and healthier & more susceptible to treatment*
- ⚠ *It also makes it easier to access, and better herbicide coverage when spraying – all of which improving results of treatment*
- ⚠ *Winter clearance may only be required for the first few years depending on how the vegetation regrows.*
- ⚠ *Knotweed or contaminated material is classed as a “controlled” waste so has strict transportation, storage and disposal regulations so should be left to rot down or incinerated on site.*

3. During the 2023 growing season, it essential if there is any **Japanese knotweed, it must be left to grow with no disturbance or interference.**

Please note:

- ⚠ *The knotweed must be left to grow with no disturbance or interference so that it is as big and healthy as possible. The larger the leaves and stems the more surface area on which to apply the herbicide or stems to inject making the treatment more effective.*
- ⚠ *Also the timing of treatment is essential (see v. **JAPANESE KNOTWEED CONTROL METHODS OFFERED BY KNOTWEED CONTROL Treatment Timing**)*

4. Any Japanese knotweed growth will be;
 - a. treated using a professional aquatic approved glyphosate based herbicide
 - b. by an appropriate qualified operator
 - c. under licence by Natural Resources Wales to used herbicide need water and protected sites
 - d. by an appropriate qualified operator
 - e. at the optimum time of year - in this case from mid to late autumn, before leaves change colour or fall from the lands and before the early frosts
 - f. applied via foliar spray and/or stem injection depending on the size of the leaves and stems -foliar spray in this case as the growth is so small
 - g. in the correct conditions (not windy & no rain forecast for at least an hour after application
 - h. in accordance with the herbicide label, best practice guidance and relevant legislation
 - i. following appropriate health and safety and environmental protection procedures
5. The herbicide will start working within 24 hours and carry on working for **at least 6 weeks** so again it is essential it is **left undisturbed for the herbicide to continue to work.**
6. After each year's treatment the knotweed will regrow smaller so the treatment is to be **undertaken slightly later in the season in following years** and **most likely to be applied via foliar spray.**
7. For more information **see v. JAPANESE KNOTWEED CONTROL METHODS OFFERED BY KNOTWEED CONTROL.**

Please note:

- ⚠ *After every year's treatment regrowth will be smaller and more sporadic with smaller leaves and thinner stems. Stems may be too small to inject so will be applied via foliar spray*
- ⚠ *As there is less leaf surface area on which to apply herbicide (i.e. smaller leaves) it makes successive treatments less effective which is why it can take 3-8 years to control the knotweed*
- ⚠ *Also late season treatment is the most effective as it will draw the herbicide into deeper rhizomes than earlier treatment*
- ⚠ *Later season treatment also means the smothering annual weeds have died down exposing more of the knotweed*

8. Herbicide treatment and perhaps vegetation clearance as per steps 2. **Winter . will need to be repeated for at least 3 years several years** and points 3-7, the Herbicide Treatment may need to be undertaken for quite a few more years perhaps up to 8 in areas where it is mature and established or disturbed during the project.
9. **Longer term monitoring is always required** as Japanese knotweed is a very long lived perennial and can be a highly unpredictable and notoriously hard to kill as well as remain dormant yet still viable in the soil for many years.

Please note:

- ⚠ *Japanese knotweed is a long lived perennial, is highly unpredictable and notoriously hard to kill*
- ⚠ *Knotweed Control does not guarantee ERADICATION and the lack of above ground of regrowth does not mean the knotweed has all been killed.*
- ⚠ *Japanese knotweed rhizome can remain dormant deep in the soil for over 20 years & can be broken by disturbance or a change in conditions*

7.3. The "Bund method" (excavation & herbicide treatment)

- There is no room for this method of control on this particular site so it is not an option.

7.4. On site burial

- There is no room for this method of control on this particular site so it is not an option.

8. OTHER INVASIVE NON NATIVE SPECIES (INNS) ON SITE

- During the site visit Knotweed Control observed other Invasive Non Native Species on site not just Japanese knotweed including the following;
 - Cherry laurel (*Prunus Lusitanica*)
 - Buddleia (*Buddleja Davidii*)
 - Himalayan balsam (*Impatiens glandulifera*) –possibly
 - Himalayan honeysuckle (*Leycesteria formosa*)
 - Ash die back (*Hymenoscyphus fraxineus*) likely to be on the ash trees (*Fraxinus excelsior*)

APENNDICIES

- i. KNOTWEED CONTROL SWANSEA LIMITED DETAILS**
- ii. SITE HYGIENE – BIOSECURITY MEASURES**
- iii. JAPANESE KNOTWEED CONTROL METHODS - INTERGRATED WEED MANAGEMENT (IWM)**
- iv. THE PROS AND CONS OF CONTROL METHODS**
- v. JAPANESE KNOTWEED CONTROL METHODS OFFERED BY KNOTWEED CONTROL**
- vi. LEGISLATION**
- vii. CODES & MORE INFORMATION**
- viii. KNOTWEED CONTROL SWANSEA LIMITED'S TERMS & CONDITIONS**
- i. THE ENVIRONMENT AGNECY'S SUGGESTED WORDING FOR EXCLUSION FENCING**
- ii. THE ENVIRONMENT AGNECY'S GUIDE TO JAPANESE KNOTWEED RHIZOME ID**

i. KNOTWEED CONTROL SWANSEA LIMITED DETAILS

Company: Knotweed Control Swansea Limited
Company no: 9815953
Director: Joanne Mullett
Address: 20 Penfilia Road, Brynhyfryd, Swansea, SA5 9HX
Tel: 07790505232
E mail: knotweedcontrol@gmail.com
Website: www.knotweedcontrolwales.co.uk

Surveyor: Jo Mullett
Qualifications: [Property Care Association](#)
Qualified Technician (QTPCA) (2014)
Certified Surveyor of Control & Eradication of Japanese knotweed (CSJK) (2015)
[National Proficiency Test Council](#)
Safe Use in Pesticides PA1, PA6 (2011), PA6AW (2013) & PA6INJ (2016)
Credit & Qualifications Framework for Wales (CQFW)
[Swansea University Advanced Professional Training Bioscience](#)
Invasive Plants: Identification, Ecology and Control: (2013)
[City & County of Swansea](#)
Internal training for the Control of Substances Hazardous to Health (COSHH) (2014)
[Non-native Species Secretariat e-learning](#)
Module 1. Introduction to Invasive Non-native Species
[Module 2a. Introduction to Identification and Recording](#)
Module 2b. Identification of Invasive Freshwater Plants
Module 2c. Identification of Invasive Freshwater Invertebrates
Module 2d. Identification of Invasive Riparian Plants
Module 3. Biosecurity

Property Care Association: www.property-care.org

Knotweed Control is a member of the [Property Care Association \(2015\) Invasive Weed Control Group \(PCA IWCG\)](#) which enables consumers a means of identifying specialist contractors and consultants in the control and management of invasive species, offering the highest levels of technical knowledge and practical skill.

TrustMark: www.trustmark.org.uk

As a member of the Property Care Association Knotweed Control is be default part of the [TrustMark](#), a scheme licensed by Government and supported by consumer protection groups enabling clients to find local trustworthy, reliable **tradespeople** operating to Government Endorsed Standards.

Amenity Training Register: www.basis-reg.co.uk/Schemes/Amenity/About-Amenity-Register

The BASIS Amenity Training Register is a professional register demonstrating members have up-to-date training and knowledge to responsibly manage pesticide use in the amenity sector.

The Amenity Standard www.theamenitystandard.co.uk/

A bespoke voluntary quality management standard of he Amenity Forum and backed by the Government to which highlights the need to use professionally approved operators in public spaces and promotes best practice in areas including invasive weed control.

ii. SITE HYGIENE - BIOSECURITY MEASURES

- Good site hygiene - biosecurity measures is essential on sites with Japanese knotweed to minimise the risk spreading of Japanese knotweed around or illegally, off site.
- It only takes a viable piece of Japanese knotweed material 0.7gm, the size of a pea, to make a new plant which can quickly establish so great care is needed when handling contaminated material.
- All Japanese knotweed is classed as a “controlled” waste and has very specific legal regulations regarding transport, storage
- Knotweed Control cannot be held responsible for
 - any cross contamination from untreated local sources
 - cross contamination from material moved around site
 - or new source of Japanese knotweed brought into site

Japanese Knotweed Dos and Don'ts

DO

- ✓ ... Do get professional advice on as soon as possible
- ✓ ... Do ensure contractors are members of the [Property Care Association](#) or INNSA)
- ✓ ... Do check qualifications of operators (National Proficiency Tests Council Certificate of Competence)
- ✓ ... Do work with neighbouring land owners to deal with the Japanese knotweed
- ✓ ... Do make yourself aware of Japanese knotweed & the law
- ✓ ... Do take great care not to spread the knotweed around site especially crown & rhizome material!
- ✓ ... Do thoroughly clean tools, vehicles and machinery if used near Japanese knotweed.
- ✓ ... Do put up fencing and signs to keep out where Japanese knotweed is likely to be disturbed
- ✓ ... Do take care not to read too on the internet – there are so many recycled myths!

DON'T

- ✗ ... Don't panic!
- ✗ ... Don't spread Japanese knotweed by digging, mowing, flailing, cutting, chopping or chipping etc.
- ✗ ... Don't cut down live knotweed – it needs to be big & healthy for the herbicide treatment to be effective
- ✗ ... Don't put knotweed material in council black bag, green waste or take to Civic Amenity Sites
- ✗ ... Don't put it in your compost bin – you won't to kill it this way and you could spread it in the garden.
- ✗ ... Don't allow Japanese knotweed to spread into the wild or neighbouring land
- ✗ ... Don't break the law so find out about your responsibilities
- ✗ ... Don't ignore Japanese knotweed – the problem won't go away on its own & will only get worse!

iii. JAPANESE KNOTWEED CONTROL METHODS - Integrated Weed Management (IWM)

- Integrated Weed Management (IWM) is the use of a combination of preventive, cultural, mechanical (physical), chemical (herbicide) or biological practices in order to control weed, invasive non-native or problematic plants including Japanese knotweed.
- There are several different recognised methods of dealing with Japanese knotweed (see the Property Care Association's [Code of Practice: Management of Japanese knotweed 2018](#))
- Each have their own advantages and disadvantages (see **iv. PROS AND CONS OF JAPANESE KNOTWEED CONTROL METHODS**) and the method chosen depends on a number of factors on site and in relation to the client's requirements and may change with circumstances
- The 4 general methods fall into different types;
 - a. **Physical or mechanical** (including digging/ excavation/ landfill "dig & dump"/ on site burial/ screening/ membranes/ rhizome fragmentation/ cultivation)
 - b. **Chemical or herbicide** control
 - c. **A combination of control** (including "**Bund method**" **excavation & herbicide treatment**)
 - d. **Biological/ biological agent/ bio-control** - currently unavailable as at the research phase
- Each control method for Japanese knotweed is chosen appropriate to the site, the time frames and money available and each have their own advantages and disadvantages (see **iv. PROS AND CONS OF CONTROL METHODS**) but all require great care but there should always monitoring of the site following control due to the highly invasive and persistent nature of Japanese knotweed.
- It is not uncommon for Japanese knotweed to respond to inconsistency/ incorrect/ incomplete herbicide treatment, control or disturbance in unpredictable way making subsequent treatment more complicated, prolonged and expensive.
- Control options currently include;
 - **Herbicide treatment:** applying herbicide to Japanese Knotweed in situ. See **v. JAPANESE KNOTWEED CONTROL METHODS OFFERED BY KNOTWEED CONTROL**
 - "**Dig & dump**" (**excavation & landfill**): exaction of Japanese knotweed material and removal to a landfill. At least 1 season of herbicide treatment is recommended before excavation and some herbicide treatment may be required to "mop up" any small remains.
 - The "**Bund method**" (**excavation & herbicide treatment**): excavation and movement of Japanese Knotweed material to an area of the site where it will not be disturbed. Creation of a bund and subsequent treatment with herbicide.
 - **Screening/ sifting:** excavation of Japanese Knotweed material and screening (sieving) the material through a mesh or other selective system to remove rhizome fragments, which are then disposed of correctly and safely. The soil that passed through the screener will still be classed as controlled waste and may be used on site but must be located where it will not be disturbed. This soil will then need to be monitored for at least two growing seasons and any regrowth treated with herbicide as per the stockpiling treatment above, or dug out (usually manually), before control can be considered complete.

-
- **Rhizome fragmentation and cultivation:** digging and breaking up rhizome material and soil with the aim of increasing the leaf surface area to rhizome volume ratio and to un-compact, disturb and aerate the soil. Crown removal can be integrated into such works, including prior to the commencement of herbicide treatment. The subsequent Japanese Knotweed growth is then treated with herbicide.
 - **On site burial:** excavation of Japanese Knotweed material with burial at another part of the site at an appropriate depth to prevent regrowth. Monitoring of the area will still be required and any regrowth treated with herbicide.
 - **Root barrier membrane:** prevention of horizontal and vertical growth of Japanese Knotweed by installing a vertical and/or horizontal membrane barrier. Monitoring of the area will still be required for at least two growing seasons and any regrowth treated with herbicide.
 - **Removal to landfill:** excavation and transport of Japanese Knotweed material to a licensed landfill using haulage vehicles. Monitoring of the area will still be required and, although all rhizome material should have been removed, any regrowth treated with herbicide.
 - **Biological control:** There are currently no approved methods for the biological control of Japanese Knotweed. Trials are being conducted by CABI for several biocontrol agents.

iv. PROS AND CONS OF CONTROL METHODS

- The following table has been taken from the Property Care Association [Code of Practice Management of Japanese Knotweed](#) and shows a comprehensive list of the pros and cons of different control methods.

Herbicide treatment	
Pros	Cons
• Cost effective • Treatment can be carried out in situ without risk of spreading the plant further. • Quickly reduces the capacity of the plant to spread on/off site. • Quickly eliminates the capacity of the plant to impact built structures. • Easy to administer	• Can take many years to achieve acceptable results, especially where stands are mature. • Management plans that rely solely on herbicide treatment must include at least 2 years of monitoring after all evidence of growth has ceased. • Herbicide treatment alone should not be recommended on sites with future development plans that involve the soil being dug and disturbed. • Construction works cannot continue in areas still containing the plant and the risks associated with landscaping treated soils, e.g. stimulating regrowth, should be made clear to the client and mitigated for. • The use of some herbicides is restricted near waterbodies and desired vegetation. • Some herbicides can persist in the soil. • If soil is disturbed at a later date, regrowth can occur. • Effective control requires expert knowledge of herbicide treatment of Japanese Knotweed. • Soil which contains Japanese Knotweed that has been treated with herbicide is still classed as controlled waste if it enters the waste stream. • Herbicide treatment can induce temporary dormancy.

Stockpiling	
Pros	Cons
• Cost effective • Site work can be undertaken while treatment takes place elsewhere on-site.	• Requires an area that can be left undisturbed for several years. • Soil from a stockpile must remain on the site. • The same cons as herbicide treatment apply in the stockpile area. • Plant material can be accidentally spread e.g. after a change in ownership. • The depth of the stockpiled soil must be appropriate for the future use of the soil. • Rhizome buried deeper in a bund is less likely to express itself and may become dormant; as such, bunds should be created as shallow as is practical and should not exceed 0.5m. • If larger bunds are created, it may be necessary to apply for planning permission.
Screening	
Pros	Cons
• Can be cost effective but not always. • Less material needs to be disposed of to waste facility. • The treated soil can be re-introduced on site as fill or in soft landscaping areas. •	• Where soil needs to be imported, less is required from elsewhere to fill voids created by excavation. • All screened soil is still classed as controlled waste • Small fragments of Japanese Knotweed will still be present in the soil and could lead to re-infestation. • Area where screened soils are re-used must be monitored for regrowth. • Follow up herbicide treatment or manual removal may be required. • Plant material can be accidentally spread during movement. • Soil type and makeup dictate if it can be screened or not. • Rhizome fragmentation and cultivation, including crown removal
Rhizome fragmentation and cultivation, including crown removal	
Pros	Cons
• Increases the leaf surface area to rhizome volume ratio • Breaks up and aerates the soil. • Can increase the effectiveness of herbicides under certain scenarios. • Can improve the potential for eradication on sites where the Japanese Knotweed is persistent. • Crown removal removes a large amount of surface and underground biomass.	• Most above ground vegetation must be cleared, even desirable plants. • Cleared vegetation would usually need to be disposed of. • A large area must be dug to ensure all rhizome containing soil has been included. • Rhizome located deeper in the soil may be missed and result in regrowth. • Soil should be compacted at the end of the treatment to help reduce the potential of deep soil rhizome regrowth. • Crown removal can be time consuming or impractical for large infestations and removed crown must be managed appropriately

Burial	
Pros	Cons
- Does not require a set-a-side area for control. - Work can continue immediately after burial. - Quickly removes the Japanese Knotweed from an undesirable area	- Restrictions remain on the site, e.g. in some areas deep excavation would interfere with buried material. - The use of the area above burial site is limited. - Typically requires a large hole to receive material, so it may not be possible if soil is shallow or water table is high. - The appropriate environment agency must be notified. - Plant material can be accidentally spread during movement.
Root barrier	
Pros	Cons
- Can be installed to reduce the chance of horizontal and vertical rhizome spread. - Can be used to protect structures, hard surfaces and services. - Work can continue immediately after installation in areas protected by membranes.	- Tears in the membrane or poorly sealed seams between sheets can be exploited by growing rhizome. - Can only be installed in favourable weather conditions. - Damp and/or wet conditions and/or work surfaces will reduce the robustness of heat welded seals. - Surface drainage and underground water can affect installation and ponding can occur, all of which must be taken into consideration. - Installation of root barrier is a form of control/prevention to be used in conjunction with other methodology, as it is not in itself a method of eradication.
Landfill	
Pros	Cons
- Quickly removes the Japanese Knotweed from an undesirable area - No restrictions left onsite. - Work can continue immediately after removal. - Fast and efficient	- Relatively expensive - Disposal to landfill reduces valuable landfill capacity and needs haulage (which damages the environment and increases the risk of Japanese Knotweed spreading) and in the long term unsustainable. As such, disposal to landfill should only be considered as last resort when Japanese - Knotweed cannot be classed as a controlled waste with specific storage , transportation and disposal regulations and controls
Biological control	
Pro	Con
Targeted control of a specific species after extensive lab and field tests	- Not currently commercially available as still in the research phase - Does not kill Japanese knotweed outright but another control method to hinder growth

v. JAPANESE KNOTWEED CONTROL METHODS OFFERED BY KNOTWEED CONTROL

GLYPHOSATE BASED HERBICIDE CONTROL

- Generally acknowledged as the cheapest & often the best front-line tool for Japanese knotweed control for residential situations Knotweed Control Swansea Limited only offers in-situ glyphosate-based herbicide/ clearance/ monitoring programmes
- A professional glyphosate-based, aquatic approved herbicide applied following best practice (see [Optimising physiochemical control of Japanese knotweed](#)) via stem injection and/ or foliar spray.
- Control using glyphosate typically takes 3 - 8 years & the success of any treatment is determined by a number of factors some of which are not easy to know or predict even from the site visits as detailed later.
- Tall, strong and healthy knotweed is more susceptible to herbicide treatment so it must be left to grow with no undisturbed with no inference before application (i.e. no mowing, cutting, strimming, herbicide treatment, compaction of soil, covering, tramping, grazing, digging/ excavation or covering with membrane/ mulch/ decking etc.) as it could negatively affect the ongoing treatment and invalidate guarantees and insurance.
- Glyphosate starts working within 24 hours, shows signs of response within 7 days (leaves browning & dropping) and continues to work for over 6 weeks.
- Glyphosate applied to the stems or leaves is translocated to the growing cells of plant (meristem) interfering with protein production, stopping cell division and causing the plant, over time, to starve.
- After each year's treatment, the size of the Japanese knotweed will reduce so in following years there are less leaves and surface area on which the herbicide can be absorbed therefore the response becomes affective less and dramatic, one reason why treatment takes so long.

Please note:

- ⚠ *Knotweed Control cannot be held responsible for any growth or cross-contamination from untreated local sources, cross-contamination across site or new material brought onto site, therefore, good site hygiene (biosecurity) is essential to prevent reinfection and spread. If good site hygiene practices are not followed it could invalidate the guarantees*
- ⚠ *Under the Control of Pesticides Regulations 1986 a [Simple or Higher Risk Agreement for the use of Herbicide near water or a designated site](#) may be required from Natural Resources Wales.*
- ⚠ *Aquatic approved herbicides only must be used near water courses by qualified operators.*

Glyphosate application


- Stem injection is very effective, highly targeted method but stems need to be at least 8mm in diameter.
- Foliar spray is used on stems less than 8mm in diameter and must be applied when it is not windy and there is no rain for a least an hour after treatment and great care is needed to protect pollinating insects.
- Treatment should be repeated until there is no evidence of regrowth.

People Pets & Animals

- As per product label; *"People, pets and wildlife need not be kept out of treated areas. It is best not to walk in areas where the spray is still wet as transfer to other vegetation may lead to unwanted damage to other foliage. Once the spray is dry this cannot occur. Keep stock out of treated areas for 5 days. Treated poisonous plant species [e.g. ragwort] must be removed before regrazing or conserving"*
- Japanese knotweed is NOT a poisonous plant therefore does not require to be removed after treatment.

Treatment Timing

- Treatment can take place once the knotweed is large enough, green and actively growing, before the knotweed dies back in the autumn or is damaged by early frosts.
- Optimum treatment time is mid-summer to late autumn as described below.

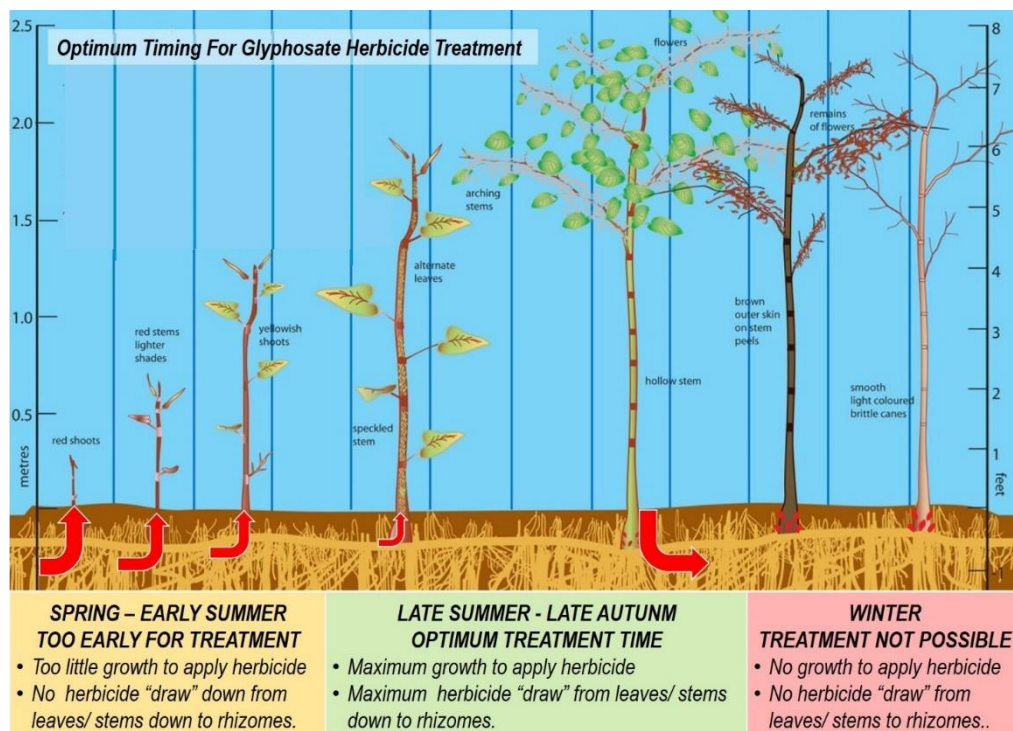

Original graphic
courtesy of Cornwall
Knotweed Forum

Factors Affecting Herbicide Treatment

- Factors affecting treatment efficacy include
 - The length of time an area has been infected (density, health and size of knotweed)
 - Previous control (e.g. herbicide use, digging, cutting, mowing)
 - Time of year treatment takes place
 - Herbicide application method and dosage
 - Re or cross-contamination from existing or new sources
 - Other environmental conditions (e.g. drought, flood, humidity soil type, fertility, plant stress)
 - Incorrect, incomplete or inconsistency control (see **Incorrect Control** below)

Incorrect Control

- Japanese knotweed is unpredictable and can respond to incorrect, incomplete or inconsistent control in several ways, making subsequent treatment more complicated, prolonged and expensive therefore trying to tackle the problem yourself can make the situation worse
- This can include mowing, cutting, strimming, herbicide treatment, compaction of soil, covering, tramping, grazing, digging/ excavation or covering with membrane/ mulch/ decking etc.
- There should be no disturbance or deviation from the Japanese knotweed Management Plan as this can negatively affect the ongoing treatment and invalidate guarantees and insurance.

Response to Incorrect Control

- The response of the knotweed to incorrect control includes;
 - Increased rate of spread and or growth
 - Deformation of subsequent years' growth called sub lethal bonsai growth
 - Enforced dormancy of which has been documented for up to 20 years
- Antagonistic effect of previous to subsequent treatments reducing the overall effectiveness

CLEARANCE & CONTROLLED RHIZOME FRAGMENTATION/ CULTIVATION

- Clearance of old Japanese knotweed canes & other vegetation may be needed especially in the winter to improve access, allow the knotweed to grow impeded and enable better access and herbicide coverage when spraying.
- Knotweed or contaminated material is classed as a “controlled” waste so has strict transportation, storage and disposal regulations so should be left to rot down or incinerated on site.
- After each year’s treatment, the size of the Japanese knotweed will reduce so in following years there are less leaves and surface area on which the herbicide can be absorbed therefore the response becomes affective less and dramatic, one reason why treatment takes so long.
- Controlled rhizome fragmentation/ cultivation at this point of done correctly can stimulate dormant growth and is then treated with herbicide the following season and may be deemed as suitable.

Please note: Clearance

 Great care is needed not to spread any of the viable knotweed material around or off site so good biosecurity measures will be followed.

 All Japanese knotweed material is classed as “controlled waste” has strict transportation, storage and disposal regulations so should be left to rot down or incinerated on site.

MONITORING

- Although 2 years is usually sufficient to determine if regrowth will take place, is not a guarantee the knotweed has been eradicated.
- If soil is disturbed after this period regrowth can occur due to exposing deeper rhizome that might be dormant and has been recorded as long as 20 years, after treatment appears to have been complete.
- The Property Care Association’s [Code of Practice; Management of Japanese knotweed 2018](#) states;
“The final monitoring visit is the visit carried out after the completion of control action and after which there has been at least two full growing seasons with no evidence of Japanese Knotweed growth. In this context, growing season refers to the entire active growth period in a given year. Although two full growing seasons are usually sufficient to determine if regrowth will take place, if soil is disturbed after this period regrowth can sometimes occur due to exposing deeper rhizome that might be dormant.”

vi. LEGISLATION

Professional advice should always be sought regarding the legalities of Japanese knotweed as it is a complex and new area of law, the following points can be used for basic guidance. Although not illegal to have Japanese knotweed on your land:

- **Private nuisance** Japanese knotweed could be deemed as a private nuisance where Japanese knotweed causes someone unreasonable interference with the enjoyment or use of their land
- **Wildlife & Countryside Act 1981**; it is an offense to plant or otherwise allow Japanese knotweed & other plants on Schedule 9 list to spread in the wild. DEFRA define 'the wild' as *"The diverse range of natural and semi-natural habitats and their associated wild native flora and fauna in the rural and urban environments in general. This can also be broadly described as the general open environment."*
- **Environmental Protection Act 1990**; Japanese knotweed & contaminated material is "controlled waste" requiring specific disposal regulations.
- **Hazardous Waste Regulations 2005** if certain herbicides have been used it could be classes as a "hazardous waste" requiring specific disposal regulation.
- **Duty of Care Regulations 1991**: Both controlled and hazardous wastes have specific paperwork requirements for handling, transportation and disposal.
- Under the **Town & Country Planning Act 1990**; Planning conditions to treat Japanese knotweed can be enforced so developers have to treat Japanese knotweed
- **Misrepresentation Act 1965**; If a vendor lies or omits information about a property being "affected" by Japanese knotweed on the TA6 Property Information Form (since 2013) they could be in breach of the.
- Professional negligence; Surveyors have a duty to record the presence of Japanese knotweed otherwise a claim could be made for
- Consumer Protection Regulations; Estate Agents also have an obligation to disclose the presence of Japanese knotweed as a "material fact" through the
- **Anti-Social Behaviour Crime and Policing Act 2014**: knotweed is not specifically mentioned but community protection notices can be used against individuals who are acting unreasonably and who persistently or continually act in a way that has a detrimental effect on the quality of life of those in the locality.
- **Regulation (1143/2014) on Invasive Alien Species (IAS)**; Surprisingly Japanese knotweed is NOT listed a species of Union concern by the European Commission on their or any of the updated lists.
- **Infrastructure Act 2015**, Welsh Ministers and Natural Resources Wales (others in other UK counties) are able to arrange 'Species Control Agreements' & serve 'Orders' on land owners who allow non-native invasive species to establish on their land.

vii. CODES & MORE INFORMATION

Knotweed Control operates in compliance with all current legislation and best practise guidance in the treatment of Japanese knotweed and other invasive non-native species including:

- Property Care Association's [Code of Practice for the Management of Japanese knotweed 2012](#)
- Property Care Association's [Code of Practice; Management of Japanese knotweed 2018](#)
- Royal Institution of Chartered Surveyors (RICS) [Professional standard for Japanese knotweed 2022](#)
- Royal Institution of Chartered Surveyors (RICS) [information paper on Japanese knotweed 2012](#)
- Royal Institution of Chartered Surveyors (RICS) [information paper amendment 2015](#).
- Environment Agency [Managing Japanese knotweed on Development Sites: Code of Practice 2013](#)
- The Invasive Non-Native Specialists Association (INNSA) [Technical Standards](#)
- Swansea University research paper [Optimising physiochemical control of Japanese knotweed 2018](#)
- Fennell, Wade, Bacon; [Japanese knotweed: An analysis of capacity to cause structural damage 2018](#)

For the safe and responsible use, storage and transportation of pesticides Knotweed Control follows:

- DEFRA's [Code of Practice for Using Plant Protection Products 2008](#)
- Crop Protection Association [Amenity Best Practice: Using Pesticides in the Community 2013](#)

More Information

- UK Government www.gov.uk/guidance/prevent-the-spread-of-harmful-invasive-and-non-native-plants
- **Non-native Species Secretariat** www.nonnativespecies.org/
- Devon County Council www.devon.gov.uk/japanese_knotweed
- House of Commons, Science and Technology Committee [Japanese knotweed and the built environment Seventeenth Report of Session 2017–19](#)

viii. KNOTWEED CONTROL'S TERMS & CONDITIONS

1. INTRODUCTION

- These Terms & Conditions (T&C) form the agreement between Knotweed Control Swansea Limited (Knotweed Control) and the client(s) & may be amended within reason any time.

2. COPY RIGHT

- Materials created by Knotweed Control including reports, document formats, diagrams, photos etc. created by Knotweed Control
 - Remain the property of Knotweed Control,
 - Are subject to copyright
 - Cannot be share of reproduced unless by written agreement in advance
 - May only be used for the purpose they were originally intended unless with prior agreement

3. SITE VISITS & REPORTS

- Knotweed Control will undertake visual, non-intrusive inspection from safely accessible areas both inside and where possible, outside the subject property boundaries.
- Information for reports will be based on data collected during site visits and where if suitable, client(s), neighbours, verified biological records as well as other resources such as on line maps/ records & photos.
- Even if there is no obvious Japanese knotweed seen during a visit, does not guarantee there is no Japanese knotweed on site.
- Material could have been unintentionally or deliberately concealed, removed or treated with herbicide but there still could still be dormant or viable rhizome underground, hidden behind walls, hedges or fences or in dense vegetation.
- When Japanese knotweed dies down in the winter with little or no visible signs from winter through spring or sometime event into late summer.

4. BOUNDARIES, PERMISSIONS & ACCESS

- Knotweed Control cannot be held responsible for omissions of land where boundaries plans have not been made available or incorrect or misleading information given.
- The herbicide treatment, clearance & monitoring phase can commence once:
 - Permission is gained from my client from all land owners here the Japanese knotweed is to be controlled.
 - My client(s) is/ are responsible for gaining permission from other land owners where knotweed is to be treated and this will be assumed at the start of any works
 - Conditions are safe and appropriate for the works
- Where landowners cannot be located, the client(s) will be required to give written permission for treatment in the owner's absence.
- The client(s) will need to arrange access with tenants or occupiers etc.

5. ESTIMATES

- Estimates remain valid for the season in which they are given.
- Estimates are an indication of costs but might need to revised for changes such as if;
 - There have been any changes undertaken on site since Knotweed Control's visit,
 - The extent of the Japanese knotweed has been e.g. hidden, treated with herbicide or cleared or
 - The visit has been undertaken during the winter through to spring when it can be hard to estimate the full extent of the knotweed.
- If Knotweed Control deems conditions too dangerous it reserves the right to cancel works, cease operations or charge extra to cover additional risk and/ or costs to make the site safe.

6. PAYMENT & REFUNDS

- Invoices can be paid with cash, cheque or through BACS and are deemed to have been received once funds have been cleared.
- Receipts are available on request as record of payment.
- Some works will be invoiced and must be paid up front and in full before works are undertaken such as guarantee packages when a property is being sold.
- Other works will be invoiced after works have taken place such as site visits, Japanese knotweed Management Plan Reports or annual treatment or which must be paid within 14 days unless stated as different on the invoice or agreed in writing
- Where there are late or non-payments;
 - An administration fee & interest will be charged
 - Legal action will be taken to recover costs
 - Upfront payment for future works may be required or works refused altogether
 - No refunds will be made of payments to date
 - Guarantees will be invalidated.
- Where the Japanese knotweed treated area covers ground with multiple owners land and cost have been agreed to be shared, it is up to my client(s) to pay Knotweed Control's invoice and they must recover costs from other land owners themselves. Invoices will not be split.
- No refunds will be made where Guarantees Packages have been paid for but no longer required.
- Guarantee Packages payment be placed in an escrow Transact account, a third party holding account where the full contact cost of the works is paid up front and Knotweed Control will drawing down money annually after works have been undertaken. Extra fees to cover admin and annual draw down fees.

7. SITE HYGIENE – BIOSECURITY

- Knotweed Control cannot be held responsible for any growth untreated local sources or cross contamination from new contaminated material brought onto site therefore good site hygiene (biosecurity measures) is essential to prevent reinfection and spread.

8. CANCELLATION OF SERVICES

- If the client(s) wishes to cancel services outstanding invoices will be sent and any out of pocket expenses from Knotweed Control will be charged.
- Knotweed Control retains the right to cancel works if the site is deemed unsafe or where invoices unpaid.

9. COMPLAINTS

- Knotweed Control strives to deliver a service that meets client(s)'s satisfaction but the event of a complaint Knotweed Control will work with the client(s) to come to a mutually suitable solution.
- When a problem cannot be resolved between the client(s) and Knotweed Control an independent person or persons from the Property Care Association Invasive Weed Control Group can be asked to inspect services.
- Any costs incurred through this process will be payable by the client(s).

10. GUARANTEE PACKAGES


- Knotweed Control offers Guarantee Packages which combine **Knotweed Control's Guarantee** and an **Insurance Backed Guarantee (IBG)**
- Site visits & Japanese knotweed Management Plan (JKMP). (JKMP) required for Guarantee Package as creates the word of the works on which the guarantee is based.
- Insurance Backed Guarantee (IBG) policy costs are per property and includes Insurance Premium Tax
- Where Insurance Backed Guarantee (IBG) is required and **others have undertaken treatment, there may be additional costs** due to the extra time required and risk involved (you wouldn't expect a roofer to guarantee someone else's work!)

- The **Knotweed Control's Guarantee** is an guarantee to treat any Japanese knotweed regrowth in the treatment area during the suggested guarantee phase as per the Japanese knotweed Management Plan (JKMP)
- The **Insurance Backed Guarantee (IBG)** is a policy taken out through an third party insurance company to ensure that in the unlikely event Knotweed Control ceases to trade, works will be honoured by another contractor arranged through the insurance company.
- Guarantee packages will;
 - Include a herbicide treatment, clearance and monitoring, details of which are stated in the Japanese knotweed Management Plan (JKMP)
 - **Knotweed Control's Guarantee** then starts after the suggested treatment period
 - After **2 growing seasons with no Japanese knotweed regrowth** a “**completion certificate**” will be issued by Knotweed Control and the **Insurance Backed Guarantee (IBG)** then commences.
- Guarantee packages remain valid as long as
 - There is **no interference in the treatment area** (i.e. no mowing, cutting, strimming, herbicide treatment, compaction of soil, covering, tramping, grazing, digging/ excavation or covering with membrane/ mulch/ decking etc.) Light, hand weeding is permitted.
 - There is **no deviation** from the Japanese knotweed Management Plan by anyone other than Knotweed Control (unless agreed in advance in writing)
 - Knotweed Control may change the detail of the Japanese knotweed in keeping with research, good practice and legation or depending on how the Japanese knotweed responds to treatment
 - Permission Agreement(s) are in place **from all landowners in the treatment area** & for the time frame required and it is the **client's responsivity to gain permission** from land owners before works commence. This is **assumed at the start of the works**
 - There are no permissions revoked during the treatment monitoring and guarantee phase by any other land owners where treatment is to be undertaken a in the Japanese knotweed Management Plan.
 - All invoices are **paid upfront and in full** (unless agreed in advance and in writing)
 - Knotweed Control is informed of any regrowth in the treatment area **as soon as it appears and must be within 3 months of the growth.**
 - Japanese knotweed Management Plans (JKMP) & Guarantee Packages are specific to each individual property although the works themselves may affect other properties.
 - Knotweed Control Swansea Limited's Terms & Conditions apply to Knotweed Control's Guarantee
 - Guarantee Protection Insurance Ltd (GPI)'s Term & Conditions apply to the Insurance Backed Guarantees
 - Guarantee Packages can be transferred to the new property owners as long as Knotweed Control has been given **written notice with the new owner's contact details within 3 months of the sale** (name, address, email and phone number) in order to be able to honour any on-going works. There will be administration costs associated with updating guarantee details by the insurance company but not normally by Knotweed Control Swansea Limited
 - No refunds or legal claims can be made against Knotweed Control Swansea Limited if the points above are not followed and will void Guarantee Packages.



Restricted Access

**The soil in this area
contains Japanese knotweed
and is being treated.
Do not enter unless authorised.
Do not remove soil from this
area without authorisation.**

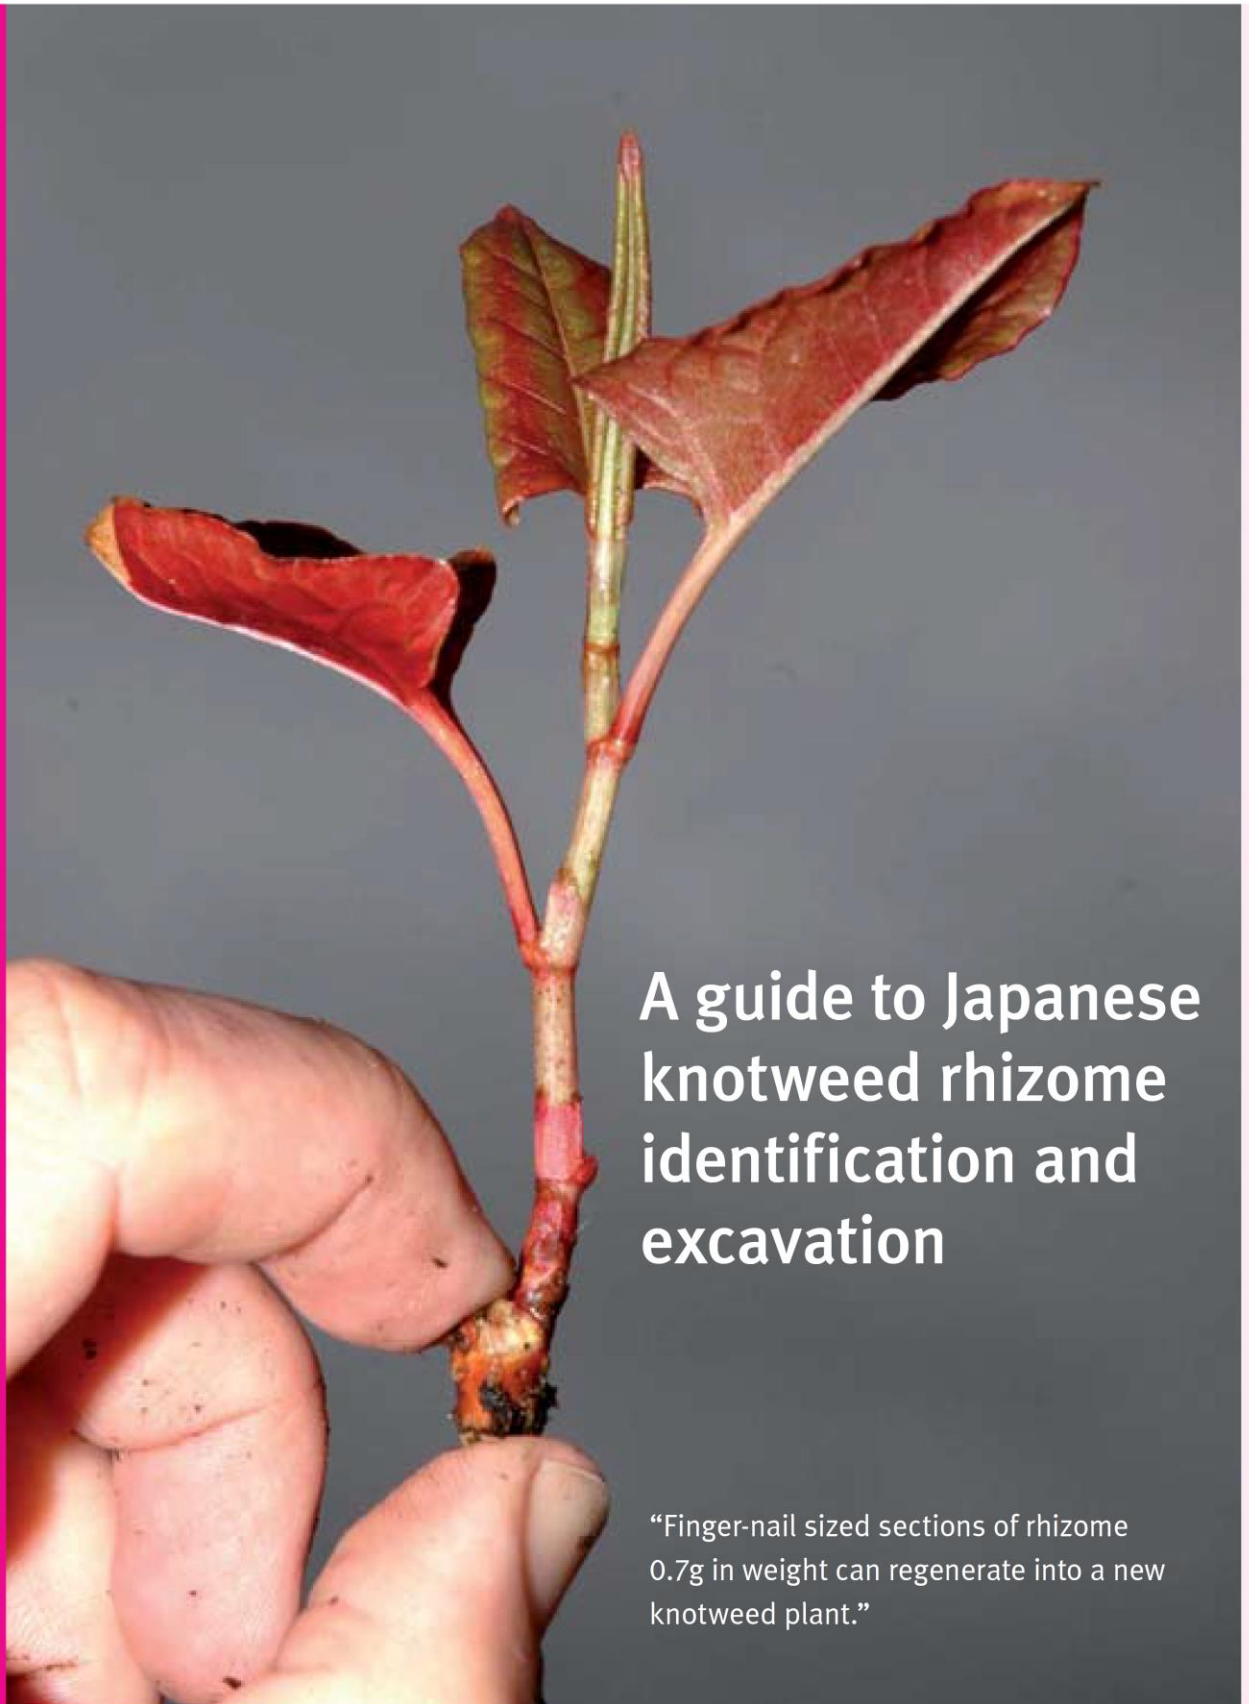

A guide to Japanese knotweed rhizome identification and excavation

“Finger-nail sized sections of rhizome 0.7g in weight can regenerate into a new knotweed plant.”

In addition to the rhizome described within the identification chart, very new rhizome growth, delicate and white in appearance, can be found during the growing season.

v) How do I remove rhizome?

Put simply, remove the rhizome with extreme care. It is important to read the code of practice before starting excavation. The majority of knotweed rhizome is confined to the top 0.5m of soil. Remove the soil by first scraping off the crowns and surface rhizome and putting to one side. Crowns and rhizome can be dried and burned (see Section 5.2 of Code) prior to treatment with the remaining soil. Crown material in particular is resistant to burning; therefore it is important to regard this material as still potentially infectious.

The next 0.5-1m of soil can then be removed and put aside, and then the remaining soil to a depth of approximately 3m can be excavated. This material should form the base of a bund (See Section 5.5 of Code), or the top layer of buried material (See Sections 5.4 and 4.1 of Code). This process of excavation can be proportioned to any depth of excavation, rather than adopting the 3m generalised depth.

Guidance on the containment and movement of knotweed-infested soil is provided within Sections 2, 6 and 7 of the Code of Practice.

Careful use of the information within this guide should enable operators to effectively inspect the edge of their excavation for remaining rhizome. Depending on the history of the site, the depth to which knotweed rhizome extends can vary between 0.5m – 10m. The history of the infestation, soil type and the water table can all have a profound impact on the extent of rhizome. Situations in which rhizome is greater than 3m tends to be associated with situations in which additional waste has been regularly dumped on an established knotweed stand, or wind-blown sand has created a dune system.

Careful excavation of rhizome has the potential to significantly reduce the volume of waste removed instead of simply excavating a 7m x 3m volume of soil. It also ensures effective removal in situations where a 7m x 3m excavation is an under-estimate. In all cases the precautionary approach must be adopted rather than risk leaving rhizome behind.



A guide to Japanese knotweed rhizome identification and excavation



This guide should be used in conjunction with the Environment Agency code of practice, 'managing Japanese knotweed on development sites'. It has been produced as a separate guide to facilitate use during excavations.

i) What is Japanese knotweed?

Japanese knotweed *Fallopia japonica* was introduced into the UK during the mid-nineteenth century as an ornamental plant. It has since become one of the most problematic invasive weeds in Europe (see Section 1 of Code)

Japanese knotweed is a perennial weed, producing tall canes, up to 3m (10 feet) in height during the summer. The canes have characteristic purple flecks, and produce branches from nodes along its length. These branches support shovel-shaped leaves and clusters of white flowers in autumn. The canes die off in winter, turning brown and shedding their leaves. This produces dense mulch that precludes the growth of native plants.



ii) What is Japanese knotweed rhizome?

Japanese knotweed canes grow from dense crowns that also produce extensive underground stems, called rhizomes. These rhizomes also produce fine, white, hair-like roots. It is hard to state with certainty the likely extent of rhizome spread from the parent plant. Research has shown that rhizome can grow a distance of at least 7m (23 feet) and achieve a depth of at least 2m (6 feet) from the parent crown. However, the actual extent of the rhizome can vary considerably depending on the soil type and the history of the site. Many knotweed infestations start life as a result of fly-tipped waste, and repeated applications of waste on top of the initial infestation can result in a deep matrix of rhizome.



iii) Why is it important to be able to identify Japanese knotweed rhizome?

Whilst knotweed can regenerate from small sections of cane, most knotweed in the UK arises from rhizome and crown material. Finger-nail sized sections of rhizome 0.7 g in weight can regenerate into a new knotweed plant. It appears that the regenerative potential of rhizome varies. Thick, old woody tissue appears to be less able to produce new growth than crown material or thinner succulent rhizome. This has implications for those excavating knotweed rhizomes, where there is a risk of thin terminal rhizome from the edge of the cut being overlooked, which would have a high regenerative potential.

There are often situations in which it is necessary to be able to identify rhizome without the benefit of intact knotweed canes for assistance. If a site is undisturbed it is fairly easy to recognise characteristic summer growth, or the dead winter canes. If the site has already been scraped, it is necessary to inspect the waste material for evidence of knotweed; dead canes, leaves and rhizome, to establish if the weed is present on site. Knowledge of rhizome identification is then required to identify the location and extent of the infestation.

The cost of knotweed management can be significantly reduced if knotweed and non-knotweed waste streams can be kept separate. If poor initial management of a site has already precluded this option, this should be of great concern to any subsequent developer.

Waste hauliers also need to take care to inspect waste material prior to accepting it (See Section 6.2 of Code). Soil containing viable knotweed material is not suitable for disposal under an exemption from Section 34 of the Environmental Protection Act 1990. Section 34 imposes a duty of care on a person who produces, imports, carries, keeps, treats or disposes of controlled waste, or acts as a broker for such wastes.

iv) How do I recognise rhizome?

An identification chart for knotweed rhizome, and a comparison with other commonly encountered roots, is provided within Appendix II. The former Welsh Development Agency, now part of the Welsh Assembly Government, has produced a tabular guide to the identification of knotweed rhizome that is reproduced in Appendix III with their kind permission.



Root / rhizome identification chart - Japanese knotweed

Plants commonly found on development sites



Japanese knotweed *Fallopia japonica* (and other Asiatic invasive knotweeds).

Japanese knotweed is commonly encountered on brownfield sites, where soil disturbance and fly-tipping are common. Close proximity to rivers, roads and railways may also provide a source of invasion.

External appearance of root or rhizome



Colour:

Dark brown, lighter when dried.

Texture:

Smooth skin, becoming rough when desiccated.

Features:

often forming long knotty lengths. May support small red buds, particularly on crowns (base of stem). Fine hair-like roots common, particularly on thinner sections.

Snap Test



Snapability:

Easy. Very carrot-like in structure and colour when fresh. More woody when dry. Older material, particularly near the crown, can be very woody. Colour can vary from deep red to pale yellow, with orange the most common. Younger fresh material usually has a different coloured core.

Scrape Test



Outer layer:

Thin skin, easily removed when fresh.

Inner layer:

Pale threads often run through darker fibrous flesh, particularly in larger rhizome. Often variations in colour through rhizome when split lengthways. Crown material is often caked with soil and can be hard to recognise. Cleaning should reveal red buds and characteristic flesh.

Not all rhizome regenerates in the same manner and the factors that determine rhizome regeneration are the subject of research. It appears that older rhizome becomes woody, and tends to be utilised by the plant for food storage, whereas the fresh young rhizome is more carrot-like and much more infectious. Therefore, the small pieces at the extreme edge of the rhizome ring are potentially the most infectious, and therefore require the greatest of care. It is good practice to excavate another 0.5m around the perimeter of the cut after all rhizome has been apparently removed as a further precaution.

Rhizome is an underground stem, rather than a root, and will tend to spread laterally. The rhizome at the periphery of the matrix will tend to be shallow, therefore the excavation usually describes a saucer-shaped profile.

Having excavated the rhizome it is essential that waste streams are kept separate and that rhizome is not allowed to contaminate spoil that has been removed from areas free from rhizome.



Remember:

Do not excavate rhizome unless you have to, especially if you do not have the capacity to treat the material on site.

A 0.7g piece of rhizome is approximately the size of your little fingernail, and this may be capable of growing into a new plant.


The matrix of the rhizome will vary in size and extent, depending on the nature and history of the site. Careful use of this guide will minimise the waste

you produce and significantly reduce your costs.

Rhizome may remain dormant for at least 20 years. Dormant rhizome may regrow if it is disturbed. Lack of regrowth is not evidence of eradication.

Avoid spreading rhizome by following the guidance given within the knotweed code of practice.

If you spread rhizome into the environment you may be liable to prosecution under the Wildlife & Countryside Act 1981.

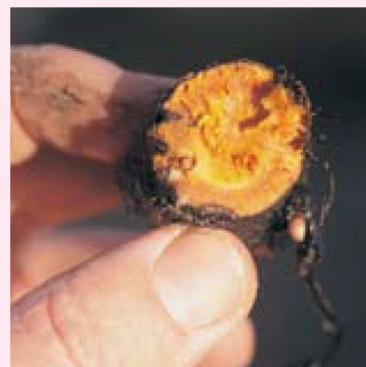

Root / Rhizome identification chart - other common plants

Plants commonly found on development sites

**Dock:**

Common on disturbed ground and in topsoil. Agricultural weed and covered by the Weeds Act 1959. Closest native plant to knotweed, so similar root appearance.

External appearance of root or rhizome

**Colour:**

pale red/brown.

Texture:

Fleshy skin.

Features:

Tapering, with branches clustered near the tip. Lacking the knotty appearance of knotweed.

Snap Test

**Snapability:**

Easy. Rubbery, but lacks the carrot-like snappiness of knotweed. Core is similar colour to the rest of the root, lacking the colour variation of knotweed rhizome.

Scrape Test


**Outer layer:**

Thin skin, similar to knotweed.

Inner layer:

fleshy, with a distinct core. Orange/yellow in colour, but usually paler than knotweed.

Plants commonly found on development sites

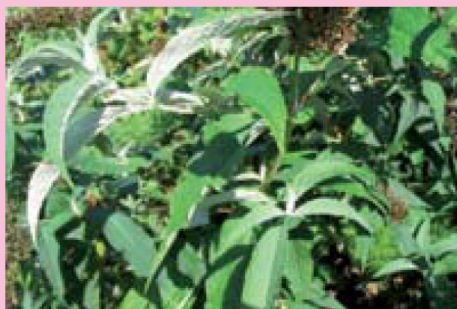

Buddleja (Butterfly bush):

Introduced shrub (intro: 1890), colonising waste ground and masonry. Spread by seed. Pink, purple or white flowers. Corky bark. Silver underside to leaves.

External appearance of root or rhizome



Colour:

Pale brown.

Texture:

Bark-like.

Features:

Bark easily damaged and revealing the woody core. Tough.

Snap Test



Snapability:

Very poor. Tends to rip rather than break cleanly. Distinct core.

Scrape Test



Outer layer:

Thin wrinkled bark.

Inner layer:

White wood.

Root / Rhizome identification chart - other common plants

Plants commonly found on development sites

**Elder:**

Native shrub, typical of disturbed ground and wasteland. White clusters of flowers in spring, black berries in autumn.

External appearance of root or rhizome

**Colour:**

Pale brown/yellow

Texture:

Fleshy and smooth. Wrinkled if desiccated.

Features:

Fleshy rootlets.

Snap Test

**Snapability:**

Reasonable. Thin sections snap, but larger sections are too woody. Tends to tear.

Scrape Test


**Outer layer:**

Skin easily removed.

Inner layer:

White fleshy layer with a pale woody core.

Plants commonly found on development sites

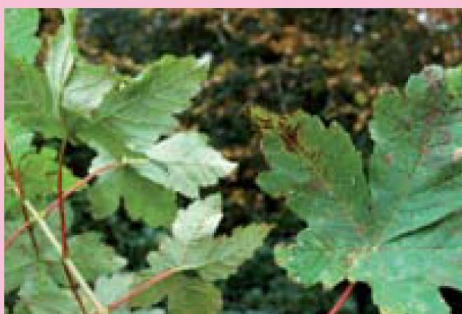

Sycamore (and most other trees):

Trees are common colonisers of waste ground.
Their roots are occasionally mistaken for rhizome.

External appearance of root or rhizome



Colour:

Mid-brown.

Texture:

Fairly smooth and even.

Features:

Does not fragment as easily as knotweed. Tend to remain in tapered sections. Fine rootlets.

Snap Test



Snapability:

Very poor. Very woody, tending to break and tear rather than snap. Fairly uniform in colour and structure.

Scrape Test



Outer layer:

Tough bark.

Inner layer:

Pale coloured wood.

Table for the identification of Japanese knotweed rhizome

General characteristics	Yes	No
Twig-like appearance		
Fleshy with hardness like carrot		
Brittle when fresh, break easily like carrot		
Young rhizome is white and very soft		
Exterior of rhizome	Yes	No
Colour dark brown, like coffee granules		
Texture of the outer bark leathery		
When bark is removed, tissue is pale orange/yellow		
Nodes at 1-2cm spacing		
Nodes slightly enlarged and 'knotty'		
At nodes white fibrous roots are common		
If present, fresh buds at nodes are red/pink		
Interior of rhizome		
Longitudinal view	Yes	No
Colour: pale orange and light yellow, similar to a carrot		
Central core is usually dark orange/brown, like rust, and sometimes hollow		
Cross section	Yes	No
Cortex with rays coming from centre, like spokes from a wheel		
TOTAL		

If the 'yes score is greater than the 'no' score, then treat the identified rhizome as Japanese knotweed.

Reproduced with kind permission of the former Welsh Development Agency, now part of the Welsh Assembly Government.

APPENDIX 6 – CEMP MASTERPLAN

[illegible]

Survey Details

1. OS grid & datum determined by GPS
2. North arrow indicates approximate North
3. Scale factor 1,00000
4. Contour interval 0.5m
5. All internal monobase details to be checked prior to site works

1
 2
 3
 4
 5
 6
 7
 8
 9
 10
 11
 12
 13
 14
 15
 16
 17
 18
 19
 20
 21
 22
 23
 24
 25
 26
 27
 28
 29
 30
 31
 32
 33
 34
 35
 36
 37
 38
 39
 40
 41
 42
 43
 44
 45
 46
 47
 48
 49
 50
 51
 52
 53
 54
 55
 56
 57
 58
 59
 60
 61
 62
 63
 64
 65
 66
 67
 68
 69
 70
 71
 72
 73
 74
 75
 76
 77
 78
 79
 80
 81
 82
 83
 84
 85
 86
 87
 88
 89
 90
 91
 92
 93
 94
 95
 96
 97
 98
 99
 100

APPENDIX 7 DEMOLITION METHOD STATEMENT

Demolition Method Statement

Cardonnel Court
CARDONNEL ROAD
SKEWEN
NEATH

23-00333

SA10 6BS

MS 01 REV 02

23rd October 2023

Author – Daniel Beck

Structural Demolition

Inc. Internal strip out in preparation for full structural demolition.
Grub up ground bearing slab and foundations.
Works near adjoining rail line.

HEALTH & SAFETY NOTE TO ALL PERSONS ENGAGED TO CARRY OUT ANY WORKS ON SITE ON BEHALF OF ALLCLEAR DEMOLITION

ALL STAFF EITHER DIRECTLY EMPLOYED OR SUB-CONTRACTED TO ALLCLEAR DEMOLITION ARE EXPECTED TO COMPLY AND FOLLOW ALL SITE RULES, REGULATIONS, AND WORK TO AND COMPLY WITH ALL METHODS OF WORKS AND RISK ASSESSMENTS AND ENSURE AT ALL TIMES THEY KEEP THEMSELVES AND COLLEAGUES SAFE.

ALL PERSONS ARE EXPECTED TO BE MINDFUL OF THE WORKS THEY ARE BEING ASKED TO DO AND IF AT ANY POINT THEY FEEL THE WORKS ARE BEING UNDERTAKEN UNSAFELY OR INDEED SEE ANY PRACTICES OR PERSONS CARRYING OUT ANY WORKS THEY DEEM TO BE UNSAFE THEY ARE TO MAKE EITHER ALLCLEAR DEMOLITION'S SITE MANAGER OF IF ANOTHER CONTRACTOR THEIR MANAGER IMMEDIATELY AWARE AND ENSURE THE ACTIVITY IS STOPPED AND CORRECTIVE ACTIONS TAKEN.

IF IN DOUBT

STOP, ASK, TELL

KEEP EVERYONE AROUND YOU SAFE!

Allclear Demolition Ltd
The Quarry Gap
250 Dick Lane
Bradford.
West Yorkshire.
BD4 8JH
Tel: 0113 204746

Joshua@allclearsiteservices.co.uk

Dan@allclearsiteservices.co.uk

This **Method Statement** has been produced in accordance with **BS6187:2011 Code of Practice for Demolition** and **Regulation 20 of the CDM Regulations 2015**, the information contained herein are to be complied with by all site personnel. This Method statement is classed as a live document and information may be changed or added as the works progress.

Table of Contents

Title	Page Number
Introduction and General Comments	3
Welfare and Accommodation	5
Working Hours	5
Services	5
Safety	5
Operation 1 – SITE ESTABLISHMENT	9
Operation 2 – DEMOLITION	11

Cardonnel Court, Cardonnel Road, Skewen, NEATH



Allclear Demolition Directory

Name / Position	Email	Tel No.
Josh Dean Director	Josh@allclearsiteservices.co.uk	0113 2047468
Natalie Watson Business Development Manager	Natalie@allclearsiteservices.co.uk	0113 2047468
Daniel Beck Project Co-Ordinator	Dan@allclearsiteservices.co.uk	07803 847163
TBC Site Supervisor		

1. Introduction and General Comments

- 1.1 This document is the demolition method statement describing the internal strip out followed by the structural demolition works at the above site. Allclear Demolition have been appointed to undertake the these works by Squirrel Wood Properties.
- 1.2 This Method Statement is to be read in conjunction with the Demolition and Construction Environmental Management Plan (DCEMP), the requirements of which must be strictly observed.
- 1.3 Allclear Demolition has visited site and assessed the structures and how they are stabilised and confirm that the sequence of operations detailed below is a safe system of work. The likelihood of damage to adjacent structures or nuisance to the occupiers due to ground-borne vibration is considered to be high due to the proximity of the neighbouring buildings and occupying tenants, the proposed method of works has been planned in such a way to minimise disruption.
- 1.4 Allclear Demolition employees must always whilst on site comply with the requirements of the Health and Safety at Work Act 1974 etc., the Construction (Design and Management) Regulations 2015 and all other relevant safety legislation codes, standards, and guidance.
- 1.5 Allclear Demolition employees are familiar with the British Standard B.S. 6187 Code of Practice for Demolition 2011 which has been referred to during the preparation of this Method Statement.
- 1.6 Plant certificates will be obtained for all plant used and copies of the certificates retained on site to demonstrate compliance with relevant legislation (PUWER, LOLER)
- 1.7 All site personnel are to produce CSCS / CCDO licenses. All plant operators are to produce CPC / NPORS licenses. All staff involved in the demolition element of the works are to have current asbestos-awareness training certificates and or CAT B and face-fit tests. Each member of site staff will be made aware of DCEMP and their requirements to comply with it and will also be provided with a copy of this DCEMP.

1.8 **SITE STAFF**

(Additional Labour if required will be provided on site dependant on workload & programme)

Operatives	Inc. Regular visits by Senior Management.
1 – 2 No. Site Supervisor Up to 4 No Plant / Machine Operatives. Up to 8 No Demolition Operatives.	

1.9 **PLANT & EQUIPMENT**

(Additional Plant and equipment will be provided on site dependant on workload & programme)

Plant
Demolition Specific Excavators with relevant attachments Skid steer loaders (bobcat) with relevant attachments Self-contained pressure-washer for dust suppression / standpipe / hoses / Fine mist water sprayer Mobile Elevated Working Platforms (MEWPS)
Equipment
Hand tools (including sledgehammers, shovels, brooms, wrecking-bars, 18v impacts drivers) Circular (“Stihl”) saws, Reciprocating Saws (or 110v Variant) Oxyacetylene Cutting Equipment. Bunded fuel tank with drip tray and spill kit 2.0m high “Heras” fencing Podium towers or Scaffold towers

- 1.10 Previous experience of similar work is such that noise levels as high as the Upper Exposure Action Value (85dB(A)) are not expected to occur. The proposed method of working and the equipment to be used have been selected, in part, to reduce noise levels to the lowest reasonably practicable level in line with the Control of Noise at Work Regulations 2005 (Reg 6(1)) and it is not considered necessary to undertake any noise measurement (Reg 5(2)(c)). Should it be necessary to modify the method of demolition, this position will be reviewed (Reg 5(4)(b)).
- In addition to this, the measures set out in DCEMP to control noise and vibration will be undertaken during the course of the demolition works.
- 1.11 All waste materials will be removed from site utilising 40 / 35 / 20 cu yd roll-on-off (Hook load or "roro) skips for general waste, timber, and scrap steel and concrete arisings. All waste will be accompanied by a duty of care waste transfer note which describes the waste, and a copy will be retained on site.
- 1.12 Allclear Demolition will endeavour to undertake the work described below in such a way as to minimise the impact of that work. Therefore, the supervisor will:
- Take all reasonable steps to minimise the creation of dust, using water sprays to dampen buildings being demolished and the demolition arisings.*
- Curtail, suspend, or re-arrange work as necessary to allow the demolition to proceed if possible whilst reducing its impact on any the occupiers and neighbouring properties / premises.*
- Ensure all plant is fit for its purpose and adequately maintained so that noise generation is within the manufacturer's stated maximum noise level.*
- Consider activity on site at the start of the day to minimise disturbance of the neighbours. Reversing manoeuvres will be avoided in the early morning to prevent reversing sirens sounding. Mobile plant, which requires approximately 20 minutes idling to warm-up before a shift, will be parked sensibly away from nearby residential properties.*
- Monitor the condition of the public highway when HGVs are leaving site. A jet wash will be used if necessary. Self-propelled road sweepers will be engaged from time to time as necessary to keep the highway clean.*
- 1.13 All visitors to site will receive an induction from Principal Contractor along with Allclear Demolition's Site supervisor before being admitted to the works area. During the induction, the current activities on site will be described to assist visitors in anticipating the presence of mobile plant on site. If necessary, visitors will be accompanied / chaperoned around site. All workers and visitors to site will be required to wear the necessary PPE, including high visibility vests.

ADDITIONS AND OR AMENDMENTS MAY BE MADE TO THIS MEHOD STATEMENT FROM TIME TO TIME AS WORKS PROGRESS. VARYING ELEMENTS OF WORKS AND OR PROCEDURES MAY CHANGE TO ENSURE TASKS ARE CARRIED OUT SAFELY AND CORRECTLY. ANY ADDITIONS OR AMENDMENTS WILL BE DISCUSSED WITH ALLCLEAR'S SITE PERSONNEL AND CLIENTS SITE MANAGEMENT TEAM. THE SYSTEMS AND PROCEDURES DISCUSSED ALONG WITH PLAN OF WORKS AGREED WILL BE DISCUSSED AND EXPLAINED TO ALL ALLCLEAR SITE OPERATIVES.

2. Welfare and Accommodation

- 2.1 Suitable albeit temporary welfare facilities and a compound will be established within the curtilage of the site, prepared, and maintained by the Principal Contractor as described in the DCEMP.
- 2.2 The temporary site accommodation may comprise of a self-contained welfare unit provided by a local hire company. The facilities comply with the Construction (Design & Management) Regulations 2015 and will be maintained to a high standard of hygiene by all site operatives.

3. Working Hours

7.30 am - 5.00pm Monday-Friday
8.00 am – 4.00pm Saturday-Sunday

4. Services

- 4.1 All services to the area of works are to be disconnected or isolated and arranged by the client.
- 4.2 Allclear Demolition Ltd reserves the right to cease or indeed not begin any works on site if live services remain. **The client can arrange for services to be terminated / isolated within the area of works by a suitably qualified person to permit works to begin.**
- 4.3 The water supplies to the building will be terminated at the external stop-taps. Mains water supplies to the site are to be retained for as long as possible to provide water for dust suppression. Once water supply is terminated (cut off) a self-contained pressure washer bowsers will be used.
- 4.4 A full copy of services plans, and disconnections / isolations is to be provided by the client and reviewed by Allclear Demolition before work commences on site. Mains records for the site will be maintained by the client in the site office.

EXISTING DRAINS

- 4.5 All existing drain runs which will have been recorded by survey are to be maintained and kept clear of all demolition materials and debris. All gullies and channel drains, including gullies serving downpipes are to be kept clear to allow proper draining of precipitation falling on the site. Allclear will construct temporary bunds as required to intercept surface water run-off and prevent rainwater discharge beyond the site boundary.

STREAM / DITCH

- 4.6 Located at the northern boundary, running parallel an old wooden fence, a ditch and stream along with a line of trees all backing onto the rear gardens of 2 to 17 Bendle Close will be inspected and if required, gaps within the fence will be protected with barrier fencing reducing the risk of debris leaving the site boundary throughout tasking.

5. Safety

All necessary Site Registers, Risk Assessments, Method Statements, Relevant Surveys, Plant Certification, Waste Carriers, Insurance etc will be kept on site under the control of Allclear Demolition's Site supervisor and can be inspected at any time. All accidents are to be reported and subsequently entered in the site accident report book.

- 5.1 Senior Staff at Allclear Demolition will endeavour to measure Health and Safety on site by conducting regular internal site safety audits ensuring works are being conducted to a high standard and in accordance with the agreed contract.

- 5.2 The mandatory first aid requirements for a construction site are covered in the Health and Safety (First Aid) Regulations. The appointed person (Allclear site supervisor) will provide and stock a first aid box with sufficient supplies to cater to the number of workers on site. An appointed person must be always on-site.
- 5.3 All operatives on site must wear full PPE including as a minimum safety boot, hard hats, a high visibility vest or coat and gloves. Additional PPE requirements as identified within the risk assessments will be utilised when undertaking specific tasks. A supply of spare hard hats, overalls, gloves, goggles, masks, and relevant PPE will be stored on Site.



EN ISO 20345



BS EN 397



EN 471



EN 420



EN 352



EN 166



FFP3

- 5.4 Smoking is not permitted anywhere on site. A smoking zone will be established within the site compound / welfare area, with an additional smoking zone and or zones located at specific points around the site.
- 5.5 Adequate segregation of pedestrians and vehicular traffic will always be maintained. Unobstructed access to and egress from the buildings must always be maintained. Pedestrian access to the buildings will be defined using suitable and adequate barriers. Reversing of vehicles and plant will always be minimised. This will be highlighted on a site plan and will form part of the site induction for all operatives.
- 5.6 Emergency procedures will be in line with Allclear Demolition's protocols. All incidents on site (including near misses) are to be reported to Allclear demolition's site management and recorded on the relevant documentation for the incident (near miss, accident, dangerous occurrence etc).
- 5.7 Emergency contact numbers are posted on the wall of the welfare facilities. For major emergencies, Allclear demolition's Site supervisor is to be informed to enable them to coordinate the emergency services on arrival on site and to manage or suspend on-going site activities.
- 5.8 Mobile plant will be used, along with relevant waste skips positioned within exclusion zones formed using 2.0m high Heras fencing.

PLANT REFUELLING

- 5.9 As detailed in the DCEMP, refuelling plant and machinery on site, plant operators are to refuel in the designated re-fuelling areas where a bunded fuel tank will be stored together with spill kits. Should any spillages occur the spill kits provided shall be used immediately and the site team shall be informed of such spillages. Fuel will be stored in the containment area.
- 5.10 During the refuel process engines must always be switched off. Plant operators are to use the plants own refilling pipe. This shall be placed into the tank and the pump switched on. Operators are to ensure that the cap is removed from the fuel tank during this process to allow the gases to escape preventing tank expansion.
- 5.11 Upon completion of refuelling the pump shall be switched off and the pipe shall be removed from the tank but must remain within the bunded area. The pump shall be then switched on again to drain any excess fuel from the pipe itself. The pipe shall then be removed from the tank and place back in its housing within the plant/ machinery. The bowser/ tank shall then be locked by the operator and the designated area secured.

DUST

- 5.12 Dry areas of works will be dampened down to prevent the spread of airborne dust. All personnel working in a dusty area shall, where necessary, wear a dust mask deemed suitable by the HSE (Health and Safety Executive)
- 5.13 During the demolition works a self-contained pressure washer bowser and, if made available, a standpipe and hoses will be utilised for dust suppression. Subsequently, both will be positioned outside of the immediate demolition zone. Water will be delivered into the area using the gun attachment on the bowser / hoses. An added pressure washer / standpipe will be attached to the working end of the excavator arm throughout tasking.

HOT WORKS

- 5.14 Should it be necessary to undertake any hot-cutting, Circular ("Stihl") saws / reciprocating saw or 110v variants will be used. Only certified operatives will be used to undertake these works, which will be in accordance with the Risk Assessments (hot works). A permit to undertake hot works will be provided daily.
- 5.15 If Oxyacetylene cutting equipment is required, gas and oxygen bottles will be stored separately in fenced off areas with appropriate signage.
- 5.16 Fire Extinguishers – In date, brought to site for use throughout hot works taskings.
- 5.17 Added to this, mains water supplies to the site in the form of fire hydrants are to be retained for as long as possible to provide water for potential extinguishing purposes.

GUIDANCE ON EMERGENCY RESCUE - MEWP

- 1) **Rescue Plan**
Normal and auxiliary control systems built into a mobile elevating work platform (MEWP) will allow the operator to bring the platform of the machine safely to ground level under controlled conditions. It is extremely unusual not to be able to lower the platform using these controls or for all these systems to fail. The following is an example of a rescue plan for people who work at height using a MEWP.

EMERGENCY SITUATION	PROPOSED ACTION
Failure of upper control functions while elevated.	Where the normal upper control functions fail, the operator will use the upper auxiliary controls to lower the platform safely.
Failure of the operator to be able to operate the MEWP functions while elevated due to one of the following reasons: A. Operator incapacitated. B. Auxiliary functions fail to operate from upper control station	Where the operator is incapable of lowering the raised platform using the upper controls, an appointed person familiarised in the use of the 'ground' controls will lower the platform safely using the normal ground controls.
Failure of normal ground controls	Where the normal ground controls fail, an appointed person familiarised in the use of the ground controls will use the ground auxiliary controls to safely lower the platform.
Failure of ALL normal and auxiliary lowering functions.	Where all normal and auxiliary functions have failed a competent and authorised service engineer should be contacted

Names of nominated ground person(s) on site familiarised and authorised to lower the work platform in the event of an emergency or a machine malfunction.

Name	Signature

This rescue plan should be brought to the notice of those exposed to the risk of working at height and those supervising and managing the same work at height.

2) Consideration for mid-air rescue:

A mid-air platform rescue should only be considered in exceptional circumstances and only after:

- All normal and auxiliary lowering procedures have been attempted and these are unable to lower the platform.
- Site management have contacted the competent and authorised service engineer listed in the rescue plan, to report failure of normal and auxiliary lowering systems and request engineering access.

If after inspection by the competent engineering assistance, it is not possible to affect a timely repair to allow the machine to be brought to the ground safely; senior site management should be contacted for permission to carry out mid-air rescue.

Or

Where the competent engineering assistance is not readily available and an immediate risk exists to the health and safety of any occupants from remaining in the elevated basket until an engineer can attend, then senior management should be contacted for permission to carry out mid-air rescue.

3) Code of Practice for mid-air rescue

- A. Rescue using another MEWP should only be performed once a site-specific risk assessment has been carried out and a specific plan has been documented and approved by senior management.
- B. The rescue machine must be positioned to enable the rescue procedure to be carried out without compromising the safety of any personnel involved in the rescue procedure.
- C. The Platforms of both machines must be adjacent to each other with a minimal gap between them, unless exceptional circumstances mean this is not possible. (Where this is not possible, the circumstances shall be recorded on to the risk assessment form.)
- D. Where reasonably practical, precautions should be taken to prevent inadvertent movement of both platforms during the transfer.
- E. The person being rescued (transferred from basket to basket) should wear a full body harness with an adjustable lanyard – the lanyard should be attached to the anchor point on the rescue machine before transfer takes place.
- F. Care must be taken to not overload the rescue machine during transfer. This may mean making more than one journey to complete the rescue.

Operation 1

6. Site Establishment

The site is currently a derelict nursing home complex in a triangle of land between Cardonnel Road running diagonally from the northwest to the southeast, Bendle Close to the north and a railway line to the east. Network Rail which operates one of the main transport links from South Wales to London.

The footprint of the old buildings cover most of the east of the site with tarmacked parking and access towards the west. The boundary along Cardonnel Road from the northwest to the southeast consists of a raised concrete bed with woody shrubs, the old vehicle and pedestal entrance and a soil bank.

The boundary along Bendle Close or northern boundary has running parallel an old wooden fence, a ditch and stream and a line of trees all backing onto the rear gardens of 2 to 17 Bendle Close. The narrow entrance of Cardonnel road branches out with the two boundaries either side partially retaining the road on one side and a water course on the other.

The boundary to the east has a fence separating the railway line embankment which falls steeply away down to the track, along the longest axis of the old building. A visual inspection of the building did not reveal any significant structural issues with the primary structure, though the timber decking at the rear of the building is currently not safely accessible due to the condition of the timber.



The boundary of site and agreed areas of works have been established by the client and Allclear Demolition. Additional 2.0m high Heras fencing will be utilised within the site as segregation, waste skip compounds and drop zone areas. Warning signs will be displayed at appropriate points of segregation throughout the site.

Waste material and demolition arisings will be removed from site by mechanical means, loading into 40yd waste skips located within an established compound.

- 6.1 Prior to any works commence on site and before any strip out and minor demolition works begin, a thorough, systematic search of the task area is to be undertaken by the Allclear Demolition site manager to ensure no trespassers, other unauthorised persons are within the building. The integrity of the exclusion zone will be checked at the beginning and end of every working day and after breaks to ensure, so far as it is reasonably practicable to do so, that no person is within the immediate tasking area.

Bat Survey

BE Ecological Ltd: Survey Issue 1, Version A, June 2023

Section 9 - Method Statement

- 6.2 A suitably licenced and experienced ecologist will be on call for the duration of the works.
- 6.3 Before any work begins on site, a briefing for contractors and other site-staff 'toolbox talk' will be given by an ecologist. The briefing will cover the issues in respect of protected species they may encounter on site, where they might find them, methods of working, and what they need to know to avoid committing an offence. Every briefing attendee will be provided with a copy of a Method Statement and the contact details of an ecologist and Natural Resources Wales.
- 6.4 If at any point bats or evidence of bats is found, all works will cease, BE Ecological Ltd informed and NRW consulted.
- 6.5 If bats or their signs are found, an EPS licence may be required before works can legally resume.

Japanese Knotweed

Knotweed Control (Swansea) Ltd: Survey CC/ SA10 6BS/2023, 1st February 2023

Japanese knotweed Management Plan & Method Statement.

- 6.6 There is a high risk of cross contamination of potentially viable knotweed material during the demolition and removal due to the proximity of the knotweed to the structures – the building, foundations and car park and path areas including concrete and tarmac.
- 6.7 Work on again should start in areas that are **knotweed FREE areas first** moving towards the areas with Japanese knotweed so there is reduced likelihood of cross containable or spreading viable propagules.
- 6.8 When demolishing structures or removing them from site, the knotweed should be disturbed as little as possible including the rhizome buffer zone 7m from the visible above the ground knotweed canes.
- 6.9 When removing materials and structures from site near the knotweed, careful extraction is required as not to pick up viable Japanese knotweed propagules and moving them around or off site especially on treads on vehicles and footwear or the structures or materials themselves.
- 6.10 Careful **cleaning e.g. pressure washing and inspection** of any treads on vehicles and footwear or the structures or materials needs to be undertaken by the Japanese knotweed Clerk of Works to ensure no potential knotweed propagules are taken before leaving the location.
- 6.11 Any vegetation, concrete, spoil, tarmac, soil etc. potentially contaminated with Japanese knotweed material is classed as a controlled waste (see vi. **LEGALSATION**) **so should be kept to a minimal and stored transported and disposed of appropriately.**

Operation 2

7. Structural Demolition

- ASBESTOS CONTAINING MATERIALS
- INTERNAL STRIP OUT (GENERAL) ACROSS SITE
- STRUCTURAL DEMOLITION
- WORKING ADJACENT TO LIVE RAILWAY
- FOUNDATIONS & FOOTINGS
- LOGISTICS FOR WASTE REMOVAL

Description of Works

This Method statement is the outline describing the works associated with the complete structural demolition, including grubbing out and removal of existing foundations of the former Cardonnal Court nursing home, a single storey T shaped plan formation. 39 individual rooms, constructed of load bearing masonry walls with timber joists supporting the ceiling and forming the floor for the attic. The existing pitched roof profile is likely formed with timber rafters throughout.



Existing Site Plan

On completion of site set up an internal soft strip of fixtures and fittings, doors, windows and anything not structurally integral to the building will take place in preparation for the structural demolition. All soft stripping works are to be carried out manually by operatives utilising hand tools, separating, and disposing off site all arisings utilising 40yd waste skips.

Demolition of the superstructure will be undertaken by mechanical means using demolition-specific excavators with appropriate attachments. All arisings are to be either stockpiled away from the immediate task area in preparation for the removal from site or loaded directly into waste skips. Following the demolition task, the existing ground bearing slab is to be grubbed up and removed from site along with all risings produced from the structural demolition.

The area around any demolition tasks will be segregated and drop zones established using Heras fencing with appropriate signage attached. Entry will be restricted to demolition personnel only.

Risk assessments for this process; for the tools, plant and equipment which will be utilised to undertake this work and for the associated hazards are recorded in a separate document. The risk assessments and this method statement are mutually complementary.

ASBESTOS CONTAINING MATERIALS

*A pre-demolition / pre-refurbishment survey in line with HSG 264 has been produced for the building on site. Surveys were undertaken by **Environmental Management Solutions**, Survey Ref: **E-31670**, On **27th October 2022**. A copy of the R&D survey is available on site and kept in the site managers office.*

NO ASBESTOS DETECTED

- 7.1 All Allclear Demolition Ltd staff are CAT B (NNLW) Notifiable Non-Licence Waste asbestos removal trained operatives. Staff are trained and experienced in asbestos identification (identification in the form of samples sent to an accredited laboratory will still be required to positively identify the suspect material) and removal. If suspect materials other than those identified in the report are suspected or identified **works will cease** and the area made safe, additional procedures for the safe removal of the material will be required depending on the material discovered and revised RAMS / PLAN OF WORKS produced covering the removal. All staff will be briefed on this during the induction process including RAMS induction.


INTERNAL STRIP OUT (GENERAL) ACROSS SITE

Soft stripping as the name suggests is the removal / stripping of all / most of the soft materials within a building, this is generally, carpets, loose furnishings, doors, panelling etc., mainly anything that is not structural or integral to the building, most of the building on site will need a varying degree of soft stripping, some to assist in the removal of asbestos containing materials if identified, and others to assist in the demolition. Where it is possible materials can be left within the building and removed mechanically where possible to minimise the manual handling and exposure of operatives.

- 7.2 The nature of the work is such that manual handling is unavoidable. Toolbox talks will be held on this subject at intervals during the work to ensure operatives do not put themselves at risk of musculoskeletal injury due to their work. The toolbox talk will draw on the guidance in the HSE's publication "Getting to Grips with Manual Handling" (INDG143)
- 7.3 Pedestrian access to the works area will be via specified routes to be confirmed by the site manager during the site induction. Allclear Demolition Ltd operatives are to use only the specified routes to and from the works areas.
- 7.4 Heras fencing or pedestrian barriers will be used as edge protection.
- 7.5 In general, soft-stripping is a reverse of the fitting-out of a building; so, carpets and floor coverings are removed first followed by "second fix" features then "first fix" features and finally internal non-structural walls. Working sensibly and systematically away from the building access point, demolition operatives will remove all loose furniture by hand and using hand carts, wheelbarrows, trolleys etc to agreed drop zone points on the outside of the building.
- 7.6 Using hand tools, the demolition operatives will then strip out all identified doors, frames, windows, timber of any description, (not appertaining to roof or main structure) toilets, pipe work, ducting, electrical items, carpet, window coverings and any debris.
- 7.7 Arising's from the stripping tasks will be deposited directly into the skips wherever possible, which will be in a fenced loading area. Alternatively, materials will be retrieved using the skid-steer dumper which will be used to convey the material to the skips for subsequent removal to a recycling facility or transfer station. It will be the responsibility of the site supervisor to ensure that suitable loading areas are maintained, and that fencing integrity will be in place (most notably immediately after removal of skips).
- 7.8 Access to the ceilings will be via podium tower / scaffold tower – where the latter is used it will be inspected prior to use by a PASMA trained operative and a tag confirming it is safe to use applied. The tower will be inspected daily, and the tag updated accordingly.

STRUCTURAL DEMOLITION

Following the internal soft strip, removing all materials not structural or integral to the building, the sequenced structural demolition down to existing slab level of the former nursing home building will commence. Consisting of brickwork façade, internal blockwork partitions, timber roof trusses with supporting timber beams, with a hipped tile covered roof. Roof structures are to be removed initially, followed by the external brick and internal blockwork partitions are to be raised to slab level, processing and removing all arisings from site.

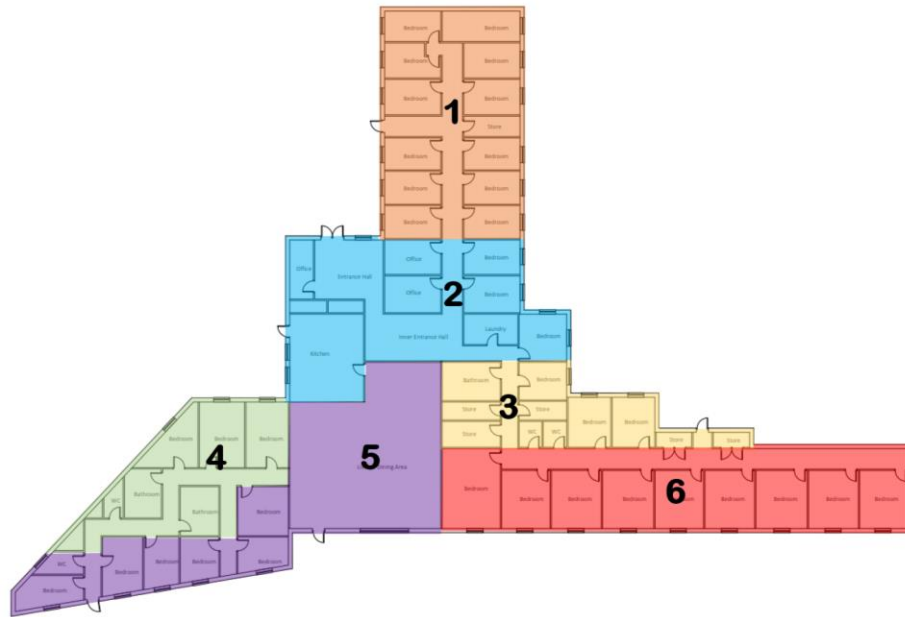

Proposed Demolition Sequence

- 7.9 Demolition of the superstructure will be undertaken by mechanical means using demolition-specific excavator with appropriate attachments. Tasking shall be planned so that at the end of each shift, works are left in a safe position overnight.
- 7.10 During the demolition works either a self-contained pressure washer or a standpipe and hoses will be utilised for dust suppression. The pressure washer / standpipe will be positioned outside of the immediate demolition zone. Water will be delivered into the area using the gun attachment on the bowser / hoses.
- 7.11 The area around the designated building will be segregated using Heras fencing with appropriate signage attached. Entry will be restricted to demolition personnel only. Banks men provided during demolition works are to be kept out of the demolition areas when demolition is being undertaken.
- 7.12 The plant operator must ensure the area is checked and clear before commencing with demolition tasking. Banks men will not be permitted to work near or under any blocks / walls within the demolition area.
- 7.13 This operation will begin by ensuring with the use of a self-contained pressure-washer unit that operatives will keep the works area wet throughout the tasking.
- 7.14 Starting from within the site boundary, using the demolition specific excavator with selecta grab attachment, the operator will firstly grab a section of the tile covered roof truss and purlins, allowing loose tiles to fall within the footprint of the building. Removing individual timber trusses from the building, placing directly into waste skips nearby or placed away from the immediate tasking area for

processing later. Any loose brick / block will be allowed to fall to the foot of the wall within the building footprint.

- 7.15 This process will continue, removing sections of exposed roof truss and purlins, in the process exposing the buildings brick and blockwork gable and side elevations ready for removal.
- 7.16 Again, using the Selecta grab attachment, the outer gable and side walls will be worked down from roof to ground floor level with all arisings being caused to fall to the ground at the foot of the wall or within the building footprint.
- 7.17 Once a section of the external gable and side brick walls have been removed down to ground floor level, the operator will then remove further sections of the wooden roof structure moving through the building. Progressing, further sections of the gable and side walls will be worked down to ground level with all arising being caused to fall within the building footprint.
- 7.18 Any internal walls will also be removed. If the walls are wooden stud walls they will be grabbed and removed and either placed directly into a skip or placed away from the immediate works area for processing later, for brick /block walls, again these will be grabbed with all arisings allowed to fall within the footprint of the building.
- 7.19 The processes described above in paras 7.9 – 7.18 will continue working through the single storey building being demolished. At all times the building will be stepped in profile. Demolition of the roof will always be further advanced than the floors below such that the building develops a stepped profile in cross section to maintain the stability of the building and to limit the imposed and very short-term loading from demolition arisings. Any imposed loading is estimated to be significantly less than the loading applied when the building was occupied.
- 7.20 On completion, the ground bearing slab will be cleared of all arisings which will be subsequently stockpiled ready for the removal from site. When an accumulation of blockwork and brick (hardcore) materials has been generated the excavator shall load the materials onto 8 Wheel tipper wagons, removing the materials from site to a local recycling centre.

WORKING ADJACENT TO LIVE RAILWAY

"The Network rail representatives have an interest in the works being undertaken due to the proximity of their asset. All demolition works being undertaken should be outlined in a method statement and programme of works" - Structural Demolition Report, Doc Ref: C1953-CB3-ZZ-XX-RP-S-0001

Rail Safety Brief to be given to all operatives at the start of works.

- 7.21 Network Rail (NWR) will provide a copy of their emergency procedures for the stopping of trains and power isolation if this is required. Copies of the procedures shall be always displayed in the site cabin and communicated to the operatives during the site induction. The contents of the emergency procedures shall be kept confidential and shall not be disclosed to any third parties away from the site.
- 7.22 **If required** during the commencement of demolition works highlighted in sequence areas 5 and 6, Network Rail supervision (Rail Safety Supervisor – RSS) may want to be present for these works, generally if the tasking is within 10m of NWR boundary fence. Weather conditions shall be monitored, and the works will not be carried out in any strong windy conditions.
- 7.23 **Reducing Risk** - A physical demarcation line will be established utilising the existing boundary fencing panels with debris netting attached along with added kickboards reducing the risk of debris from rolling down the embankment onto the railway line approx. 20m distance from demolition operations.

- 7.24 Manual Demolition will be considered when reducing the structural wall nearest to the NWR boundary fence utilising hand tools with access gained with the use of a tower scaffold, allowing arisings to fall within the building footprint.
- 7.25 On the attached plan below, hatched in yellow, this will be demarcated on site using the existing fencing. Operatives and plant shall not be positioned beyond this area. Highlighted in Yellow is a complete out of bounds area. At no time shall any plant, MEWP or the like work in this area. All excavators to be used are standard 360 excavators, no cranes, no long/ high reaches required for these works.



Demarcation line – Yellow dash Out of Bounds – Yellow Live Railway Line – Red dash

REMOVAL OF FOOTINGS AND FOUNDATIONS

This element of the method statement consists of the removal of ground bearing floor slabs, foundations, and hard stands in their entirety. Ensuring that the structure has been demolished down to the slab level before the commencement of this task, confirming that services have been identified and disconnection outside the footprint of the site, further, that certification has been issued and a hard copy available within the site office.

- 7.26 Once the structure has been demolished down to the ground bearing slab, the redundant materials will be cleared from the working area leaving only the slab hardstanding and foundations.
- 7.27 Using the bucket attachment on the demolition excavator the ground bearing slab will be lifted, commencing in one corner, a small excavation will be undertaken to expose the underside of the slab. The demolition excavator will be positioned on the slab section, the bucket will be beneath, then under mechanical pressure exerted by the excavator the slab will be lifted and released which will cause the slab to fracture.
- 7.28 Should the slab require pre-weakening then the demolition excavator fitted with a hydraulic breaker attachment will break various holes within the slab. This will be in strategic locations pre-weakening the slab; this will result in the slab breaking up more easily when lifted.
- 7.29 On completion of the sectional removal of concrete hardstanding, foundations and footings, operatives will establish stockpiles of arisings. Whilst removing foundations the sides of the excavation will be battered back to prevent them collapsing under the weight of the machine and to ensure that no vertical drops are left on the site.

LOGISTICS FOR WASTE REMOVAL

- 7.30 Waste shall be segregated as far as reasonably practical on site.
- Waste arisings** will be removed as Wood, Plasterboard, General Waste, hardcore and clean metallic waste arisings, all will be removed from the work area and loaded into skips / wagons for removal from site.
- 7.31 It has been agreed that a waste skip compound will be established within the curtilage of the site within a segregated fenced off compound.
- 7.32 Waste skips shall be loaded by mechanical means utilising the demolition specific excavator with grab attachment.
- 7.33 Egress for the removal of waste materials and disposing off site all arisings will be by utilising 40yd waste skips and 8-wheel tipper wagons.
- 7.34 All waste materials removed from site will be accompanied by a duty of care waste transfer note which describes the waste, and a copy will be retained on site.

Site Access & Egress

- 7.35 The construction route into the site will be via the M4, exiting at junction 43, and via the B4290 / Burrows Road onto Bosworth Road and then via the existing site arrangements off Meadow Lane from Cardonnel Road

ALL PERSONS SIGNING BELOW

This is record of document / task specific induction – by signing below you confirm that:

1. The contents of the Method Statement/Plan of Work and related assessments, Document Reference as detailed, have been explained to you or read by you and that you understand the contents and requirements detailed therein.
2. You will work in a safe manner as detailed in Method Statements/Plan of Work and related assessments.
3. If you cannot follow the Method Statement and related assessments due to any reason you will advise the Site Supervisor and work with them to review and change the Method Statement and related assessment(s) if appropriate

NOTE: Personnel can receive induction into as many Method Statements/other Documents as needed but do not start work without receiving induction and 'signing on'

Project No: 23-00333		Project Title: Cardonnel Court, Cardonnel Road, Skewen, Neath SA10 6BS	
MS Issue: 01 Revision Number: 02		Date Issued: 23 Oct 23	Title: CARDONNEL COURT - NEATH
DATE	NAME (PRINT)	SIGNATURE	INDUCTION BY (INITIALS)

Method Statement Amendment Sheet

Job / Project Title		
MS Revision Nr.		
Date		
Completed by:	<i>Name</i>	<i>Signature</i>

Description of Works	
Task <i>What is the task</i>	
Duration of Task	
Sequence <i>How are you going to do the task?</i>	
Location	

Resources Required	
Personnel	
Supervision	
Plant & Equipment	

Assessment of Significant Risks for all Tasks.	
Access <i>Working at height / enclosed spaces?</i>	
Others at Risk <i>Other site Personnel / Members of Public?</i>	
Noise / Manual Handling	
Hot Works <i>Permit Issued / Fire Fighting Equipment?</i>	

APPENDIX 8 -SURFACE WATER DRAINAGE PLAN



THE DITCH ALONG THE NORTHERN BOUNDARY WILL BE PROTECTED BY A CONCRETE PIERCE FENCE. THE FENCE WILL BE PROTECTED WITH BARBED FENCING TO REDUCE THE RISK OF DEBRIS LEAVING THE SITE DURING CONSTRUCTION. CONSTRUCTION, IF REQUIRED.

CONTRACTORS COMPOUND
• Storage of materials
• Plant and machinery
• Welfare facilities

SITE ACCESS AND PARKING
• Site access for construction traffic
• Access for construction deliveries
• Contractors parking

SITE ACCESS

- KEY:**
- EXISTING BUILDING OUTLINE
 - PROPOSED BUILDING OUTLINE
 - SILT PROTECTION BARRIER
 - SITE RED LINE BOUNDARY
 - TREE PROTECTION FENCELINE AS PER ARBORICULTURAL TECHNICIAN SERVICES LTD REPORT
 - SITE WALLS
 - HAZARDOUS WASTE CONTAINMENT AREA
 - CONTRACTORS COMPOUND
 - Storage of materials
 - Plant and machinery
 - Welfare facilities
 - SITE ACCESS AND PARKING
 - Site access for construction traffic
 - Access for construction deliveries
 - Contractors parking
 - SOFT LANDSCAPED AREAS
 - BIN STORE GRASS ROOF
 - TEMPORARY CONSTRUCTION PHASE BUNDLED PROTECTION TO DRAINAGE DITCH
 - TEMPORARY CONSTRUCTION PHASE SETTLEMENT POND/ SURFACE WATER DRAINAGE CHANNEL

NOTE:
INDICATIVE ONLY. THE FINAL DESIGN OF THE DRAINAGE CHANNELS WILL BE DEVELOPED BY THE MAIN CONTRACTOR. DRAINAGE CHANNELS WILL BE DEVELOPED BY THE MAIN CONTRACTOR. DRAINAGE CHANNELS WILL BE DEVELOPED BY THE MAIN CONTRACTOR. DRAINAGE CHANNELS WILL BE DEVELOPED BY THE MAIN CONTRACTOR.

BIRD BOX IN LANDSCAPED AREAS

INTEGRATED BATT TUBES AT HIGH LEVEL

ABBREVIATIONS	DESCRIPTION
A	Access
B	Bin Store
C	Compound
D	Ditch
E	Existing
F	Fence
G	Grass
H	Hazardous Waste
I	Impervious
J	Junction
K	Kiln
L	Landscaped
M	Main
N	Northern
O	Outline
P	Parking
Q	Quarry
R	Road
S	Settlement Pond
T	Temporary
U	Unit
V	Vent
W	Welfare
X	Excavation
Y	Yard
Z	Zone
AA	Access
AB	Access
AC	Access
AD	Access
AE	Access
AF	Access
AG	Access
AH	Access
AI	Access
AJ	Access
AK	Access
AL	Access
AM	Access
AN	Access
AO	Access
AP	Access
AQ	Access
AR	Access
AS	Access
AT	Access
AU	Access
AV	Access
AW	Access
AX	Access
AY	Access
AZ	Access
BA	Access
BB	Access
BC	Access
BD	Access
BE	Access
BF	Access
BG	Access
BH	Access
BI	Access
BJ	Access
BK	Access
BL	Access
BM	Access
BN	Access
BO	Access
BP	Access
BQ	Access
BR	Access
BS	Access
BT	Access
BU	Access
BV	Access
BW	Access
BX	Access
BY	Access
BZ	Access
CA	Access
CB	Access
CC	Access
CD	Access
CE	Access
CF	Access
CG	Access
CH	Access
CI	Access
CJ	Access
CK	Access
CL	Access
CM	Access
CN	Access
CO	Access
CP	Access
CQ	Access
CR	Access
CS	Access
CT	Access
CU	Access
CV	Access
CW	Access
CX	Access
CY	Access
CZ	Access
DA	Access
DB	Access
DC	Access
DD	Access
DE	Access
DF	Access
DG	Access
DH	Access
DI	Access
DJ	Access
DK	Access
DL	Access
DM	Access
DN	Access
DO	Access
DP	Access
DQ	Access
DR	Access
DS	Access
DT	Access
DU	Access
DV	Access
DW	Access
DX	Access
DY	Access
DZ	Access
EA	Access
EB	Access
EC	Access
ED	Access
EE	Access
EF	Access
EG	Access
EH	Access
EI	Access
EJ	Access
EK	Access
EL	Access
EM	Access
EN	Access
EO	Access
EP	Access
EQ	Access
ER	Access
ES	Access
ET	Access
EU	Access
EV	Access
EW	Access
EX	Access
EY	Access
EZ	Access
FA	Access
FB	Access
FC	Access
FD	Access
FE	Access
FF	Access
FG	Access
FH	Access
FI	Access
FJ	Access
FK	Access
FL	Access
FM	Access
FN	Access
FO	Access
FP	Access
FQ	Access
FR	Access
FS	Access
FT	Access
FU	Access
FV	Access
FW	Access
FX	Access
FY	Access
FZ	Access
GA	Access
GB	Access
GC	Access
GD	Access
GE	Access
GF	Access
GG	Access
GH	Access
GI	Access
GJ	Access
GK	Access
GL	Access
GM	Access
GN	Access
GO	Access
GP	Access
GQ	Access
GR	Access
GS	Access
GT	Access
GU	Access
GV	Access
GW	Access
GX	Access
GY	Access
GZ	Access
HA	Access
HB	Access
HC	Access
HD	Access
HE	Access
HF	Access
HG	Access
HH	Access
HI	Access
HJ	Access
HK	Access
HL	Access
HM	Access
HN	Access
HO	Access
HP	Access
HQ	Access
HR	Access
HS	Access
HT	Access
HU	Access
HV	Access
HW	Access
HX	Access
HY	Access
HZ	Access
IA	Access
IB	Access
IC	Access
ID	Access
IE	Access
IF	Access
IG	Access
IH	Access
II	Access
IJ	Access
IK	Access
IL	Access
IM	Access
IN	Access
IO	Access
IP	Access
IQ	Access
IR	Access
IS	Access
IT	Access
IU	Access
IV	Access
IW	Access
IX	Access
IY	Access
IZ	Access
JA	Access
JB	Access
JC	Access
JD	Access
JE	Access
JF	Access
JG	Access
JH	Access
JI	Access
JJ	Access
JK	Access
JL	Access
JM	Access
JN	Access
JO	Access
JP	Access
JQ	Access
JR	Access
JS	Access
JT	Access
JU	Access
JV	Access
JW	Access
JX	Access
JY	Access
JZ	Access
KA	Access
KB	Access
KC	Access
KD	Access
KE	Access
KF	Access
KG	Access
KH	Access
KI	Access
KJ	Access
KK	Access
KL	Access
KM	Access
KN	Access
KO	Access
KP	Access
KQ	Access
KR	Access
KS	Access
KT	Access
KU	Access
KV	Access
KW	Access
KX	Access
KY	Access
KZ	Access
LA	Access
LB	Access
LC	Access
LD	Access
LE	Access
LF	Access
LG	Access
LH	Access
LI	Access
LJ	Access
LK	Access
LL	Access
LM	Access
LN	Access
LO	Access
LP	Access
LQ	Access
LR	Access
LS	Access
LT	Access
LU	Access
LV	Access
LW	Access
LX	Access
LY	Access
LZ	Access
MA	Access
MB	Access
MC	Access
MD	Access
ME	Access
MF	Access
MG	Access
MH	Access
MI	Access
MJ	Access
MK	Access
ML	Access
MM	Access
MN	Access
MO	Access
MP	Access
MQ	Access
MR	Access
MS	Access
MT	Access
MU	Access
MV	Access
MW	Access
MX	Access
MY	Access
MZ	Access
NA	Access
NB	Access
NC	Access
ND	Access
NE	Access
NF	Access
NG	Access
NH	Access
NI	Access
NJ	Access
NK	Access
NL	Access
NM	Access
NN	Access
NO	Access
NP	Access
NQ	Access
NR	Access
NS	Access
NT	Access
NU	Access
NV	Access
NW	Access
NX	Access
NY	Access
NZ	Access
OA	Access
OB	Access
OC	Access
OD	Access
OE	Access
OF	Access
OG	Access
OH	Access
OI	Access
OJ	Access
OK	Access
OL	Access
OM	Access
ON	Access
OO	Access
OP	Access
OQ	Access
OR	Access
OS	Access
OT	Access
OU	Access
OV	Access
OW	Access
OX	Access
OY	Access
OZ	Access
PA	Access
PB	Access
PC	Access
PD	Access
PE	Access
PF	Access
PG	Access
PH	Access
PI	Access
PJ	Access
PK	Access
PL	Access
PM	Access
PN	Access
PO	Access
PP	Access
PQ	Access
PR	Access
PS	Access
PT	Access
PU	Access
PV	Access
PW	Access
PX	Access
PY	Access
PZ	Access
QA	Access
QB	Access
QC	Access
QD	Access
QE	Access
QF	Access
QG	Access
QH	Access
QI	Access
QJ	Access
QK	Access
QL	Access
QM	Access
QN	Access
QO	Access
QP	Access
QQ	Access
QR	Access
QS	Access
QT	Access
QU	Access
QV	Access
QW	Access
QX	Access
QY	Access
QZ	Access
RA	Access
RB	Access
RC	Access
RD	Access
RE	Access
RF	Access
RG	Access
RH	Access
RI	Access
RJ	Access
RK	Access
RL	Access
RM	Access
RN	Access
RO	Access
RP	Access
RQ	Access
RR	Access
RS	Access
RT	Access
RU	Access
RV	Access
RW	Access
RX	Access
RY	Access
RZ	Access
SA	Access
SB	Access
SC	Access
SD	Access
SE	Access
SF	Access
SG	Access
SH	Access
SI	Access
SJ	Access
SK	Access
SL	Access
SM	Access
SN	Access
SO	Access
SP	Access
SQ	Access
SR	Access
SS	Access
ST	Access
SU	Access
SV	Access
SW	Access
SX	Access
SY	Access
SZ	Access
TA	Access
TB	Access
TC	Access
TD	Access
TE	Access
TF	Access
TG	Access
TH	Access
TI	Access
TJ	Access
TK	Access
TL	Access
TM	Access
TN	Access
TO	Access
TP	Access
TQ	Access
TR	Access
TS	Access
TT	Access
TU	Access
TV	Access
TW	Access
TX	Access
TY	Access
TZ	Access
UA	Access
UB	Access
UC	Access
UD	Access
UE	Access
UF	Access
UG	Access
UH	Access
UI	Access
UJ	Access
UK	Access
UL	Access
UM	Access
UN	Access
UO	Access
UP	Access
UQ	Access
UR	Access
US	Access
UT	Access
UU	Access
UV	Access
UW	Access
UX	Access
UY	Access
UZ	Access
VA	Access
VB	Access
VC	Access
VD	Access
VE	Access
VF	Access
VG	Access
VH	Access
VI	Access
VJ	Access
VK	Access
VL	Access
VM	Access
VN	Access
VO	Access
VP	Access
VQ	Access
VR	Access
VS	Access
VT	Access
VU	Access
VV	Access
VW	Access
VX	Access
VY	Access
VZ	Access
WA	Access
WB	Access
WC	Access
WD	Access
WE	Access
WF	Access
WG	Access
WH	Access
WI	Access
WJ	Access
WK	Access
WL	Access
WM	Access
WN	Access
WO	Access
WP	Access
WQ	Access
WR	Access
WS	Access
WT	Access
WU	Access
WV	Access
WW	Access
WX	Access
WY	Access
WZ	Access
XA	Access
XB	Access
XC	Access
XD	Access
XE	Access
XF	Access
XG	Access
XH	Access
XI	Access
XJ	Access
XK	Access
XL	Access
XM	Access
XN	Access
XO	Access
XP	Access
XQ	Access
XR	Access
XS	Access
XT	Access
XU	Access
XV	Access
XW	Access
XX	Access
XY	Access
XZ	Access
YA	Access
YB	Access
YC	Access
YD	Access
YE	Access
YF	Access
YG	Access
YH	Access
YI	Access
YJ	Access
YK	Access
YL	Access
YM	Access
YN	Access
YO	Access
YP	Access
YQ	Access
YR	Access
YS	Access
YT	Access
YU	Access
YV	Access
YW	Access
YX	Access
YY	Access
YZ	Access
ZA	Access
ZB	Access
ZC	Access
ZD	Access
ZE	Access
ZF	Access
ZG	Access
ZH	Access
ZI	Access
ZJ	Access
ZK	Access
ZL	Access
ZM	Access
ZN	Access
ZO	Access
ZP	Access
ZQ	Access
ZR	Access
ZS	Access
ZT	Access
ZU	Access
ZV	Access
ZW	Access
ZX	Access
ZY	Access
ZZ	Access



Hubley Davies
100, 101, 102, 103, 104, 105, 106, 107, 108, 109, 110, 111, 112, 113, 114, 115, 116, 117, 118, 119, 120, 121, 122, 123, 124, 125, 126, 127, 128, 129, 130, 131, 132, 133, 134, 135, 136, 137, 138, 139, 140, 141, 142, 143, 144, 145, 146, 147, 148, 149, 150, 151, 152, 153, 154, 155, 156, 157, 158, 159, 160, 161, 162, 163, 164, 165, 166, 167, 168, 1
